01 to 07 Oct 2026

> OD1 arrived at the new well location SHU-0001 and is spotting and building up the 21-1/4" BOP. OPH remains off hired.

VESSEL TRIPS	TRUCK MOVES	FLUIDS HANDLED, M³	OVERSTAY CREW
15	**79**	**1,510**	**5**
▲ 36% (11) Last week	▲ 108% (38) Last week	▼ 36% (2,374) Last week	No change (5) Last week
7 wks, from 9	7 wks, from 41	7 wks, from 1,452	7 wks, from 13

Rig OD1 — ON HIRE

Spot and build up 21-1/4" BOP

Personnel onboard	**86** incl. 57 visa
Overstay crew	KOC **1** COSL **4**
Last week	Arrived at new well location SHU-0001; preloading operation; prepare to skid; lay down CTU running tool
Next steps	Pre-spud meeting; safety drills; drill 42" hole to 100 ft BML; conduct drop gyro; drill 42" hole to 548 ft (in Kuwait Series formation)

Rig OPH — OFF HIRED

Rig off-hired

Personnel onboard	**Nil**
Overstay crew	Nil
Last week	Nil
Next steps	Nil


Daily ground operations · Wed 07 Oct 2026


- One pickup dispatched to Bureau Veritas, Shuwaikh, with six lifts of water samples received from the OD1 and OPH locations, per delivery ticket RM-SP-9048.
- Three trucks arrived from the Shuaiba Port pipe yard with three joints each of 36" R3 casing for OD1 (call-off OD-SH1-B-3-1), per delivery ticket HPM-DT-1599.
- One truck arrived from the Shuaiba Port pipe yard with three joints of 36" R3 casing for OD1 (call-off OD-SH1-B-3-1), per delivery ticket HPM-DT-1598.
- One truck arrived from NOV Ahmadi with two 6-1/2" drilling jars for OD1 (call-off OD-SH1-A-1-17), per delivery ticket HPM-DT-1600.
- Two call-off trucks arrived from a KOC facility with a KOC centralizer, redress kit, swell packer and compound for OD1 (call-off OD-SH1-B-3-1), per delivery ticket HPM-DT-1601.
- One truck arrived from COSL Mina Abdallah with two lifts for OD1 (call-off OD-SH1-B-6-3), per delivery ticket COSL-DT-OD-SH1-B-6-3.
- One truck arrived at the Shuaiba Port pipe yard from the CAT Jahra yard with a CAT power generator.
- **Seven trucks** arrived and were offloaded with 35 joints of 30" R3 casing, 234.51 ppf (CAT ID 70126882).
- One truck arrived and was offloaded with 5 joints of 30" R3 casing, 196.26 ppf (CAT ID 701268875).


- Slinging of 36" and 38" R-2 and R-3 casing joints started at the pipe yard; 11 joints loaded on four regular trucks to move them to Shuaiba berth 20.
- The cementing team arrived at Shuaiba Port to transfer bulk cement from vessel Crest Argus-5 to the port silos; **47 MT of cement** transferred to the port silos from vessel CA-1.
- Fuel transferred to shore base equipment.
- Al Mansoori completed inspection of 20 joints of 30" R3 casing, 234.51 ppf (CAT ID 70126882).
- The rest of the 36" R3 casing, with a 36" float shoe, a 36" float collar, a 38" × 36" landing joint and two 36" × 36" crossovers, transferred from the pipe yard to berth 20, per DT-HPM-1601.
- **Charlie-3** sailed to OD1 with the COSL BOP frame, per manifest CM-OD-1014.
- Loading of 36" and 38" casing on **CA5** continuing.
- Vessel movements remain under **MARSEC Level 2**.

Daily Ground Operations, as circulated in the 08.10.2026 email.

Full figures three charts, and every figure

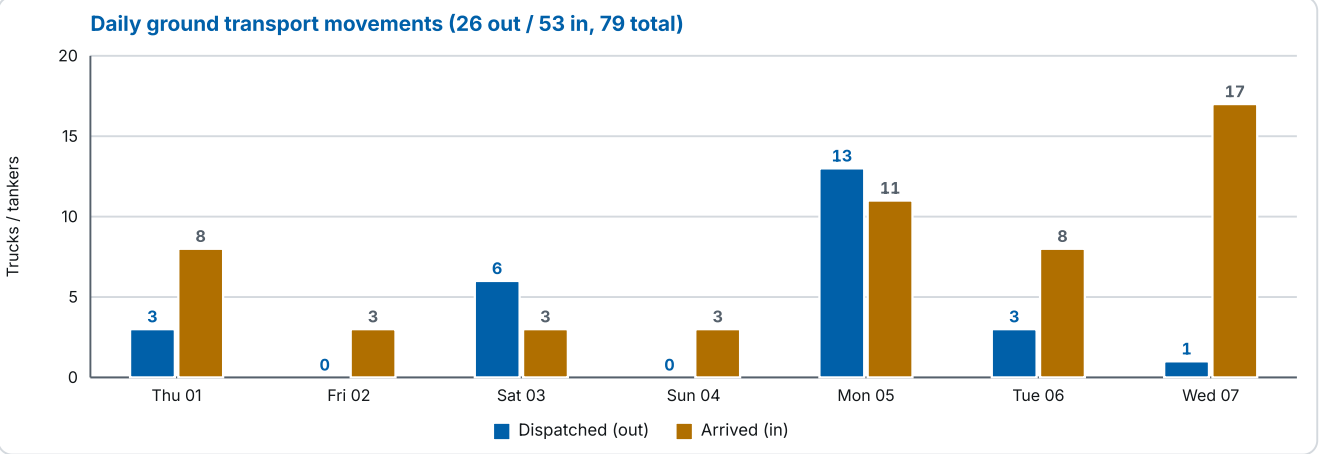

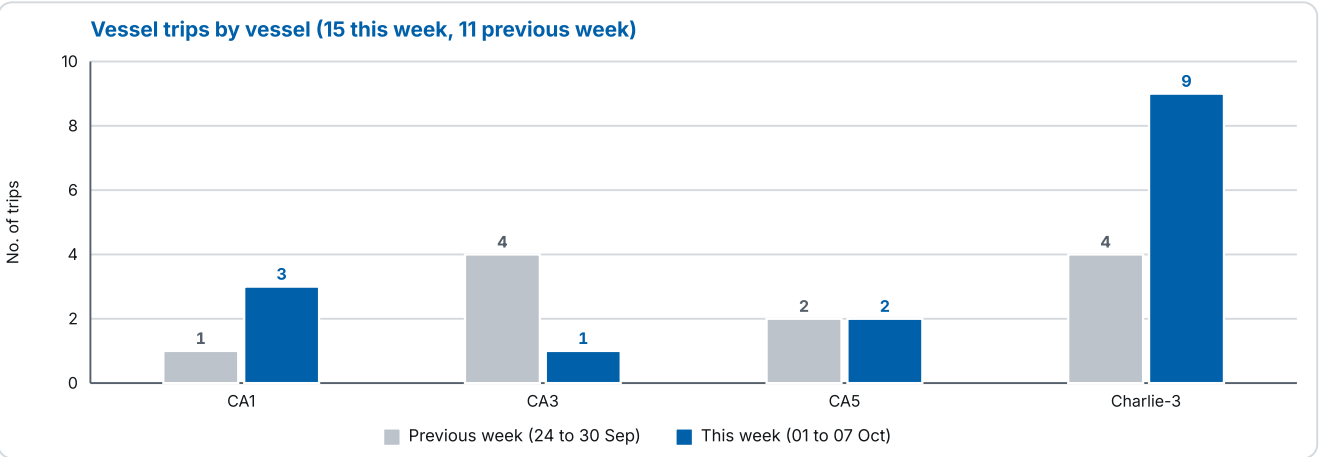

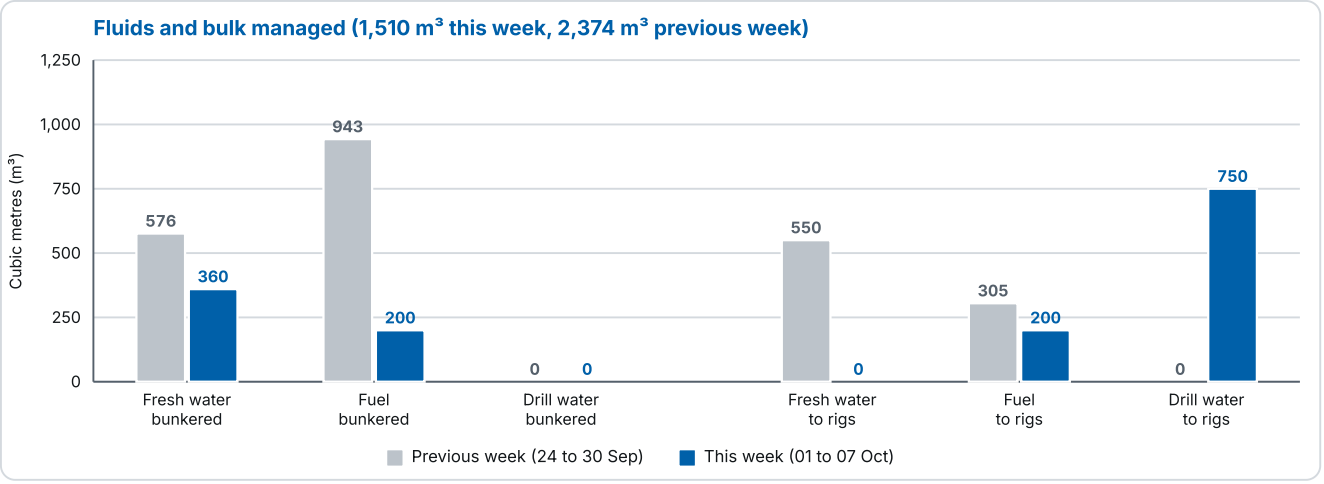

Slops: none recorded.

Metric	01 to 07 Oct 7 days	24 to 30 Sep 7 days	Change
VESSEL TRIPS			
CA1	3	1	▲ 2 (1)
CA3	1	4	▼ 3 (4)
CA5	2	2	No change (2)
Charlie-3	9	4	▲ 5 (4)
Total vessel trips	**15**	**11**	▲ 4 (11)
VESSEL MOVEMENTS port to rig, rig to port, rig to rig			
CA1	2	1	▲ 1 (1)
CA3	1	3	▼ 2 (3)
CA5	2	2	No change (2)
Charlie-3	17	9	▲ 8 (9)
Total vessel movements	**22**	**15**	▲ 7 (15)
Movements per day	3.1	2.1	▲ 1 (2.1)
GROUND TRANSPORT			
Dispatched (out)	26	19	▲ 7 (19)
Arrived (in)	53	19	▲ 34 (19)
Total truck / tanker moves	**79**	**38**	▲ 41 (38)
Moves per day	11.3	5.4	▲ 5.9 (5.4)
FLUIDS AND BULK			
Fresh water bunkered at port	360 m³	576 m³	▼ 216 m³ (576 m³)
Fuel bunkered at port	200 m³	943 m³	▼ 743 m³ (943 m³)
Drill water bunkered at port	0 m³	0 m³	No change (0 m³)
Fresh water to rigs	0 m³	550 m³	▼ 550 m³ (550 m³)
Fuel to rigs	200 m³	305 m³	▼ 105 m³ (305 m³)

Metric	01 to 07 Oct 7 days	24 to 30 Sep 7 days	Change
Drill water to rigs	750 m³	0 m³	▲ 750 m³ (0 m³)
Total fluids managed	**1,510 m³**	**2,374 m³**	▼ 864 m³ (2,374 m³)
Slops discharged	0 bbl	0 bbl	No change (0 bbl)
RIGS AND CREW			
Active rigs	1	1	No change (1)
OD1 personnel onboard	86	80	▲ 6 (80)
Overstay crew, KOC	1	1	No change (1)
Overstay crew, HLB	0	2	▼ 2 (2)
Overstay crew, COSL	4	2	▲ 2 (2)
Total overstay crew	**5**	**5**	No change (5)

Daily log 118 operations

Port operations 7 days, 90 operations

Thursday 01.10.2026 Normal	• One truck was dispatched with 3 x lifts with KOC BOP test Plugge & Wear bushings used on Well JL003 to HETCO Ahmadi facility , as per delivery ticket RM-SP-9034 • One truck was dispatched with 1 × 6.9mtr. empty basket to OWS Mina Abdallah facility , as per delivery ticket RM-SP-9035 • One truck was dispatched with 1 × 6.9mtr. empty basket to OWS Mina Abdallah facility , as per delivery ticket RM-SP-9036 • One truck arrived with 60 Joints x 5-1/2'' Drill Pipes for OD1 (Call Off: OD-SH1-B-3-3) from COSL Mina Abdallah Facility, as per delivery ticket COSL-DT- OD-SH1-B-3-3A • One truck arrived with 60 Joints x 5-1/2'' Drill Pipes for OD1 (Call Off: OD-SH1-B-3-3) from COSL Mina Abdallah Facility, as per delivery ticket COSL-DT- OD-SH1-B-3-3B • One truck arrived with 60 Joints x 5-1/2'' Drill Pipes for OD1 (Call Off: OD-SH1-B-3-3) from COSL Mina Abdallah Facility, as per delivery ticket COSL-DT- OD-SH1-B-3-3D • One truck arrived with 60 Joints x 5-1/2'' Drill Pipes for OD1 (Call Off: OD-SH1-B-1-3) from COSL Mina Abdallah Facility, as per delivery ticket COSL-DT- OD-SH1-B-1-3C • One truck arrived with 2 x lifts for OD1 as per Call Off: OD-SH1-B-2-3 from COSL Mina Abdallah Facility, as per delivery ticket COSL-DT- OD-SH1-B-2-3E • One truck arrived with 2 x lifts for OD1 as per Call Off: OD-SH1-B-1-3 from COSL Mina Abdallah Facility, as per delivery ticket COSL-DT- OD-SH1-B-1-3C • One truck arrived with 5 x Lifts for OD1 as per Call Off: OD-SH1-B-3-3 from COSL Mina Abdallah Facility, as per delivery ticket COSL-DT- OD-SH1-B-3-3E • One truck arrived with 4 x Lifts for OD1 as per Call Off: OD-SH1-B-3-3 from COSL Mina Abdallah Facility, as per delivery ticket COSL-DT- OD-SH1-B-3-3F • Loaded 1 x Truck with MLS & WH Equipment and sent to Hetco yard for Baker Inspection • Offloaded 2 x Trucks with 6 x Lifts for Rig OD-1 from COSL • Offloaded 6 x Trucks with Drill Pipes for Rig OD-1 from COSL
Friday 02.10.2026 Normal	• Fuel bunkering to CA 1 (72 M3). • Fresh water bunkering to CA 1 (216 M3). • One truck arrived with 3 x lifts for Rig OD-1 from Wireline • One truck arrived with 2 x lifts for Rig OD-1 from Wireline • One truck arrived with 2 x lifts for Rig OD-1 from COSL

Saturday 03.10.2026 Normal	• One truck was dispatched with 1 x full trash skip received from OD1(RCM-OD-942) to COSL Mina Abdallah facility , as per delivery ticket RM-SP-9037 • One truck was dispatched with 3 × 3mtr. empty H/H basket to OWS Mina Abdallah facility , as per delivery ticket RM-SP-9038 • One truck was dispatched with 3 × 3mtr. empty H/H basket to OWS Mina Abdallah facility , as per delivery ticket RM-SP-9039 • One truck was dispatched with 1 × 7mtr. empty H/H basket to Cementing Hall. Mina Abdallah facility , as per delivery ticket RM-SP-9040 • One boom truck arrived with 2 × 33'' drill bit for OD1 from Smith / Ajal Mina Abdallah Facility, as per delivery ticket HPM-DT-1593 • One truck arrived with 4 × 6' mini container with chemical loads for OD1 as per Call Off: OD-SH1-A-1-4 from BAROID Mud Plant Facility, as per delivery ticket BAR-DT-06 • One truck arrived with 4 × 6' mini container with chemical loads for OD1 as per Call Off: OD-SH1-A-1-4 from BAROID Mud Plant Facility, as per delivery ticket BAR-DT-06 • One truck arrived with 1 × 6.9mtr. basket with fishing tools for OD1 as per Call Off: OD-SH1-B-1-14 from Odfjell Mina Abdallah Facility, as per delivery ticket OWS-DT-FIS-024 • One truck was dispatched with 1 × 9mtr. empty basket to OWS Mina Abdallah facility , as per delivery ticket RM-SP-9041 • One truck was dispatched with 1 × 7.8mtr. empty basket to OWS Mina Abdallah facility , as per delivery ticket RM-SP-9042 • Offloaded Chemical Containers , Fishing Tools, and 2 × 33" Drill Bits at berth 20 • Loaded Cargo for Rig OD-1 on CA-3 • Fuel bunkering to CA 1 (71.998 M3). • Fresh water bunkering to CA 1 (108 M3).
Sunday 04.10.2026 Normal	• Loaded Cargo for Rig OD-1 on CA-3 • Loaded Cargo for Rig OD-1 on CA-1 • Loaded the food containers on Vessel Charlie-3 • Fuel bunkering to Charlie3 (20 M3). • Baroid team transferred bulk to vessel CA3 & CA1s for Rig Oriental Dragon-1. • Offloaded 11 Empty Oil Drums from Vessel Crest Argus-1 & loaded 11 Full Lube Oil Drums to Vessel Crest Argus-1 received from Al-Rashed. • 1 X truck arrived with 1 × 7mtr. basket with Cooling Line & Cementing Spares for OD1 as per Call Off: OD-SH1-B-1-8 from Cementing Hall Mina Abdallah Facility, as per delivery ticket CMT-OD-SH1-B-1-8 • 1 X truck arrived with 20' OT container with Gate Valves+ BOP Frames for OD1 as per Call Off: OD-SH1-B-4-3 from COSL Mina Abdallah Facility, as per delivery ticket COSL-DT- OD-SH1-B-4-3 • 1 X truck arrived with 2 x baskets with Odfjell TRS tools for OD1 as per Call Off: OD-SH1-A-1-13 from Odfjell Mina Abdallah Facility, as per delivery ticket OWS-DT-TRS-079 • 10X truck loaded with 24"and 18 5/8" casing and accessories of well BM-0001 to send back to KOC dispatch.

Monday 05.10.2026 Normal	• Sent the 24″and 18 5/8″ casing and accessories of BM-0001 to KOC dispatch. • 1 X Boom truck was dispatched with 4 x Lifts received from OPH to COSL Mina Abdallah facility , as per delivery ticket RM-SP-9043 • 1 X Boom truck was dispatched with Tower Light to Shuaiba Port Pipe Yard • 1 X truck arrived with 1 × 7mtr. basket with Cooling Line & Cementing Spares for OD1 as per Call Off: OD-SH1-B-1-8 from Cementing Hall Mina Abdallah Facility, as per delivery ticket CMT-OD-SH1-B-1-8 • 1 X truck was dispatched with 3 x OD1 Empty food containers to Reliance Subhan facility, as per delivery ticket RM-SP-9044 • 1 X truck arrived with 1 × 6′ mini container with Cementing tools for OD1 as per Call Off: OD-SH1-B-2-8 from Cementing Hall Mina Abdallah Facility, as per delivery ticket CMT-OD-SH1-B-2-8 • 1 X pickup arrived with 1 × 9-1/2′′ Bit for OD1 as per Call Off: OD-SH1-A-2-1 from NOV Ahmadi Facility, as per delivery KOC ticket 2026/10/5/0957 • 1 X call off truck arrived with 2 × 38′′ Casing for OD1 as per Call Off: OD-SH1-B-3-1 from KOC Y-4 to Shuaiba port Pipe yard, as per delivery KOC ticket 2026/10/5/0743 • 1 X call off truck arrived with 2 × 38′′ Casing for OD1 as per Call Off: OD-SH1-B-3-1 from KOC Y-4 to Shuaiba port Pipe yard, as per delivery KOC ticket 2026/10/5/0752 • 1 X call off truck arrived with 2 × 38′′ Casing for OD1 as per Call Off: OD-SH1-B-3-1 from KOC Y-4 to Shuaiba port Pipe yard, as per delivery KOC ticket 2026/10/5/0760 • 1 X call off truck arrived with 2 × 36′′ Casing for OD1 as per Call Off: OD-SH1-B-3-1 from KOC Y-4 to Shuaiba port Pipe yard, as per delivery KOC ticket 2026/10/5/0775 • 4 X call off truck arrived with 11 Nos Short joints of 38″& 36′′ Casing for OD1 as per Call Off: OD-SH1-B-3-1 from KOC Y-4 to Shuaiba port Pipe yard • 1 X truck arrived with 1 × 7mtr. basket with 9-1/4" NB & String Stabilizers for Pilot hole for OD1 as per Call Off: OD-SH1-A-1-15 from OWS Mina Abdallah Facility, as per delivery ticket OWS-DT-DRT-086 • Cargo operation with Vessel Crest Argus-1, loaded 7-5/8" to 30" KOC MLS Running tools (8 Lifts) on Vessel Crest Argus-1 deck. • Offloaded the 2 X 36" & 6 X 38" Casing joints for Well# SH-0001 at Shuaiba Pipe Yard. • 3 X empty Food containers loaded on 1 truck for Rig Oriental Phoenix food provision. • AL Mansoori completed the inspection of 14 Jts. as follow (6 × 38" R3 CAT ID 70126867) (2 × 36" R3 CAT ID 70126871) (1 × 38" CAT ID 70126868) (3 × 36" CAT ID 70126872) (2 × 38" CAT ID 70126869)

Tuesday 06.10.2026 Normal	• 1 X truck was dispatched with 2 x Lifts received from OD1 as per manifest RCM-OD-943 to COSL Mina Abdallah facility , as per delivery ticket RM-SP-9045 • 1 X truck was dispatched with 1 × 10′ container with COSL tools from OPH to COSL Mina Abdallah facility , as per delivery ticket RM-SP-9046 • 1 X truck arrived with 2 x Lifts for OD1 as per Call Off: OD-SH1-B-5-3 from COSL Mina Abdallah Facility, as per delivery ticket COSL-DT-OD-SH1-B-5-3A • 1 X pickup was dispatched with Hand Carry received from OD1 to HPPM, BSS Lab & Sperry SLB Mina Abdallah facility , as per delivery ticket RM-SP-9047 • 1 truck arrived with 4 x Lifts with 6.5′ Drill collar & Drill pipe for OD1 as per Call Off: OD-SH1-B-5-3 from COSL Mina Abdallah Facility, as per delivery ticket COSL-DT-OD-SH1-B-5-3B • 6 X call off truck arrived with 17 × 36′′ Casing for OD1 as per Call Off: OD-SH1-B-3-1 from KOC Y-4 to Shuaiba port Pipe yard, • 3 X empty Food containers & 1 Empty Trash Skip loaded on Vessel Charlie-3 for Rig Oriental Dragon-1. • Cargo operation with Vessel Crest Argus-1, loaded 18 cargo lifts on Vessel Crest Argus-1 deck as per updated Lookahead received from OD-1. • Offloaded 2 trucks C/w 6 cargo lifts for Rig Oriental Dragon-1 (6 L:ifts) and loaded on Vessel Crest Argus-1 deck. • AL Mansoori team Completed inspection of 17 Jts 36" R3 CAT ID 70126871 • Al Mansoori Completed inspection of 2 X 38" & 3 X 36" casing joints with 1 X-Over joint of 36" X 38". • 4 x Trucks loaded with inspected Jts 38" & 36" total of 2 × 36" R3 + 11 Short Jts as per HPM-DT-1596 & 1597, all offloaded at Berth 20 • Loaded cargo on vessel CA1 as per manifest CM-OD-1012 • Loaded cargo on vessel CA3 as per manifest CM-OD-1013

Wednesday 07.10.2026 Normal	• 1 X pickup was dispatched with 6 x Lifts with Water Sample received from OD1 & OPH location to Bureau veritas Shuwaikh facility , as per delivery ticket RM-SP-9048 • 3 X trucks arrived with 3 Joints x 36'' R3 Casing ea. for OD1 as per Call Off: OD-SH1-B-3-1 from Shuaiba Port Pipe Yard, as per delivery ticket HPM-DT-1599 • 1 X truck arrived with 3 Joints x 36'' R3 Casing for OD1 as per Call Off: OD-SH1-B-3-1 from Shuaiba Port Pipe Yard, as per delivery ticket HPM-DT-1598 • 1 X truck arrived with 2 × 6-1/2'' Drilling Jar for OD1 as per Call Off: OD-SH1-A-1-17 from NOV Ahmadi Facility, as per delivery ticket HPM-DT-1600 • 2 X Call off trucks arrived with KOC Centralizer, Redress Kit, Swell Packer & Compound for OD1 as per Call Off: OD-SH1-B-3-1 from KOC facility, as per delivery ticket HPM-DT-1601 • 1 X truck arrived with 2 x lifts for OD1 as per Call Off: OD-SH1-B-6-3 from COSL Mina Abdallah facility, as per delivery ticket COSL-DT-OD-SH1-B-6-3 • 1 X truck arrived with 1 x CAT Power Generator from CAT Jahra Yard to Shuaiba Port Pipe Yard • Arrived and completed offloading for 7 x trucks with total 35 Jts of 30" Casing R3, 234.51 ppf (CAT ID 70126882) • Arrived and completed offloading for 1 x truck with total 5 Jts of 30" Casing R3, 196.26 ppf (CAT ID 701268875) • Started slinging of 36" & 38" Casing, R-2 & R-3 joints at pipe yard & loaded 11 joints on 4 regular trucks to mobilize the casing joints to Shuaiba Berth-20. • Cementing team arrived at Shuaiba Port to transfer bulk cement from Vessel Crest Argus-5 to Port silos. Transferred 47MT Cement to Port silos from Vessel CA-1. • Fuel transferred to shore base equipment • AL Mansoori team Completed inspection on 20 Jts. of 30" R3 PPF 234.51 ,CAT ID 70126882, • Transfer rest of 36" Casing R3 + 1 x float shoe 36" + 1 x Float collar 36" + 1 x landing Joint 38" X 36" + 2 Cross Overs 36" x 36" from pipe yard to Berth 20 as per DT # DT-HPM-1601 • Vessel Charlie 3 sailed to OD-1 with COSL Bop Frame as per manifest CM-OD-1014 • Continuing loading on Vessel CA5 with 36" and 38" Casing.

Vessel movements 7 days, 28 operations

Thursday 01.10.2026 Normal	• Vessel CA1- Vessel under towing to New well location SHU-0001,Vessel arrived at new location@12:30, vessel under way to Shuaiba @13:12, Vessel secured at berth 20 @17:12, STBY at berth 20. • Vessel CA3- Vessel STBY at berth 20, Received fresh water(36 M3),ast Off and swap position, cargo operation,Cast Off and move ahead, STBY at berth 20. • Vessel CA5- Vessel STBY,anchored at OD1 location, heave up anchor@17:56vessel in post 200 mtrs from OD1 stby for safety watch • Vessel Charlie 3- Vessel STBY at berth 4 , cargo loaded, Pax in, castoff @09:45, alongside of OPH@10:55, cargo operation,Pax transferred pullout@ 11:56 , proceed to north pier, arrived north pier, @12:45,castoff and proceed to CA5@13:45,alongside of OPH@ 15:10,PAx transfer, pullout@15:22, arrived at berth 4@16:30 and STBY at berth 4

Friday 02.10.2026 Normal	• Vessel CA1 - Vessel STBY at berth 20, Received fresh water(216 M3), received fuel(72 M3), STBY at berth 20. • Vessel CA3 - Vesselremain Alongside at Shuaiba Port, Berth 20. • Vessel CA5 - Vessel in post 200 mtrs from OD1 stby for safety watch (DP mode ON) • Vessel Charlie 3 - Vessel STBY at berth 4
Saturday 03.10.2026 Normal	• Vessel CA1 - Vessel STBY at berth 20, Received fresh water(108 M3), received fuel(71.998 M3),STBY at berth 20. • Vessel CA3 - Vesselremain Alongside at Shuaiba Port, Berth 20, cargo operation. • Vessel CA5 - Vessel in post 200 mtrs from OD1 stby for safety watch (DP mode ON), pullout@01:15, STBY 500 M away. • Vessel Charlie 3 - Vessel STBY at berth 4
Sunday 04.10.2026 Normal	• Vessel CA1 - Vessel STBY at berth 20,received 3 drums of Lub oil from CREST ARGUS-3, Received Bentonite from Truck (17.11MT), cargo operation , STBY at berth 20. • Vessel CA3 - Vesselremain Alongside at Shuaiba Port, Berth 20, Cast Off from Shuaiba Port, Departed to OD1@13:18,Arrived at OD1 Location@16:36,vessel anchored and STBY at OD1 Location. • Vessel CA5 - Vessel remained anchored at OD 1 Anchorage standby w/further instruction. • Vessel Charlie 3 - Vessel STBY at berth 4 , castoff @07:30, arrived OPH @08:40,cargo operation,Pax transferred pullout@09:21,arrived at berth 4@ 10:35, cargo operation,received fresh water(20M3), Pax in, castoff @12:40, arrived OPH @13:45,pax transferred, pullout@ 13:57, arrived at berth 4@15:10 and STBY at berth 4
Monday 05.10.2026 Normal	• Vessel CA1 - Vessel STBY at berth 20 • Vessel CA3 - Vessel STBY,anchored at OD1 location, heave up anchor@13:30,in position on the port side of OD1@15:38,Deck Cargo operation, transferred Drill water, cargo operation is in progress. • Vessel CA5 - Vessel STBY,anchored at OD1 location, heave up anchor@10:05,in position on the port side of OD1@11:07, Deck Cargo operation,Pax received, Pull out@11:50, sailed, Arrived at OPH location@13:15,port side crane OPH@14:00, Transferred 1 Pax to OPH,Pull out@14:15,proceed to Shuaiba Port, vessel alongside at Berth 20 @17:35, Vessel STBY at berth 20. • Vessel Charlie 3 - Vessel STBY at berth 4 , castoff @04:45, arrived Khiran Mall@06:55, Pax in and proceed to OPH@07:30, alongside of OPH@10:15, Pax received, pullout@10:45, alongside of OD1@11:20, Pax transferred pullout@ 11:57 arrived Khiran Mall@14:50, pax transferred to Taxi boat, proceed to berth 4 @14:30, along side of berth 4 @17:35, Vessel STBY at berth 4

Tuesday 06.10.2026 Normal	• Vessel CA1 - Vessel STBY at berth 20,cargo operation, Vessel cast off @09:05,Vessel returned back@09:17,cargo loaded(15 lift), Vessel cast off @ 14:25, Vessel arrived outside 500 meters of OD1@17:30,Vessel under Port side Crane of OD1@19:34, cargo operation, started transferring drill water (ongoing), vessel remain under Port side of OD1. • Vessel CA3 - Vessel remain Alongside at Port side of OD1,Deck Cargo operation and transferring Drill water to OD1 in progress,Stop transferring Drill water(total 350M3) due to STBD engine temperature rising (sea chest accumulated of mud in shallow water operation), pull out@00:26,Exit 500M zone,DP off & Proceed to anchorage, completed the sea chest cleaning @04:00,heave up anchor@04:08, vessel in position on the p/s of OD1@05:45, cargo operation, pull out@ 09:50 and STBY 300 m away for Charlie 3 pax transfer,vessel in position on the p/s of OD1@12:24, transferred Bentonite to OD1 : 44.59 MT, cargo operation, pullout @18:24, Exit 500M zone,DP off & Proceed to anchorage @18:50 and STBY • Vessel CA5 - Vessel remain alongside at berth 20, Shuaiba Port,cargo opeartion, received fuel (36.001 M3) • Vessel Charlie 3 - Vessel STBY at berth 4 , cargo loaded, 26 Pax in, castoff @08:30, alongside of OD1@10:10, cargo operation,Pax transferred pullout@ 11:19 ,proceed to OPH, arrived OPH @11:50,collected mud samples at old location(OPH),proceed to OD1@ 12:15, arrived OD1@13:35, collected mud samples at old location,proceed to Shuaiba@ 14:10, arrived at berth 4@15:30, pax disembarked, and STBY at berth 4.
Wednesday 07.10.2026 Normal	• Vessel CA1 - Vessel remain under Portside of OD-1,drill water transferred (400M3), cargo operation,fuel transferred (200M3), Transferred Bentonite from Bulk Tank No.6 to OD1,Rig instructed vessel to stop transfer Bentonite, disconnected the line, pullout the vessel @15:38 and STBY 500 M away. • Vessel CA3 - Vessel standby anchored at OD1 Location,heave up anchor@17:21, vessel in position on the p/s of OD1@19:20, cargo operation, Commenced Transferring Barite to OD1, Stop Transferring Barite due to OD1 tank change, continued blow through of Barite line@23:40, Stop Blow through of Barite line due to DGPS Signal Jamming / unstable@23:50,Pull out 200 m away from OD1 and stand by monitoring / observed DGPS Signal@23:51. • Vessel CA5 - Vessel remain alongside at berth 20, discharged cement to Silo Tank, deck cargo operation, Shifting in berth 20, Continue deck cargo operation is in progress, Vessel remain alongside at berth 20. • Vessel Charlie 3 - Vessel STBY at berth 4 , cargo loaded,castoff @20:05 alongside STBD side of OD1@21:20, cargo operation, pullout@ 21:46 , proceed to Shuaiba@ 21:50, arrived at berth 4@23:00 and STBY at berth 4

Thanks and Best Regards,

Saud Abdulaziz AlKharji
Kuwait Oil Company (KOC)
Engineer Drilling & Workover | Drilling & Workover Operational Support Team
skharji@kockw.com | www.kockw.com
