Offshore Logistics Weekly Dashboard

Drilling & Workover Operations Support · Kuwait Oil Company

24 to 30 Sep 2026

OD1 under tow to SH-0001. OPH remains off hired.

VESSEL TRIPS	TRUCK MOVES	FLUIDS HANDLED, M³	OVERSTAY CREW
11	38	2,374	5
▼ 27% (15) Last week	▲ 46% (26) Last week	▲ 144% (973) Last week	▼ 7 (12) Last week
6 wks, from 9	6 wks, from 41	6 wks, from 1,452	6 wks, from 13

Rig OD1 — ON HIRE

Rig under tow to SH-0001

Personnel onboard	**80** incl. 56 visa
Overstay crew	KOC **1** HLB **2** COSL **2**
Last week	Nil
Next steps	Position rig at location; adjust air gap and perform preloading; dump preload; jack to drilling air gap; install fixation; cantilever skid out (including CTU); spot the 21-1/4" and 26-3/4" BOP in the moon pool area; break out MLS running tools

Rig OPH — OFF HIRED

Rig off-hired

Personnel onboard	**Nil**
Overstay crew	Nil
Last week	Nil
Next steps	Nil


Daily ground operations · Wed 30 Sep 2026


- 24" casings (R1, R2 and R3) of well BM-0001 shifted from berth 20 to the pipe yard, offloaded, and their pre-slings removed.
- **108.003 m³ of fuel** bunkered to CA3.
- **216 m³ of fresh water** bunkered to CA3.
- Three trucks loaded with MLS and wellhead equipment and sent to the Hetco yard for Baker inspection.
- One truck offloaded with shock subs and Gyro tools, and three trucks offloaded with BOPs for Rig OD1 from NOV, Gyro and COSL.
- Backload from OD1 sent to COSL.
- One truck dispatched to HETCO Ahmadi with seven lifts of KOC wellhead A–F sections used on well JL003, per delivery ticket RM-SP-9024.
- One truck dispatched to HETCO Ahmadi with six lifts of KOC wellhead A–F sections used on well RI003, per delivery ticket RM-SP-9025.
- One truck dispatched to HETCO Ahmadi with eight lifts of KOC wellhead A–F sections used on wells JL003 and RI003, per delivery ticket RM-SP-9026.


- One call-off truck dispatched to COSL Mina Abdallah with a 7.5 m empty basket and a wooden box received from OD1 via CA3, per delivery ticket RM-SP-9207.
- One call-off truck arrived from COSL Mina Abdallah with a **21-1/4" 10M double ram BOP** for OD1 (call-off OD-BM1-E-7-3), per delivery ticket COSL-DT-OD-BM1-E-7-3A.
- One call-off truck arrived from COSL Mina Abdallah with a **21-1/4" 10K single ram BOP** for OD1 (call-off OD-BM1-E-7-3), per delivery ticket COSL-DT-OD-BM1-E-7-3B.
- One call-off truck arrived from COSL Mina Abdallah with a **21-1/4" annular ram BOP** for OD1 (call-off OD-BM1-E-7-3), per delivery ticket COSL-DT-OD-BM1-E-7-3C.
- One truck arrived from NOV Ahmadi with two stabilizers for OD1 (call-off OD-SH1-B-1-17), per delivery ticket 7277.
- One truck arrived from Gyrodata Ahmadi with a 6 ft mini container of Gyro tools for OD1 (call-offs OD-SH1-B-1-16 / 2-16).
- One boom truck arrived from Al-Mansoori with bit breakers after inspection.
- One truck arrived from Odfjell Mina Abdallah with a 6 m basket of DRT tools for OD1 (call-off OD-SH1-B-1-15), per delivery ticket OWS-DT-DRT-084.
- One truck arrived from Odfjell Mina Abdallah with a 2 × 3 m basket of DRT tools for OD1 (call-off OD-SH1-B-1-15), per delivery ticket OWS-DT-DRT-085.
- Vessel movements remain under **MARSEC Level 2**.

Daily Ground Operations, as circulated in the 01.10.2026 email.

Full figures three charts, and every figure

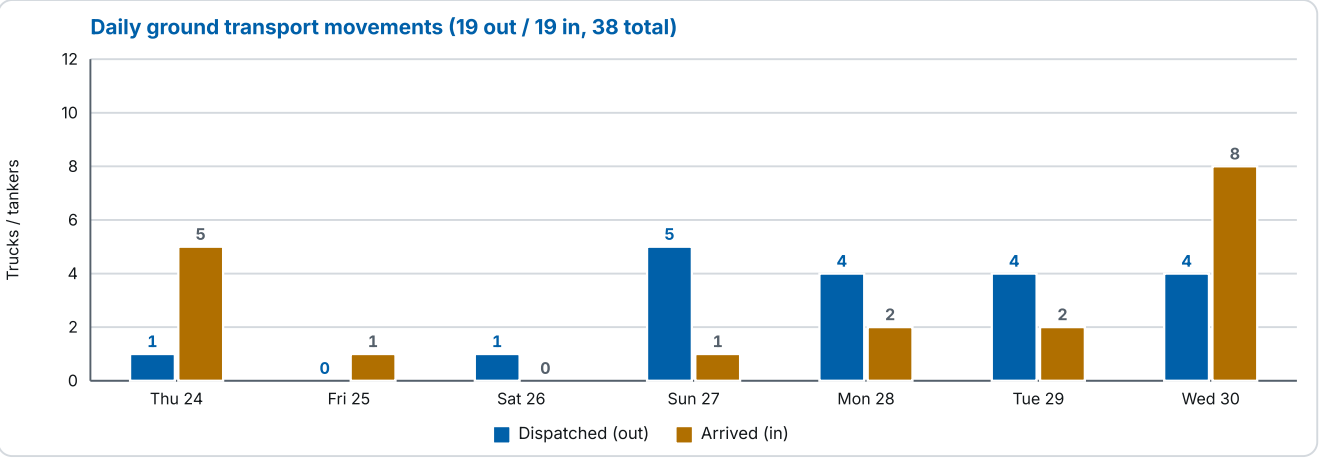

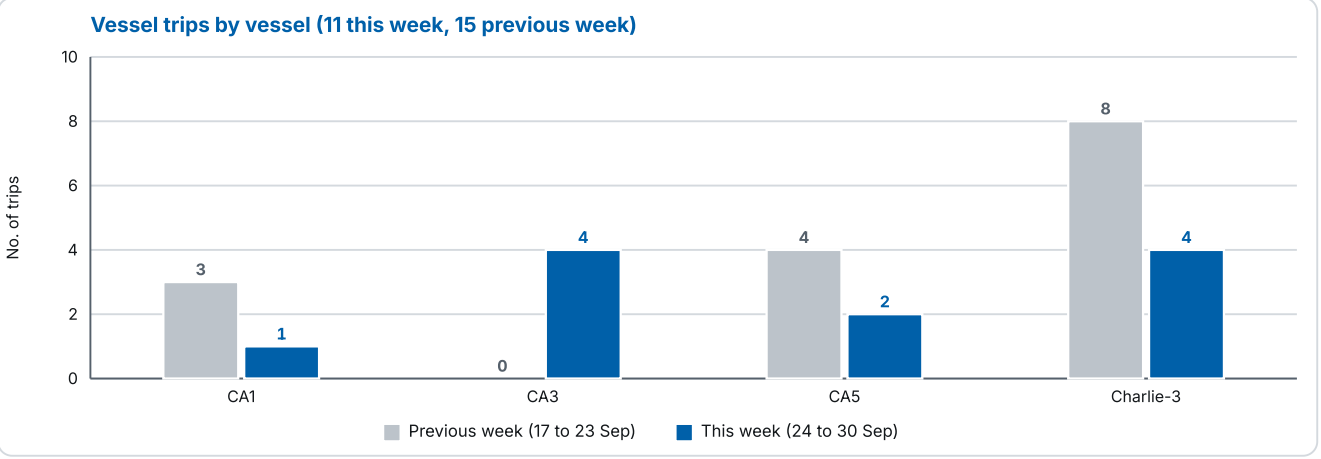

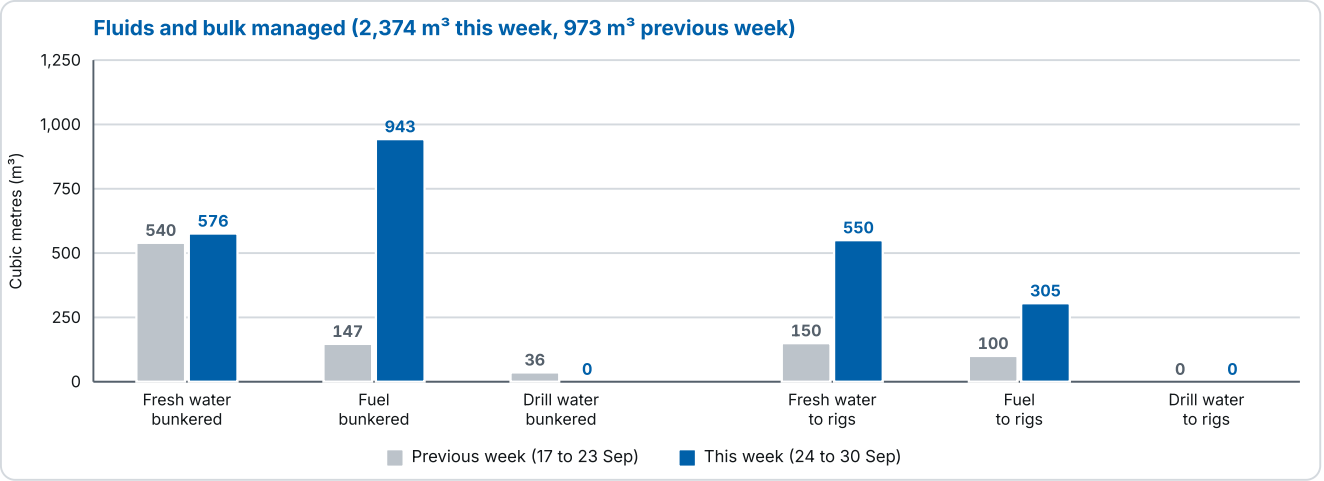

Slops: none recorded.

Metric	24 to 30 Sep 7 days	17 to 23 Sep 7 days	Change
VESSEL TRIPS			
CA1	1	3	▼ 2 (3)
CA3	4	0	▲ 4 (0)
CA5	2	4	▼ 2 (4)
Charlie-3	4	8	▼ 4 (8)
Total vessel trips	**11**	**15**	▼ 4 (15)
VESSEL MOVEMENTS port to rig, rig to port, rig to rig			
CA1	1	2	▼ 1 (2)
CA3	3	0	▲ 3 (0)
CA5	2	3	▼ 1 (3)
Charlie-3	9	14	▼ 5 (14)
Total vessel movements	**15**	**19**	▼ 4 (19)
Movements per day	2.1	2.7	▼ 0.6 (2.7)
GROUND TRANSPORT			
Dispatched (out)	19	20	▼ 1 (20)
Arrived (in)	19	6	▲ 13 (6)
Total truck / tanker moves	**38**	**26**	▲ 12 (26)
Moves per day	5.4	3.7	▲ 1.7 (3.7)
FLUIDS AND BULK			
Fresh water bunkered at port	576 m³	540 m³	▲ 36 m³ (540 m³)
Fuel bunkered at port	943 m³	147 m³	▲ 796 m³ (147 m³)
Drill water bunkered at port	0 m³	36 m³	▼ 36 m³ (36 m³)
Fresh water to rigs	550 m³	150 m³	▲ 400 m³ (150 m³)
Fuel to rigs	305 m³	100 m³	▲ 205 m³ (100 m³)

Metric	24 to 30 Sep 7 days	17 to 23 Sep 7 days	Change
Drill water to rigs	0 m³	0 m³	No change (0 m³)
Total fluids managed	**2,374 m³**	**973 m³**	▲ 1,401 m³ (973 m³)
Slops discharged	0 bbl	0 bbl	No change (0 bbl)
RIGS AND CREW			
Active rigs	1	1	No change (1)
OD1 personnel onboard	80	80	No change (80)
Overstay crew, KOC	1	0	▲ 1 (0)
Overstay crew, HLB	2	1	▲ 1 (1)
Overstay crew, COSL	2	11	▼ 9 (11)
Total overstay crew	**5**	**12**	▼ 7 (12)

Daily log 95 operations

Port operations 7 days, 67 operations

Thursday 24.09.2026 Normal	• Fuel bunkering to CA5 (141.016 M3) • One pickup was dispatched with Documents received from OD1(RCM-OD-939) to HPM Hall Mina Abdallah facility , as per delivery ticket RM-SP-9012 • One boom truck arrived with 1 × 42'' Varel Drill Bit from Varel Ahmadi facility, as per delivery ticket 2925 • One truck arrived with 1 × 10' container for OD1(call off: OD-BM1-E-5-3) and 2 x Empty Trash Skips from COSL Mina Abdallah facility, as per delivery ticket COSL-DT-OD-BM1-E-5-3A • One truck arrived with 1 × 39'' to 36'' Diverter Overshot Packer for OD1(call off: OD-BM1-E-5-3) from COSL Mina Abdallah facility, as per delivery ticket COSL-DT-OD-BM1-E-5-3B • Two trucks arrived with 4 x Empty baskets from Odfjell Mina Abdallah facility, as per delivery ticket OWS-DT-BASKET-18 no night shift
Friday 25.09.2026 Normal	• Fuel bunkering to CA3 (144 M3) • Water bunkering to CA3 (252 M3) • Offloaded 1 x Truck with 1 x Container for Rig OPH from COSL • One truck arrived with 1 × 10' container for OPH (call off: OP-RI3-N-24-3) • from COSL Mina Abdallah facility, as per delivery ticket (COSL-DT-OP-RI3-N-24-3) no night shift

Saturday 26.09.2026 Normal	• Fuel bunkering to CA3 (144 M3). • Water bunkering to CA3 (108 M3). • Loaded 1 x Truck with 1 × 28" and 1 × 22" Drill Bit and sent to Smith Ajal Workshop. • Loaded Cargo for Rig OPH on Charlie-3 as per manifest CM-OP-1265. • One Boom truck was dispatched with 2 x KOC New Drill Bits received from OD1(RCM-OD-939) to KOC / Ajal Mina Abdallah facility , as per delivery ticket RM-SP-9013 no night shift
Sunday 27.09.2026 Normal	• Loaded Cargo for Rig OD1 on Charlie-3 as per manifest CM-OD-1009. • One truck was dispatched with 1 x full trash skip received from OPH to COSL Mina Abdallah facility , as per delivery ticket RM-SP-9014. • One truck was dispatched with 4 x full mud skips received after CA-3 tank cleaning to NCC SEK Plant facility, as per delivery ticket RM-SP-9015. • One pickup sent with 4 x Sample Water Bottles received from CA3 to BAROID Lab Hall Mina Abdallah facility, as per delivery ticket RM-SP-9016. • Two trucks were dispatched with 4 x Full Trash Skips received from CA1, CA3, CA5 & Shore base + Charlie3 to HETCO Stevedoring Yard & return with the same skips after empty, as per Waste Transfer manifest WT-SB-116. • One truck arrived with 1 x Power Generator from Cummins Ahmadi facility, as per delivery ticket HPM-DT-1589. • Loaded 1 x Truck with 1 x Lift backload from Rig OPH and sent to COSL. • Loaded 1 x Truck with 4 x Full OBM Mud Skips from CA-3 Tank Cleaning and sent to SEK Plant for disposal. • Loaded 2 x Trucks with 4 x Full trash Skips and sent to Hetco for disposal. • Offloaded 1 x Truck with Generator from Cummins for Baroid. no night shift
Monday 28.09.2026 Normal	• One truck was dispatched with 3 Joints x Water Cooling Line Pipes received OD1 as per manifest RCM-OD-940 to Cementing Hall Mina Abdallah facility , as per delivery ticket RM-SP-9018 • One truck was dispatched with 3 x Lifts received from OD1 as per manifest RCM-OD-940 to COSL Mina Abdallah facility , as per delivery ticket RM-SP-9017 • One pickup sent with 2 x H-Carry received from OD1 as per manifest RCM-OD-940 to HPM Hall Mina Abdallah facility, as per delivery ticket RM-SP-9019 • One truck was dispatched with 02 x Empty food containers to Reliance Subhan facility, as per delivery ticket RM-SP-9020 • One pickup arrived with 1 x Gooseneck T-Piece for OD1 as per call off: OD-SH1-A-1-6 from SDL Hall Mina Abdallah facility, as per delivery ticket SDL-DT-OD-SH1-A-1-6 • One truck arrived with 2 x lifts for OD1 as per call off: OD-BM1-E-6-3 from COSL Mina Abdallah facility, as per delivery ticket COSL-DT-OD-BM1-E-6-3 • Loaded 1 x Truck with 3 x Lifts backload from Rig OD1 and sent to COSL • Loaded 1 x Truck with 3 x Water Cooling Lines Backload from Rig OD1 and sent to Cementing • Offloaded 1 x Pick Up Truck with Gooseneck T-Piece for Rig OD1 from Sperry • Offloaded 1 x Truck with 2 x lifts for Rig OD1 for Rig OD1 from COSL • Fuel bunkering to Charlie 3 (36.003 M3). no night shift

Tuesday 29.09.2026 Normal	• One call off truck was dispatched with 1 × 500 BBL Buffer tank received from OD1 as per manifest RCM-OD-902 to HETCO Mina Abdallah Yard from Shuaiba Port Pipe yard , as per delivery ticket RM-SP-9021. • One truck was dispatched with 6′ empty mini & 6mtr. empty basket to Solas Ahmadi & Odfjell Mina Abdallah facility , as per delivery ticket RM-SP-9022 • One pickup sent with 2 x H-Carry received from OD1 as per manifest RCM-OD-940 to KOC facility • One truck was dispatched with 02 x backloads received from OD1 as per manifest RCM-OD-941to COSL Mina Abdallah facility, as per delivery ticket RM-SP-9023 • One truck arrived with KOC MLS Running tools from KOC Land Rig SP-17 & Shuaiba Port Pipe Yard, as per delivery ticket HPM-DT-1590 • One truck arrived with 1 × 10′ container for OPH as per call off: OP-RI3-N-25-3 from COSL Mina Abdallah facility, as per delivery ticket COSL-DT-OP-RI3-N-25-3 • Loaded 1 x Call Out Truck with rental Buffer Tank and sent to Hetco Yard/ DHL • Loaded 1 x Truck with 2 x Empty Units and sent to Gyro and OWS • Loaded 1 x Truck with 2 x Empty Units and sent to Gyro and OWS • Loaded 1 x Truck with 2 x Units Backload from Rig OD1 and sent to COSL • Offloaded 1 x Truck with MLS R/T for Rig OD1 from Pipe Yard • Offloaded 1 x Truck with 1 x lift for Rig OPH from C no night shift

Wednesday 30.09.2026 Normal	• 24" casings (R1,R2 & R3) of BM-0001 well Shifted from berth 20 to Pipe Yard, offloaded and removed the pre-sling of all shifted casings. • Fuel bunkering to CA 3 (108.003 M3). • Fresh water bunkering to CA 3 (216 M3) • Loaded 3 x Trucks with MLS & WH Equipment and sent to Hetco yard for Baker Inspection • Offloaded 1 x Truck with Shock subs and Gyro Tools, Offloaded 3 x Trucks with BOPs for Rig OD1 from NOV, Gyro and COSL • Sent the backload from OD1 to COSL. • One truck was dispatched with 7 lifts containing KOC Well Head A–F Sections used on Well JL003 to HETCO Ahmadi Facility, as per Delivery Ticket RM-SP-9024. • One truck was dispatched with 6 lifts containing KOC Well Head A–F Sections used on Well RI003 to HETCO Ahmadi Facility, as per Delivery Ticket RM-SP-9025. • One truck was dispatched with 8 lifts containing KOC Well Head A–F Sections used on Wells JL003 & RI003 to HETCO Ahmadi Facility, as per Delivery Ticket RM-SP-9026. • One call-off truck was dispatched with one 7.5 m empty basket and one wooden box received from OD1 via CA3 to COSL Mina Abdallah Facility, as per Delivery Ticket RM-SP-9207. • One call-off truck arrived with one 21-1/4" 10M Double Ram BOP for OD1 (Call-Off: OD-BM1-E-7-3) from COSL Mina Abdallah Facility, as per Delivery Ticket COSL-DT-OD-BM1-E-7-3A. • One call-off truck arrived with one 21-1/4" 10K Single Ram BOP for OD1 (Call-Off: OD-BM1-E-7-3) from COSL Mina Abdallah Facility, as per Delivery Ticket COSL-DT-OD-BM1-E-7-3B. • One call-off truck arrived with one 21-1/4" Annular Ram BOP for OD1 (Call-Off: OD-BM1-E-7-3) from COSL Mina Abdallah Facility, as per Delivery Ticket COSL-DT-OD-BM1-E-7-3C. • One truck arrived with two stabilizers for OD1 (Call-Off: OD-SH1-B-1-17) from NOV Ahmadi Facility, as per Delivery Ticket 7277. • One truck arrived with one 6 ft mini container containing Gyro tools for OD1 (Call-Offs: OD-SH1-B-1-16 / 2-16) from Gyrodata Ahmadi Facility. • One boom truck arrived with bit breakers after inspection from Al-Mansoori. • One truck arrived with one 6 m basket containing DRT tools for OD1 (Call-Off: OD-SH1-B-1-15) from Odfjell Mina Abdallah Facility, as per Delivery Ticket OWS-DT-DRT-084. • One truck arrived with one 2 × 3 m basket containing DRT tools for OD1 (Call-Off: OD-SH1-B-1-15) from Odfjell Mina Abdallah Facility, as per Delivery Ticket OWS-DT-DRT-085.

Vessel movements 7 days, 28 operations

Thursday 24.09.2026 Normal	• Vessel CA1- Vessel STBY,anchored at OD1 location • Vessel CA3- Vessel STBY, OPH Location, Anchor heaved up@21:50, vessel enroute to Shuaiba port • Vessel CA5- Vessel remain alongside at berth 20, fuel received (288.016 M3)Shuaiba port, cast off from berth 20@18:50, Arrived at OPH location@21:50 and vessel STBY at OPH location • Vessel Charlie 3- Vessel STBY at berth 4

Friday 25.09.2026 Normal	• Vessel CA1 - Vessel STBY,anchored at OD1 location, Anchor heaved up@07:02,Vessel under Port side Crane@08:16, fresh water transferred (150M3), Vessel pulled out@11:30,STBY 500 away, Anchor heaved up@17:37, STBY for chopper operation, Vessel proceeded to anchorage@18:38 and STBY at OD1 location • Vessel CA3 - Vessel arrive berth 20@ 01:24, cargo operation , Pax disembark,Recevied fresh water(252 M3), receved fuel(144 M3), Mud tank cleaning completed, transferred 3 drums of Hydroulic Oil (inside basket TSB10FT04) to Jetty for CA1, Vessel remain alongside at Shuaiba Port, Berth 20. • Vessel CA5 - Vessel remain STBY at OPH Location • Vessel Charlie 3 - Vessel STBY at berth 4 , Loaded 1 lift cargo
Saturday 26.09.2026 Normal	• Vessel CA1 - Vessel STBY,anchored at OD1 location • Vessel CA3 - Vessel STBY at berth 20, Recevied fresh water(108 M3), receved fuel(144 M3) Vessel remain alongside at Shuaiba Port, Berth 20. • Vessel CA5 - Vessel remain STBY at OPH Location • Vessel Charlie 3 - Vessel STBY at berth 4 , Pax in, cargo loaded,castoff @08:30, alongside of OPH@10:18, Pax transferred, cargo load/Offload, pullout@10:56, alongside of berth 4 @12:05, Vessel STBY at berth 4
Sunday 27.09.2026 Normal	• Vessel CA1 - Vessel STBY,anchored at OD1 location • Vessel CA3 - Vessel remain alongside at Shuaiba Port, Berth 20, Completed installed Agitator Mud Tk. No.1. • Vessel CA5 - Vessel remain STBY at OPH Location • Vessel Charlie 3 - Vessel STBY at berth 4 , castoff @05:15, arrived Khiran Mall@07:25, Pax in and proceed to OPH@08:00, alongside of OPH@10:35, Pax transferred, pullout@10:48, alongside of OD1@12:15, Pax transferred,cargo operation, pullout@ 13:15, arrived Khiran Mall@14:20, pax transferred, proceed to berth 4 @14:30, along side of berth 4 @16:50, Vessel STBY at berth 4
Monday 28.09.2026 Normal	• Vessel CA1 - Vessel STBY,anchored at OD1 location ,Anchor heaved up@22:05,Vessel under Port side Crane of OD1@23:13, Transfering fresh water to Rig OD1 is in progress. • Vessel CA3 - Vessel remain alongside at Shuaiba Port,castoff@0:12,Vsl secured Alongside at p/s of Sedra II@7:00,received fuel from Sedra II (297.796 M3), vessel cast off from Sedra II@11:30,Arrived at OPH Location@17:12, transferred fresh water to OPH (300 M3), Vessel pullout@23:10 and standby, anchored at OPH Location. • Vessel CA5 - Vessel remain STBY at OPH Location, Heave up anchor@10:40, proceed to OD-1 new location, arrived and dropped anchor @13:08 and STBY at OD1 location • Vessel Charlie 3 - Vessel STBY at berth 4

Tuesday 29.09.2026 Normal	• Vessel CA1- Vessel at OD1, fresh water transferred (100M3),Vessel pulled out from OD1@01:25,STBY 500 m away, Anchor heaved up@14:30,Vessel under Port side Crane of OD1@15:24, Cargo operation, Vessel pulled ou@15:48 and and STBY at OD1 location. • Vessel CA3- Vessel STBY, OPH Location, heave up anchor@8:30,in position on the stbd side of OPH@09:55, Transferred fuel (304.992 M3), cargo operation, pullout@16:18departed to Shuaiba Port, Alongside at Shuaiba Port, Berth 20.@19:52, received fuel(72 M3), Vessel remain Alongside at Shuaiba Port, Berth 20. • Vessel CA5- vessel STBY at OD1 location • Vessel Charlie 3- Vessel STBY at berth 4 , Pax in, cargo loaded castoff @10:30, alongside port side of OD1@12:05, Pax transferred,cargo operation, pullout@13:10, alongside of berth 4 @14:35, Pax out, cargo offloaded and Vessel STBY at berth 4
Wednesday 30.09.2026 Normal	• Vessel CA1- Vessel STBY,anchored at OD1 location , Anchor heaved up@17:52, Vessel start enroute from JL-0003 with slow speed for escorting Rig ORIENTAL DRAGON-1 during her Rig move to new location SH-0001 • Vessel CA3- Vessel STBY at berth 20, received fresh water(216 M3), received fuel(108.003 M3), received bentonite, (44.59 MT), cargo operation, remain STBY at berth 20 • Vessel CA5- Vessel remained anchored near OD 1 Next location standby w/further instruction. • Vessel Charlie 3- Vessel STBY at berth 4 , Pax in, castoff @08:55, alongside port side of OD1@10:18, Pax transferred, pullout@10:25, alongside of berth 4 @11:50, Vessel STBY at berth 4

Thanks and Best Regards,

Naser M Gh Hassan
Kuwait Oil Company (KOC)
Snr Drilling & Workover Engineer | Drilling & Workover Engineering Group
NHassan@kockw.com | www.kockw.com
Tel: +965 238 72718
