08 to 14 Oct 2026

OD1 is working on a stuck string. OPH remains off hired.

VESSEL TRIPS	TRUCK MOVES	FLUIDS HANDLED, M³	OVERSTAY CREW
16	**70**	**3,324**	**3**
▲ 7% (15) Last week	▼ 11% (79) Last week	▲ 120% (1,510) Last week	▼ 2 (5) Last week
8 wks, from 9	8 wks, from 41	8 wks, from 1,452	8 wks, from 13

Rig OD1 — ON HIRE

Work on stuck string

Personnel onboard	**91** incl. 51 visa
Overstay crew	COSL **3**
Last week	Pre-spud meeting; safety drills; drilled 42" hole to 100 ft BML, then to 548 ft (in Kuwait Series formation); 570 ft TD; tight spot at 534 ft, stuck at 547 ft and 563 ft
Next steps	RIH 42" stiff BHA to bottom without pumps to check fill; drop gyro; P/O and L/D 42" stiff BHA; RIH 38" and 36" casing as per tally; install 38" bowl and slip to CTU

Rig OPH — OFF HIRED

Rig off-hired

Personnel onboard	**Nil**
Overstay crew	Nil
Last week	Nil
Next steps	Nil


Daily ground operations · Wed 14 Oct 2026


- One truck dispatched to Odfjell Mina Abdallah with an empty 5 m H/H basket, per delivery ticket RM-SP-9074.
- One pickup dispatched to the Cementing Hall at Mina Abdallah with two hand-carry items received from OD1 (manifest RCM-OD-950), per delivery ticket RM-SP-9075.
- One truck arrived from OWS Mina Abdallah with a 10.3 m basket of DRT tools for OD1 (call-off OD-SH1-C-1-15), per delivery ticket OWS-DT-DRT-089.
- One truck arrived at berth 20 from the Shuaiba Port pipe yard with five 30" short joints, per delivery ticket HPM-DT-1614.
- One truck arrived from the Baroid BSS mud plant with six 6 ft mini containers of chemicals for OD1 (call-offs OD-SH1-B-2-4 and B-1-4), per delivery ticket BAR-DT-12B.
- One truck arrived from the Baroid BSS mud plant with six 6 ft mini containers of chemicals for OD1 (call-offs OD-SH1-B-2-4 and B-1-4), per delivery ticket BAR-DT-12B.
- One truck arrived from Odfjell Mina Abdullah with a 15 ft basket holding a casing spear for 36" and 36" casing joints, for Rig OD1 (call-off OD-SH1-B-2-14), per delivery ticket OWS-FIS-030.


- 16 lifts offloaded from three trucks that arrived from the Baroid Magwa plant with mud chemicals and from Odfjell with fishing tools and a 9-1/2" drilling jar; three lifts loaded on two trucks for Odfjell.
- 30" R-1 and R-2 casing joints with 5 ft pup joints loaded at the Shuaiba pipe yard, moved to Shuaiba berth 20 and offloaded there.
- Cargo loaded on **Charlie-3**, per manifest CM-OD-1021.
- Cargo loaded on **CA5**, per manifest CM-OD-1022.
- Vessel movements remain under **MARSEC Level 2**.

Daily Ground Operations, as circulated in the 15.10.2026 email.

Full figures three charts, and every figure

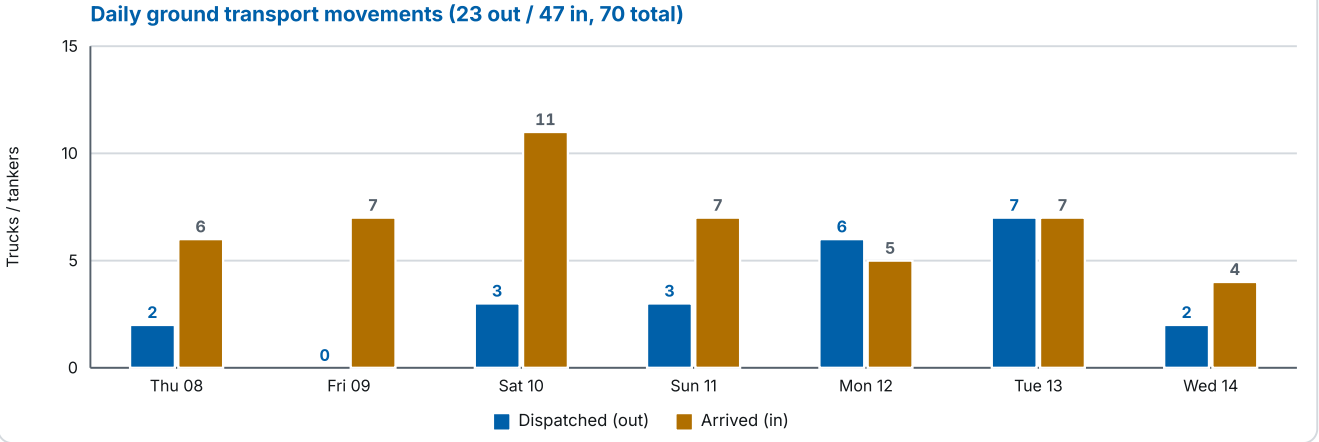

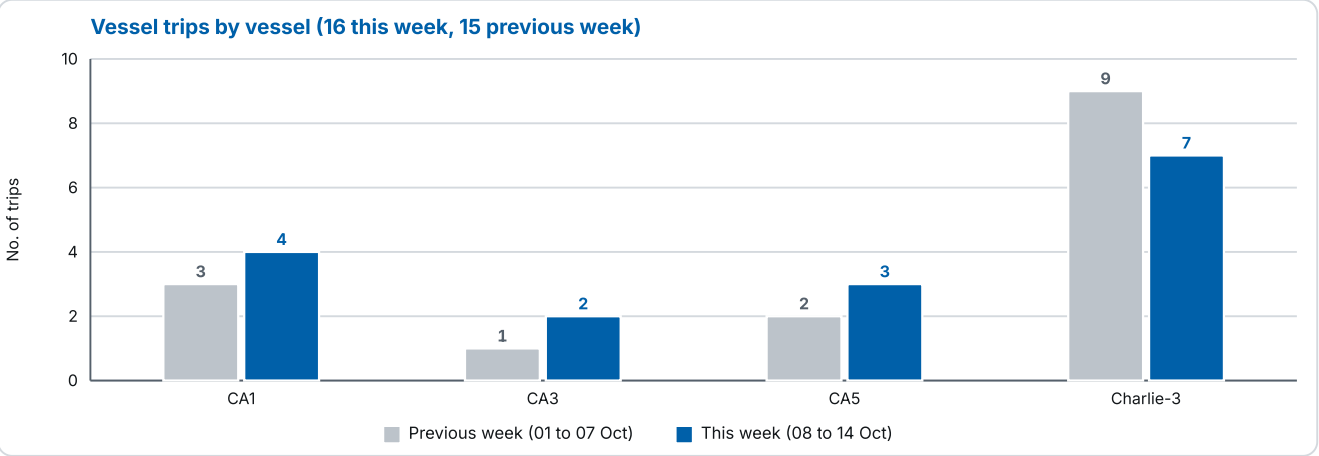

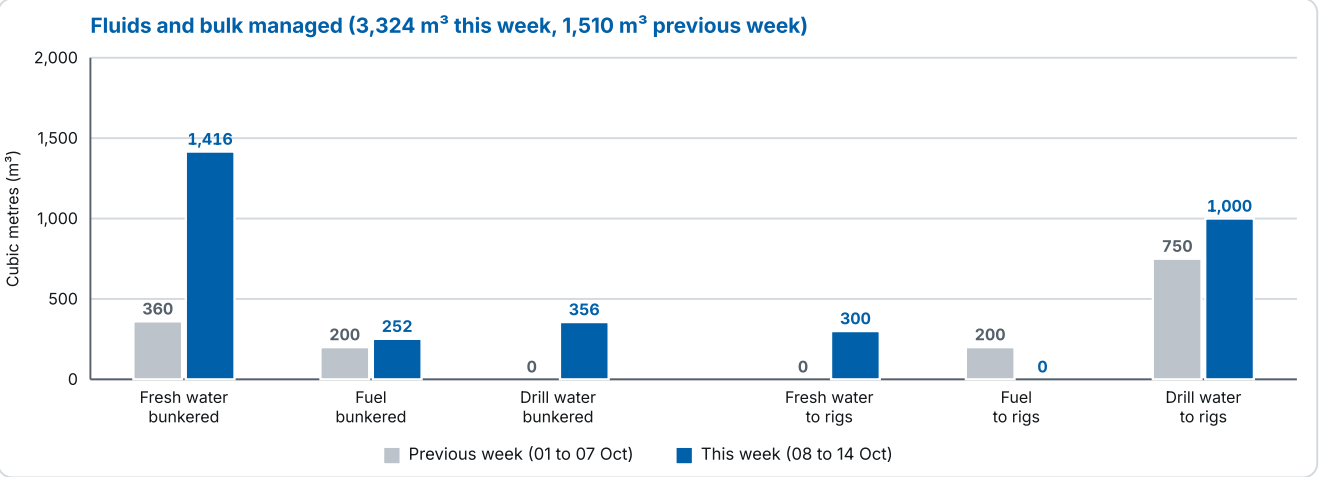

Slops: none recorded.

Metric	08 to 14 Oct 7 days	01 to 07 Oct 7 days	Change
VESSEL TRIPS			
CA1	4	3	▲ 1 (3)
CA3	2	1	▲ 1 (1)
CA5	3	2	▲ 1 (2)
Charlie-3	7	9	▼ 2 (9)
Total vessel trips	**16**	**15**	▲ 1 (15)
VESSEL MOVEMENTS port to rig, rig to port, rig to rig			
CA1	2	2	No change (2)
CA3	3	1	▲ 2 (1)
CA5	3	2	▲ 1 (2)
Charlie-3	16	17	▼ 1 (17)
Total vessel movements	**24**	**22**	▲ 2 (22)
Movements per day	3.4	3.1	▲ 0.3 (3.1)
GROUND TRANSPORT			
Dispatched (out)	23	26	▼ 3 (26)
Arrived (in)	47	53	▼ 6 (53)
Total truck / tanker moves	**70**	**79**	▼ 9 (79)
Moves per day	10.0	11.3	▼ 1.3 (11.3)
FLUIDS AND BULK			
Fresh water bunkered at port	1,416 m^3	360 m^3	▲ 1,056 m^3 (360 m^3)
Fuel bunkered at port	252 m^3	200 m^3	▲ 52 m^3 (200 m^3)
Drill water bunkered at port	356 m^3	0 m^3	▲ 356 m^3 (0 m^3)
Fresh water to rigs	300 m^3	0 m^3	▲ 300 m^3 (0 m^3)
Fuel to rigs	0 m^3	200 m^3	▼ 200 m^3 (200 m^3)
Drill water to rigs	1,000 m^3	750 m^3	▲ 250 m^3 (750 m^3)
Total fluids managed	**3,324 m^3**	**1,510 m^3**	▲ 1,814 m^3 (1,510 m^3)
Slops discharged	0 bbl	0 bbl	No change (0 bbl)
RIGS AND CREW			
Active rigs	1	1	No change (1)
OD1 personnel onboard	91	86	▲ 5 (86)
Overstay crew, KOC	0	1	▼ 1 (1)
Overstay crew, HLB	0	0	No change (0)
Overstay crew, COSL	3	4	▼ 1 (4)

Metric	08 to 14 Oct 7 days	01 to 07 Oct 7 days	Change
Total overstay crew	**3**	5	▼ 2 (5)

Daily log 134 operations

Port operations 7 days, 106 operations

Thursday
08.10.2026
Normal

- 1 X truck was dispatched with 18-5/8'' HPM Circulating equipment's to Shuaiba Port Pipe Yard , as per delivery ticket RM-SP-9049
- 1 X truck was dispatched with 1 x AL-Bahar CAT K6 Power Generator to Al-Bahar Jahara facility, as per delivery ticket RM-SP-9050
- 1 X truck arrived with 1 x Crossover Joint for OD1 as per Call Off: OD-SH1-B-2-1 from Shuaiba Port Pipe Yard, as per delivery ticket HPM-DT-1602
- 1 X truck arrived with 1 × 6mtr. basket with Casing Platform for OD1 as per Call Off: OD-SH1-B-2-2 from Shuaiba Port Pipe Yard, as per delivery ticket HPM-DT-1603
- 1 X truck arrived with 2 x Baskets with TRS tools for OD1 as per Call Off: OD-SH1-B-1-13 from OWS Mina Abdallah Facility, as per delivery ticket OWS-DT-TRS-081
- 1 X truck arrived with 3 x Baskets with TRS tools for OD1 as per Call Off: OD-SH1-B-2-13 from OWS Mina Abdallah Facility, as per delivery ticket OWS-DT-TRS-081
- 1 X truck arrived with 42 × 1.66'' tubing for OD1 as per Call Off: OD-SH1-B-2-13 from OWS Mina Abdallah Facility, as per delivery ticket OWS-DT-TRS-081
- 1 X truck arrived with 1 × 7.8mtr. basket with 36 & 38'' Drift for OD1 as per Call Off: OD-SH1-B-3-1 from Shuaiba Port Pipe Yard, as per delivery ticket HPM-DT-1604
- Al-Mansoori continued inspection at Shuaiba Pipe yard, inspected 36" Casing Joints for Well# SH0001
- Started loading 36" & 38" casing accessories, circulating swages with 36" & 38" casing Drift & casing platform & mobilized to Shuaiba Berth-20
- Continued cargo operation with Vessel Crest Argus-5, loaded 9 cargo lifts on Vessel Crest Argus-5
- 5 X trucks arrived from Odfjell, & Shuaiba Pipe Yard, offloaded the cargo & loaded on Vessel Crest Argus-5.
- Fresh Water transfer to Vessel CA-5 (40M3)

Friday 09.10.2026 Normal	• 2 X Trucks sent to Cementing for collection of Cementing Compressor & Empty 8mtr. Baskets, trucks arrived back to berth-20 as per HPM-DT-1604-A. Offloaded the compressor & baskets at Shuaiba Berth-20 • 1 X Truck sent to Odfjell for collection of 9-5/8" Fishing equipment as per RM-SP-9049 • 3 X trucks sent to Shuaiba Pipe Yard for mobilization of 30" R-3 casing joints. Trucks arrived at Shuaiba Port as per HPM-DT-1606 with 15 joints of 30" R-3 casing joints • 1 X Truck arrived from Cementing with 1 X 6ft. Mini Container with Cementing Chemicals as per Call Off OD-SH1-B-3-8, offloaded the cargo at berth-20 • Started loading 30" casing R-3 Joints from Shuaiba Pipe Yard & mobilized to Shuaiba Berth-20. • Al-Mansoori Continued inspection at Shuaiba Pipe yard, inspected 30" Casing Joints for Well# SH0001 • Started cargo operation with Vessel Crest Argus-1, offloaded 13 backload cargo lifts from Vessel Crest Argus-1 • 1 X trucks arrived from Odfjell with 9-5/8" fishing tools, offloaded the cargo and kept STBY at Shuaiba Berth-20. • Cementing team arrived at Shuaiba Port, started transferring Blend cement from Vessel Crest Argus-1 Tank# 2 to port Silo. Transferred 80MT Lafar G-Neat Cement to Tank@ 2 & Tank# 4 of Vessel Crest Argus-1 • Started transferring Fresh Water to Vessel Crest Argus-1, transferred 14 X 36,000ltrs fresh water to Vessel CA-1 • Started transferring Fuel to Vessel Crest Argus-1, transferred 04 X 36,000ltrs tankers fuel to Vessel CA-1. • Shifted Vessel Crest Argus-1 forward to end of Berth-20 to accommodate Vessel Crest Argus-3 at Berth-20 • Al-Mansoori continued inspection at Shuaiba Pipe yard, inspected 30" Casing Joints for Well# SH0001 • Fresh Water transfer to Vessel CA-5 (40M3) • Fuel Bunkering to Vessel Crest Argus-1(144.008 M3)

Saturday 10.10.2026 Normal	• 1 X truck was dispatched with OWS TRS tools received from OD1 as per manifest RCM-OD-946 to OWS Mina Abdallah facility, as per delivery ticket RM-SP-9057 • 1 X truck was dispatched with BSS trash received from OD1 as per manifest RCM-OD-946 to OWS Mina Abdallah facility, as per delivery ticket RM-SP-9057 • 1 X truck was dispatched with Cut Casing received from OD1 as per manifest RCM-OD-945 to Shuaiba Port Pipe Yard, as per delivery ticket RM-SP-9058 • 1 X truck arrived with OWS Fishing tools for OD1 as per Call Off: OD-SH1-A-1-14 from OWS Mina Abdallah facility, as per delivery ticket OWS-FIS-025 • 1 X truck arrived with 5 × 30'' R3 Casing for OD1 as per Call Off: OD-SH1-B-3-1 from Shuaiba Port Pipe Yard, as per delivery ticket HPM-DT-1608 • 1 X truck arrived with 5 × 30'' R3 Casing for OD1 as per Call Off: OD-SH1-B-3-1 from Shuaiba Port Pipe Yard, as per delivery ticket HPM-DT-1608 • 1 x truck arrived with 4 × 30'' R3 Casing for OD1 as per Call Off: OD-SH1-B-3-1 from Shuaiba Port Pipe Yard, as per delivery ticket HPM-DT-1608 • 1 x truck arrived with Chemical loads for OD1 as per Call Off: OD-SH1-A-3-4 from BSS Mud Plant, as per delivery ticket BAR-DT-09 • 2 x trucks arrived with 4 × 30'' R3 Casing for OD1 as per Call Off: OD-SH1-B-3-1 from Shuaiba Port Pipe Yard, as per delivery ticket HPM-DT-1609 • 5 X truck arrived with 22 × 30'' R3 Casing for OD1 (CAT ID 70126875) from KOC yard • 5 x Trucks offloaded with total of 22 Jts 30" R3 casing CAT ID 70126875 • Offloaded 9-5/8" fishing tools for Pilot Hole at Shuaiba Berth-20. • Offloaded Baroid Mud Chemicals and loaded on Vessel CA3 • Fuel Bunkering to Vessel CA1 (36 M3) • Fresh Water transfer to Vessel CA-3 (594 M3)

Sunday 11.10.2026 Normal	• 1 X truck was dispatched with 3 x lifts COSL tools received from OD1 as per manifest RCM-OD-945 to COSL Mina Abdallah facility, as per delivery ticket RM-SP-9059 • 1 X truck arrived with 2 x lifts for OD1 as per Call Off: OD-SH1-B-9-3 from COSL Mina Abdallah facility, as per delivery ticket COSL-DT-OD-SH1-B-3-1 • 1 X truck arrived with 5 × 30'' R1 & 15' Casing Joints for OD1 as per Call Off: OD-SH1-B-3-1 from Shuaiba Port Pipe Yard, as per delivery ticket HPM-DT-1610 • 1 X truck arrived with 4 × 30'' MLS Running tools with DSA & Base Plate for OD1 as per Call Off: OD-SH1-B-3-1 from Shuaiba Port Pipe Yard, as per delivery ticket HPM-DT-1610 • 1 X call off truck was dispatched with 2 x Rental Tower Lights back to Hetco Yard • 1 X Boom truck was loaded with 4 x X-Overs from OWS Mina Abdallah facility and deliver to Weatherford Mina Abdallah facility as per KOC Rep. request. • 1 X truck was dispatched with 3mtr. basket MLS Running tools received from OD1 as per manifest RCM-OD-946 to HETCO Ahmadi facility, as per delivery ticket RM-SP-9060 • 1 X truck arrived with 2 × 30'' Float Shoe & Collar for OD1 as per Call Off: OD-SH1-B-3-1 from Shuaiba Port Pipe Yard, as per delivery ticket HPM-DT-1610 • 1 X Call off truck arrived with 7 × 30'' R2 & 10'' Cut Casings for OD1 as per Call Off: OD-SH1-B-3-1 from Shuaiba Port Pipe Yard, as per delivery ticket HPM-DT-1611 • 1 X call off trucks arrived with 2 × 3mtr. empty baskets from OWS Mina Abdallah facility, as per delivery ticket OWS-DT-BASKET-20 • Cargo operation with Vessel Crest Argus-1, loaded 11 cargo lifts on Vessel CA-1 deck as per updated Lookahead received from Rig OD-1 • 1 X Al Rashed Lorry arrived with 12 Lube Oil Drums with 2 X Boxes, Offloaded the cargo at Berth-20 • Loaded 30" casing R-2, R-1, pup joints & 36" Float Shoe & Float Collar joint from Shuaiba Pipe Yard & mobilized to Berth-20 and offloaded all R-2, R-1 joints with pup joints and 36" back-up shoe track at berth-20 • Al Mansoori completed inspection of 5' Pup joints(02 Nos), 36" Float Shoe and collar, 38X38" X over(02 Nos) • Baroid team transferred 45.26 MT Bulk Bentonite to Vessel Crest Argus-3 from Banana mobile silos. • Fresh Water transfer to Vessel CA-1 (180 M3)

Monday 12.10.2026 Normal	• 1 X truck was dispatched with COSL tools received from OD1 as per manifest RCM-OD-945 to COSL Mina Abdallah facility, as per delivery ticket RM-SP-9061 • 1 X truck was dispatched with COSL tools received from OD1 as per manifest RCM-OD-946 to COSL Mina Abdallah facility, as per delivery ticket RM-SP-9062 • 1 X truck was dispatched with 6 × 6′ mini container received from OD1 as per manifest RCM-OD-947 to BAROID BSS Mud Plant facility, as per delivery ticket RM-SP-9063 • 1 X truck was dispatched with 1 × 10.3mtr. empty basket to OWS Mina Abdallah facility, as per delivery ticket RM-SP-9064 • 1 X truck was dispatched with 1 × 7mtr. empty basket to OWS Mina Abdallah facility, as per delivery ticket RM-SP-9065 • 1 X truck was dispatched with 3 x OD1 Empty food containers to Reliance Subhan facility, as per delivery ticket RM-SP-9066 • 1 X truck arrived with 3 x lifts for OD1 as per Call Off: OD-SH1-B-9-3B from COSL Mina Abdallah facility, as per delivery ticket COSL-DT-OD-SH1-B-3-1B • 1 X truck arrived with 1 × 7.8mtr. empty basket from COSL Mina Abdallah facility, as per delivery ticket HAL-DT-HAL-20261012 • 1 X Call off truck arrived with 1 × 36′′ Landing Joint for OD1 as per Call Off: OD-SH1-B-3-1 from Shuaiba Port Pipe Yard, as per delivery ticket HPM-DT-1612 • 1 X boom truck arrived with 1 x Cementing toolbox for OD1as per Call Off: OD-SH1-B-4-8 from Cementing Hall Mina Abdallah facility, as per delivery ticket HPM-DT-1612 • 1 X truck arrived with 6 × 6′ mini container Chemical Loads for OD1as per Call Off: OD-SH1-B-1-4)from BSS Mud Plant facility, as per delivery ticket BAR-DT-11 • Cargo operation with Vessel CA5, offloaded 23 backload cargo lifts from Vessel deck as per RCM-OD-947 & loaded 60 empty Mud skips on Vessel CA-5 deck. • Cargo operation with Vessel Charlie-3, offloaded 1 backload cargo lift from Charlie-3 deck • Loaded 15 cargo lifts on 6 regular truck & sent to service providers, offloaded 12 cargo lifts during the day shift received from COSL, Cementing Baroid & KOC. • Baroid team transferred Bulk Barite to Vessel Crest Argus-5 from Banana mobile silos. • Al-Mansoori conducted Inspection of 36" Landing Joints at Shuaiba Pipe Yard. • Fresh Water transfer to Vessel CA-5 (220M3)

Tuesday 13.10.2026 Normal	• 1 X truck was dispatched with 2 × 12'' Shock Sub received from OD1 as per manifest RCM-OD-948 & 6.5'' Drilling Jar to NOV Ahmadi facility, as per delivery ticket RM-SP-9068 • 1 X truck was dispatched with COSL tools received from OD1 as per RCM-OD-947 to COSL Mina Abdallah facility, as per delivery ticket RM-SP-9069 • 1 X truck was dispatched with COSL tools received from OD1 as per RCM-OD-947 to COSL Mina Abdallah facility, as per delivery ticket RM-SP-9070 • 1 X truck was dispatched with 5 × 6' empty mini container to BAROID BSS Mud facility, as per delivery ticket RM-SP-9071 • 1 X truck was dispatched with 6 × 6' empty mini container to BAROID BSS Mud facility, as per delivery ticket RM-SP-9072 • 1 X pickup was dispatched with 3 x Hand Carry received from OD1 as per manifest RCM-OD-949 to HPM, Cementing & BAROID Lab Hall Mina Abdallah facility, as per delivery ticket RM-SP-9073 • 1 X truck was dispatched with 4 x Full Trash Skips received from CA1, CA3, CA5 & Charlie 3 & Shore base to Hetco Stevedoring facility, as per delivery ticket WT-SB-117 • 1 X truck arrived with 1 × 38'' Short Joint from KOC Yard-4 to Shuaiba Port Pipe Yard, as per KOC delivery ticket 2026/10/13/0474 • 1 X truck arrived with 1 × 38'' Short Joint from KOC Yard-4 to Shuaiba Port Pipe Yard, as per KOC delivery ticket 2026/10/13/0511 • 1 X truck arrived with DRT tools for OD1 as per Call Off: OD-SH1-C-2-15 from OWS Mina Abdallah facility, as per delivery ticket OWS-DT-DRT-087 • 1 X truck arrived with 1 × 7 Empty basket from NOV Ahmadi facility, as per delivery ticket HPM-DT-1613 • 1 X truck arrived with 1 × 7mtr. basket DRT tools for OD1 as per Call Off: OD-SH1-C-2-15 from OWS Mina Abdallah facility, as per delivery ticket OWS-DT-DRT-087 • Loaded 22 cargo lifts on 7 regular truck & sent to service providers & offloaded 5 cargo lifts during the day shift received from KOC, Odfjell & KOC. • Offloaded 2 X trucks at Shuaiba Pipe Yard with 3 X 30" R-1 Casing joint & 1 X 38" R-1 Casing Joint received from KOC Yard# 5. • 1 X truck arrived with 1 × 7mtr. basket DRT tools for OD1 as per Call Off: OD-SH1-C-2-15 from OWS Mina Abdallah facility, as per delivery ticket OWS-DT-DRT-088 • Al-Mansoori conducted Inspection of 30" R-1 Casing Joints at Shuaiba Pipe Yard. • Offloaded 1 X Basket with 33" String stabilizers & 33" Near bit Stabilizers received from Odfjell. • Fresh Water transfer to Vessel Charlie-3 (18 M3) • Transferred Fuel to Vessel CA5 (72.002 M3)

Wednesday 14.10.2026 Normal	• 1 X truck was dispatched with 1 × 5mtr. H/H basket Empty to Odfjell Mina Abdallah facility, as per delivery ticket RM-SP-9074 • 1 X pickup was dispatched with 2 x Hand Carry received from OD1 as per manifest RCM-OD-950 to Cementing Hall Mina Abdallah facility, as per delivery ticket RM-SP-9075 • 1 X truck arrived with 1 × 10.3mtr. basket DRT tools for OD1 as per Call Off: OD-SH1-C-1-15 from OWS Mina Abdallah facility, as per delivery ticket OWS-DT-DRT-089 • 1 X truck arrived with 5 × 30'' Short Joint from Shuaiba Port Pipe Yard to Berth-20, as per delivery ticket HPM-DT-1614 • 1 X truck arrived with 6 × 6' mini container Chemical loads for OD1 as per Call Off: OD-SH1-B-2-4 & B-1-4 from BAROID BSS Mud Plant facility, as per delivery ticket BAR-DT-12B • 1 X truck arrived with 6 × 6' mini container Chemical loads for OD1 (Call Off: OD-SH1-B-2-4 & B-1-4) from BAROID BSS Mud Plant facility, as per delivery ticket BAR-DT-12B • 1 X truck arrived with 1 × 15' Basket with Casing Spear for 36" & 36" Casing joints for Rig OD1 as per Call Off: OD-SH1-B-2-14 from Odfjell Mina Abdullah facility, as per delivery ticket OWS-FIS-030 • Offloaded 16 lifts from 3 X trucks arrived from Baroid Magwa plant with Mud Chemicals & Odfjell with Fishing tools & 9-1/2" Drilling Jar & loaded 3 X lifts on 2 trucks for odfjell. • Loaded 30" R-1 & R-2 Casing joints with 5ft. Pup Joints joint from Shuaiba Pipe Yard & mobilized to Shuaiba Berth-20 and offloaded casing joints at berth-20. • Loaded cargo Charlie-3 as per manifest CM-OD-1021. • Loaded cargo CA5 as per manifest CM-OD-1022.

Vessel movements 7 days, 28 operations

Thursday 08.10.2026 Normal	• Vessel CA1- Vessel remain at OD1 location,Anchor heaved up@06:25, Vessel under Starboard side Crane of OD1@07:40,Transferred Drill water(200 M3), Cargo operation,Transferred Fresh water (100M3), Vessel pulled out@15:50 shifted to port side,Transferred Bentonite from Bulk Tank No.6(40.11MT), Vessel pulled out @20:00, sailed to Shuaiba@20:30, arrived and secure Berth 20@23:35. • Vessel CA3- Vessel t 200 m away from OD1 and stand by, monitoring / observed DGPS Signal, approaching OD1, in position on the p/s OD1@01:50, transferred barite to OD1, Stop Transferring Barite to OD1 due to the Line chock@6:55, pull out 50 m from OD1 @7:02,pull out 300 m away from OD1@9:16,waiting for instruction, Approach p/s OD1@10:20,in position on the p/s OD1@10:42, Resumed Barite transfer(250MT), pull out@16:10,STBY 500 M away from OD1. • Vessel CA5- Vessel remain alongside at berth 20, deck cargo operation, received drill water(40M3), Cast off@16:36,arrived at OD 1 location@19:36,In post p/s crane OD 1@20:50, transferred drill water(200M3) • Vessel Charlie 3- Vessel STBY at berth 4 , Pax in,castoff @08:05, alongside port side of OD1@09:20, Pax transferred, pullout@ 09:42 , proceed to Shuaiba, arrived at berth 4@11:55, pax disembarkerd, and STBY at berth 4.

Friday 09.10.2026 Normal	• Vessel CA1 - Vessel at berth 20, Received Drill Water and fres water(504 M3), received fuel (180M3), Transferred B cement to onshore Silo tank(12.2 MT), received G cement(80 MT), Vessel shifted forward along berth 20@17:18, resumed receiving drill water , Vessel cast off@19:18, arrived Anchorage area@20:42 and remain STBY. • Vessel CA3 - Vessel STBY 500 M away from OD1, heave up anchor@0:08, in position on the p/s OD1@2:40,transferred barite to OD1(20MT), Deck Cargo operation, pulled 300m away@13:45,back to position on the p/s OD1@14:26,deck Cargo operation, pull out@ 15:54, departed to Shuaiba Port@15:54, secured alongside at Shuaiba@19:45, received bentonite(40.6MT), Deck Cargo operation, fresh water receiving in progress. • Vessel CA5 - vessel pulled out 500 M away from OD1@ 00:20 and STBY, heave up anchor@15:05, in position on the p/s OD1@16:10, cargo operation is in progress. • Vessel Charlie 3 - Vessel STBY at berth 4, castoff @12:25, alongside port side of OD1@13:40, Pax received, pullout@ 13:43 , proceed to Shuaiba, arrived at berth 4@14:45, Loaded cargo,castoff @ 22:05, alongside STBD side of OD1@23:10,cargo offloaded, pax received, pullout@ 23:40 and vessel underway to berth 4
Saturday 10.10.2026 Normal	• Vessel CA1 - Vessel STBY at anchorage,Anchor heaved up@05:12, Vessel proceed to berth 20,Vessel secured Port side@07:12,Received Drill water(144M3), received fuel(36M3), STBY at berth 20 • Vessel CA3 - Vessel STBY at Berth 20, Received Drill and fresh water(594 M3), transferred cement to silo(47 MT),received Cement from Shore Trucks (120 MT) , cargo operation, Vessel remain secured Port side of berth 20 • Vessel CA5 - at OD1, cargo operation is in progress,pullout to 300 M@ 11:00, vessel back to p/s crane OD 1 @12:15, pullout to 400 M@15:36 and STBY. • Vessel Charlie 3 - Vessel STBY at berth 4, castoff @5:30, arrived Khiran@07:40, pax embarked from Khiran,proceed to OD1, alongside port side of OD1@11:25,Pax in/out, pullout@ 11:35, arrived Khiran@14:20, pax disembarked,proceed to Shuaiba@14:40, secured at berth 4@16:50 and STBY.
Sunday 11.10.2026 Normal	• Vessel CA1 - Vessel STBY at Berth 20, Received Drill and fresh water(180M3), Received Bentonite(45.26 MT), cargo operation, Vessel remain secured Port side of berth 20 • Vessel CA3 - Vessel STBY at Berth 20, Received Drill water(72 M3), vessel cast off Departed to OD1@3:00, arrived at OD1 Location@6:00, vessel in position on the p/s OD1@19:10,Cement to OD1 (120 MT), vessel remain alongside at s/s of OD1. • Vessel CA5 - at OD1 STBY 400 M away,In p/s crane@06:50,deck cargo operation,loss DGPS signal ,pull out 20 mtrs@10:30, vessel in p/s crane @11:10,deck cargo operation, Barite transferred (47MT), Pull out 500m@19:00 and STBY. • Vessel Charlie 3 - Vessel STBY at berth 4,Loaded cargo.

Monday 12.10.2026 Normal	• Vessel CA1 - Vessel STBY at Berth 20, cargo loaded, castoff@15:18, Vessel arrivedOD1@18:24 and STBY at anchorage. • Vessel CA3 - Vessel remain alongside at s/s of OD1, cargo operation, pull out@01:36,STBY and anchored at OD1 Location, heave up anchor@07:30, vessel in position on the p/s OD1@08:40,Deck cargo operation,Pullout@ 09:33,STBY 500m away,heave up anchor@13:20, vessel in position on the p/s OD1@14:18,cargo operation, transferred fresh water(200M3), transferring drilling water is in progress. • Vessel CA5 - STBY at OD1 location,Heave up anchor@3:20,Arrived at shuaiba port@7:00,recieved drilling water (140M3), received fresh water(80M3), deck cargo operation,barite received(164 MT), vessel emain alongside at berth 20, Shuaiba port • Vessel Charlie 3 - Vessel STBY at berth 4,Pax embarked,castoff @09:00,alongside STBD side of OD1@10:05, Pax transferred, cargo offloaded, pullout@ 10:36 500m zone, back to rig STBD side@12:55, pax in,loaded cargo, pullout@13:11, secured at berth 4@14:20, pax disembarked and STBY at berth 4
Tuesday 13.10.2026 Normal	• Vessel CA1 - Vessel remains standby anchorage near OD1,Anchor heaved up@12:22, STBD side of rig@13:30, transferred G cement(65 MT),cargo operation, pullout@20:10 and moved to anchorage. • Vessel CA3 - Vessel remain alongside at p/s of OD1, transferred drilling water(400M3) cargo operation, is in progress. • Vessel CA5 - vessel remain alongside at berth 20, Shuaiba port, received fuel (72.002 M3) • Vessel Charlie 3 - Vessel STBY at berth 4,Pax embarked,castoff @09:00,alongside STBD side of OD1@10:05, Pax transferred, cargo offloaded, pullout@ 10:55, secured at berth 4@12:10, pax disembarked, fresh water received(18M3),and STBY at berth 4.
Wednesday 14.10.2026 Normal	• Vessel CA1 - Vessel remains standby anchorage near OD1 • Vessel CA3 - Vessel remain alongside at p/s of OD1, cargo operation, pull out@05:30,Exit 500M zone,vessel back to position on the p/s OD1@07:00, transferred Base Oil to OD1 (300 Bbls), transferr(40.6MT),transferred drill water(200M3),cargo operation, pull out@19:26,Exit 500M zone,DP off & Vsl Departed to Shuaiba Port@19:45,Secured alongside at Shuaiba Port@23:10. • Vessel CA5 - vessel remain alongside at berth 20, Shuaiba port, Cast off@18:18,Arrived at OD 1 location@21:20 and remain anchored at OD 1 location • Vessel Charlie 3 - Vessel STBY at berth 4,Pax embarked,castoff @06:45,alongside STBD side of OD1@08:05, Pax transferred, pullout@ 8:15, secured at berth 20@09:30, Loaded cargo, castoff @13:20, arrived Khiran@15:25,Pax in,proceed to OD1@15:35, alongside STBD side of OD1@18:30,offloaded cargo, Pax transferred, pullout@19:00, secured alongside of berth 4@20:35 and STBY at berth 4.

Thanks and Best Regards,

Naser M Gh Hassan
Kuwait Oil Company (KOC)
Snr Drilling & Workover Engineer | Drilling & Workover Engineering Group
NHassan@kockw.com | www.kockw.com
Tel: +965 238 72718
