

20 to 25 Aug 2026

OD1 finished the wellhead N/D and is preparing to move to BOUM-0001. OPH off-hired, and overstay crew appeared for the first time at 13.

VESSEL TRIPS

9

Baseline week, no comparison

VESSEL MOVEMENTS

22

Baseline week, no comparison

TRUCK MOVES

41

41 counted once each (46 as published)
Baseline week, no comparison

FLUIDS HANDLED, M³

1,452

Baseline week, no comparison

OVERSTAY CREW

13

Baseline week, no comparison

Rig OD1

ON HIRE

Rig preparations for next well

Personnel onboard	82 incl. 55 visa
Overstay crew	HLB 2 COSL 11
Last week	N/D wellhead sections, install 30" corrosion cap, rig maintenance as plan
Next steps	Rig preparation for move; rig move for new well BOUM-0001

Rig OPH

OFF HIRED

Rig off-hired


Personnel onboard	Nil
Overstay crew	Nil
Last week	Nil
Next steps	Nil. Backload demobilisation to COSL Mina Abdallah ongoing

What happened


- **OD1 completed the wellhead N/D and the 30" corrosion cap installation.** The rig is preparing to move to new well **BOUM-0001**.
- **Overstay crew rose to 13** (HLB 2, COSL 11) from nil the week before. Contractor demobilisation needs follow up with COSL.
- Lower vessel and truck activity follows **OPH being off-hired**, one active rig against two the week before, not a reduction in service level.
- CA1 carried the bulk and cargo programme across 4 trips, including a 52 lift peak offload at Shuaiba on Sat 22.
- Charlie-3 handled all crew changes across 5 trips, including 14 Pax via MM Port on Sat 22, and an 18 in / 8 out change at OD1.
- Ground activity peaked on **Tue 25 with 9 dispatches**, driven by OPH demobilisation: batch mixers, an 18-3/4" annular BOP and DP backloads to COSL Mina Abdallah.
- **4 vacuum trucks of 9.0 ppg contaminated slops** went to MG-0348 and **3 full mud skips** to the NCC SEK plant, loaded Sun 23 and dispatched Mon 24, with no HSE incident. CA1 also transferred 320 bbl of slops to vacuum tankers at Shuaiba.
- Vessel movements remain under **MARSEC Level 2**.

Full figures three charts, and every figure


Daily ground transport movements (30 out / 11 in, 41 total)

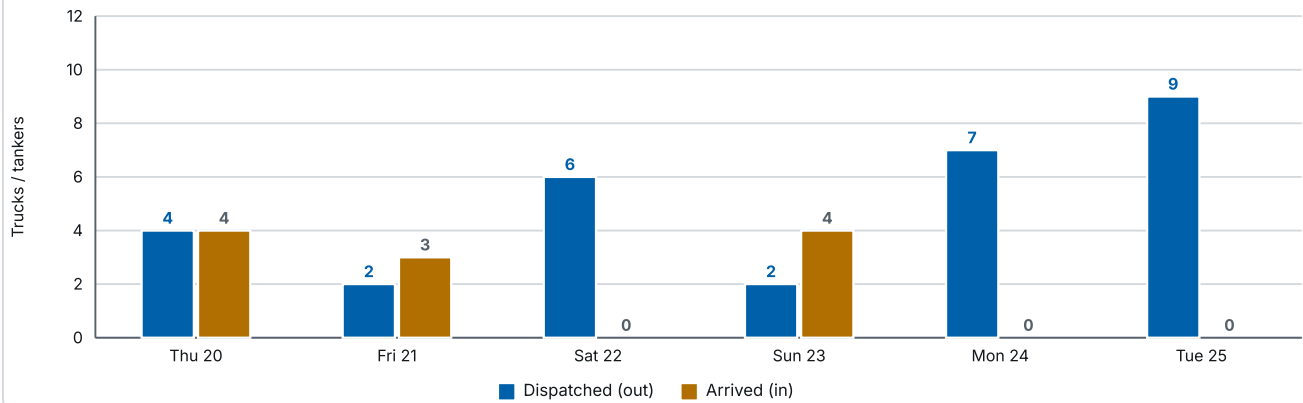

Vessel trips by vessel (9 total)

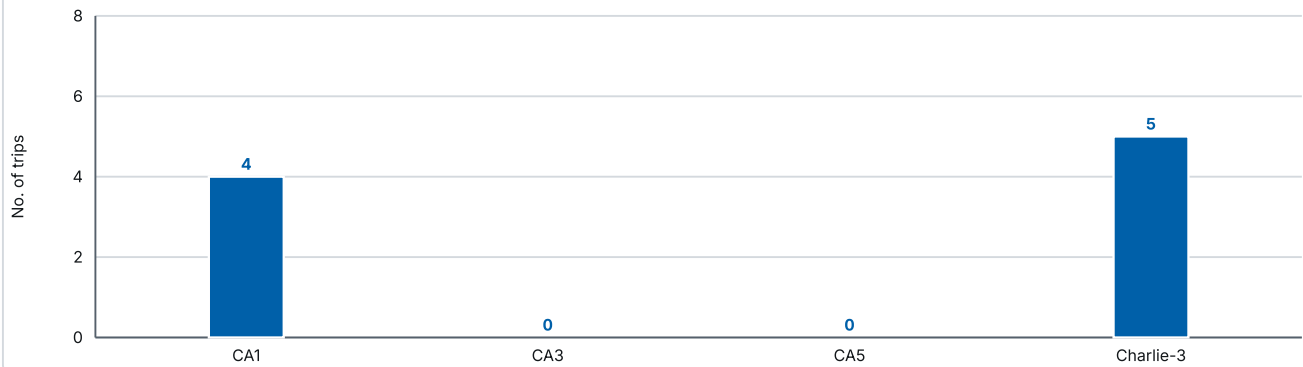

Fluids and bulk managed (1,452 m³ total)

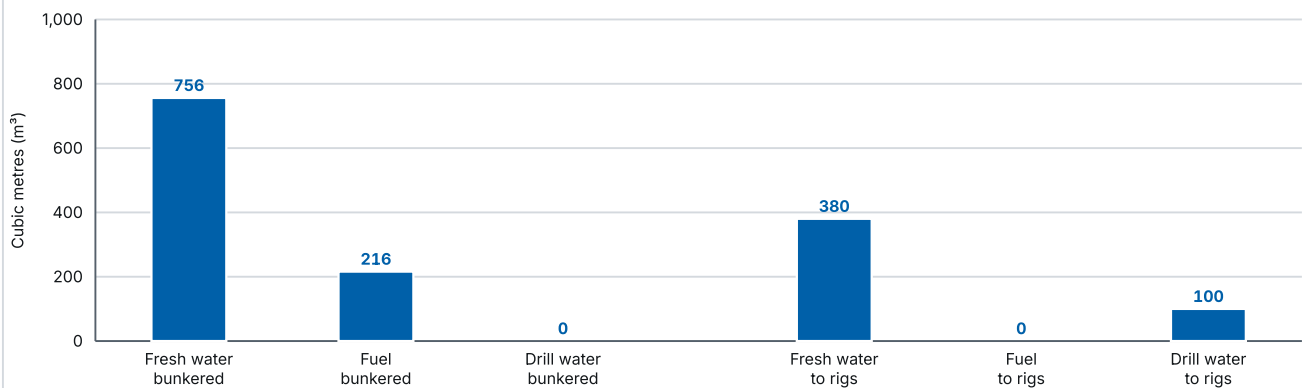

Slops: 320 bbl discharged to vacuum tankers.

Daily log 52 operations

Port operations 6 days, 28 operations

Thursday 20.08.2026 Not Normal	- One boom Truck loaded with 3 DST X-Overs, 9 KOC X-Overs and 2 Landing Nipples sent to Shuaiba Pipe Yard & DST Facility. - One truck loaded with 1 Mini container and 1 Basket with Well Testing tool rack and Propane Cylinders sent to SWT facility. - One truck loaded with 1 cargo Basket with Well Testing equipment and sent to SWT facility. - One truck loaded with Well head Sec-C, Sec-D, Sec-E & Sec-F with 3-1/2" Tubing Pup joints and sent to Shuaiba Pipe yard. - Two trucks arrived at Shuaiba Port from Odfjell with 36" & 38" TRS equipment as per Call Off OD-JL3-N-8-13 for OD1. - Two trucks arrived at Shuaiba Port from COSL Warehouse as per Call Off OP-RI3-N-16-3 for OPH. no night shift
Friday 21.08.2026 Not Normal	- Two Trucks sent to Shuaiba Pipe Yard with 31 joints of 7-5/8", 9-5/8", 13-5/8" & 18-5/8" R-3 casing as per RCM-OD-916 & 919. - Two Trucks arrived from PE/ FRAC with 2 Baskets, offloaded the baskets at Shuaiba Berth-20. - One truck arrived from MPD Facility with 2 baskets. Offloaded at Shuaiba Berth-20. no night shift
Saturday 22.08.2026 Not Normal	- Three trucks were dispatched with 8 lifts received from OD1 to OWS Mina Abdallah facility. - Two trucks were dispatched with 14 bundles of DP, DC & HWDP received from OD1 & OPH to COSL Mina Abdallah facility. - One truck was dispatched with 4 lifts received from OD1 to OWS Mina Abdallah facility. no night shift
Sunday 23.08.2026 Not Normal	- One truck was dispatched with 3 lifts received from OPH (RCM-OP-1185) to CMT hall Mina Abdallah facility. - One truck was dispatched with 3 lifts received from OD1 (RCM-OD-923) to COSL Mina Abdallah facility. - Four vacuum trucks were loaded with 9.0ppg contaminated oily Slops received from OD1 to MG-0348 for disposal. - Four trucks arrived with 16 lifts for OD1 (call off: OD-JL3-N-12-3) from COSL Mina Abdallah facility. - One truck was loaded with 3 full mud skips received from OD1 to NCC SEK plant. no night shift
Monday 24.08.2026 Not Normal	- Four vacuum trucks were dispatched with 9.0ppg contaminated oily Slops received from OD1 to MG-0348 for disposal. - One truck was dispatched with 3 full mud skips received from OD1 to NCC SEK plant. - One truck was dispatched with 7 lifts with Cut Casing received from OD1 to KOC Shuaiba Port Pipe yard. - One truck was dispatched with 7 lifts with MLS Running tool with cut casing received from OD1 to KOC Shuaiba Port Pipe yard. no night shift

Tuesday
25.08.2026
Not Normal

- Two trucks were dispatched with 2 Batch Mixer received from OD1 & OPH to Cementing Hall Mina Abdallah facility.
- Two trucks were dispatched with 2 backloads received from OPH to COSL Mina Abdallah facility.
- One truck was dispatched with 2 backloads received from OPH to COSL / TSS Hall Mina Abdallah facility.
- One truck was dispatched with 2 joints 30" R3 casing from Berth- 20 to KOC Shuaiba Port pipe yard facility.
- One truck was dispatched with 2 joints 18-5/8" & 24" R3 casing ea. from Bert- 20 to KOC Shuaiba Port pipe yard facility.
- One truck was dispatched with 3 joints 5-1/2" DP received from OPH to COSL Mina Abdallah facility.
- One truck was dispatched with 1 × 18-3/4" Annular BOP received from OPH to COSL Mina Abdallah facility.

no night shift

Vessel movements 6 days, 24 operations

Thursday
20.08.2026
Normal

- Vessel CA1 - Vessel arrive OD1, pull out due to weather, vessel STBY 500 meter of OD1, at 05:50 vessel sail to Shuiaba port, arrived Shuaiba port at 09:50, vessel received 108 m3 fresh water, pick up 4 Pax MOI cargo operation, backload 4 lifts, at 15:07 cast off and sail to OD1, arrived OD1 at 18:46, cargo operation, backload 2 lifts, at 19:12 pull out and sail to Shuaiba port, arrived Shuaiba port at 22:34, MOI 4 Pax disembarked, cargo operation, offload 15 lifts from OPH and 2 lifts from OD1, vessel received 36 m3 fresh water, Vessel STBY at Shuiba port.
- Vessel CA3 - vessel STBY at OPH location,.
- Vessel CA5 - vessel STBY at OD1 location
- Vessel Charlie 3 - Vessel STBY at Shuaiba Port B.4.

Friday
21.08.2026
Normal


- Vessel CA1 - vessel at Shuaiba port B.20, cargo operation, backloading 6 lifts, received 72 m3 fresh water, at 03:25 cast off and sail to OD1, vessel arrived OD1 at 07:15, cargo operation, offload 7 lifts and backload 40 lifts, transfer 200 m3 fresh water to OD1, at 22:55 pull out and sail 500 meter away from OD1, vessel STBY 500 meter away from OD1 location.
- Vessel CA3 - vessel STBY at OPH location,.
- Vessel CA5 - vessel STBY at OD1 location
- Vessel Charlie 3 - vessel STBY at Shuaiba port, at 16:45 cast off and sail to OD1, arrived OD1 at 18:00, received 1 Pax,, at 18:06 pull out and sail to Shuaiba port, arrived Shuaiba port at 19:20, disemberked 1 Pax, vessel STBY at Shuaiba port B.4.

Saturday 22.08.2026 Normal	• Vessel CA1 - vessel STBY 500 meter away from OD1, at 00:30 vessel sail to Shuaiba port, arrived Shuaiba port at 04:10, cargo operation, offload 52 lifts, backload 12 lifts, vessel received 216 m3 fresh water, at 15:25 cast off and sail to OD1, arrived OD1 at 19:25, cargo operation, offload 7 lifts, backload 3 lifts, transfer 100 m3 drill water to OD1, at 22:18 pull out and sail 500 meter away from OD1, vessel STBY 500 meter away from OD1 location. • Vessel CA3 - vessel STBY at OPH location. • Vessel CA5 - vessel STBY at OD1 location. • Vessel Charlie 3 - Vessel STBY at Shuaiba port, at 06:05 cast off and sail to MM port loaction, arrived MM port location at 07:35, receied 14 Pax from Abul Kheer boat, sail to OPH, arrived OPH at 09:12, transfer 6 Pax to OPH, at 09:32 pull out and sail to OD1, arrived OD1 at 10:55, tranfer Pax (8 out / 18 in), at 11:40 pull out and sail to OPH, arrived OPH at 13:06, transfer Pax (4 out/ 4 in), cargo operation, backload 3 lifts, at 14:17 pull out and sail to MM port location, at 15:20 arrived MM port location, transfer 10 Pax to Abul Kheer boat, arrived Shuaiba port at 17:10, disembark 8 Pax, offload 3 lifts vessel STBY at Shuaiba port B.4.
Sunday 23.08.2026 Normal	• Vessel CA1 - vessel STBY 500 meter away from OD1 location, at 05:20 vessel under portside of OD1, received 290 bbl SLOP, cargo operation, backload 2 lifts, at 07:38 pull out and sail to Shuaiba port, arrived shuaiba port at 11:12, cargo operation, offloading 5 lifts, backloading 32 lifts, transfer 320 bbl SLOP to vacuum tankers, received 108 m3 fresh water, at 18:45 cast off and sail to OD1, arrived OD1 at 22:32, cargo operation, offload 9 lifts and backload 1 lifts, vessel at OD1 • Vessel CA3 - vessel STBY at OPH location. • Vessel CA5 - vessel STBY at OD1 location. • Vessel Charlie 3 - Vessel STBY at Shuaiba port, backload 2 lifts, at 09:45 cast off and sail to OD1, cargo operation offload 2 lifts, at 11:15 pull out and sail to shuaiba port, arrived Shuaiba port at 12:40, vessel STBY at Shuaiba port B.4.
Monday 24.08.2026 Normal	• Vessel CA1 - vessel at OD1, cargo operation, offload 8 lifts,backload 1 lift, at 01:25 pull out and sail to OPH, arrived OPH at 09:55, cago operation, offload 17 lifts, backload 10 lifts, transfer 180 m3 fresh water to OPH, transfer 1 Pax of CA3 to OPH, at 17:00 pull out and sail to Shuaiba port, arrived Shuaiba port at 20:20, disembarked 1 Pax, received 72 m3 Fuel and 36 m3 fresh water, cargo operation, backload 7 lifts, vessel at Shuaiba port B.20. • Vessel CA3 - vessel STBY at OPH location. • Vessel CA5 - vessel STBY at OD1 location. • Vessel Charlie 3 - vessel STBY at Shuaiba port B.4.
Tuesday 25.08.2026 Normal	• Vessel CA1 - Vessel at Shuaiba port, continue cargo operation, offload 3 lifts, vessel received 144 m3 Fuel and 180 m3 fresh water, vessel STBY at Shuaiba port B.20. • Vessel CA3 - vessel STBY at OPH location. • Vessel CA5 - vessel STBY at OD1 location. • Vessel Charlie 3 - Vessel STBY at Shuaiba port, embarked 16 Pax, at 07:40 cast off and sail to OD1, arrived OD1 at 09:00, transfer Pax (16 Pax out/19 Pax in), at 09:19 pull out and sail to Shuaiba port, arrived Shuaiba port at 10:45, disembarked 19 Pax, cargo operation, backload 3 lifts, at 12:00 cast off and sail to MM port, Arrived MM port location at 13:25, received 1 Pax from Abul Kheer boat, at 13:35 sail to OD1, arrived OD1 at 15:55, cargo operation, offload 3 lifts, transfer 1 Pax to OD1, , at 16:51 pull out and sail to Shuaiba port, arrived Shuaiba port at 18:15, vessel STBY at Shuaiba port B.4.

One trip is one outbound voyage from Shuaiba Port plus its return; a rig to rig transit is not a new trip. A vessel movement is a transit between locations -- port to rig, rig to port or rig to rig -- so a pull-out and re-berth at the same rig is not one. A truck move counts one truck unit per dispatch or arrival, and a truck loaded on one day and dispatched the next is one movement, counted on dispatch. Every week is counted on that one rule, which is why 20 to 25 Aug reads 41 truck moves here against the 46 its own report published. Source: DWOS_Weekly_Offshore_Logistics_Report_26.08.2026.xlsx (report 22, sheets Port and Vessel), plus Offshore_Logistics_Weekly_Update_26082026_v2.html and the 26.08.2026 email for the rig summaries. This is the earliest week tracked here, so no comparison is drawn. The 26 Aug 2026 report compared it against 06 to 12 Aug 2026: 16 vessel trips, 68 truck moves, 2 active rigs, nil overstay.

26 Aug to 02 Sep 2026

OD1 cut the 38" conductor and was released to BOUM-0001, now waiting on location clearance. Overstay down to 10, OPH still off-hired.

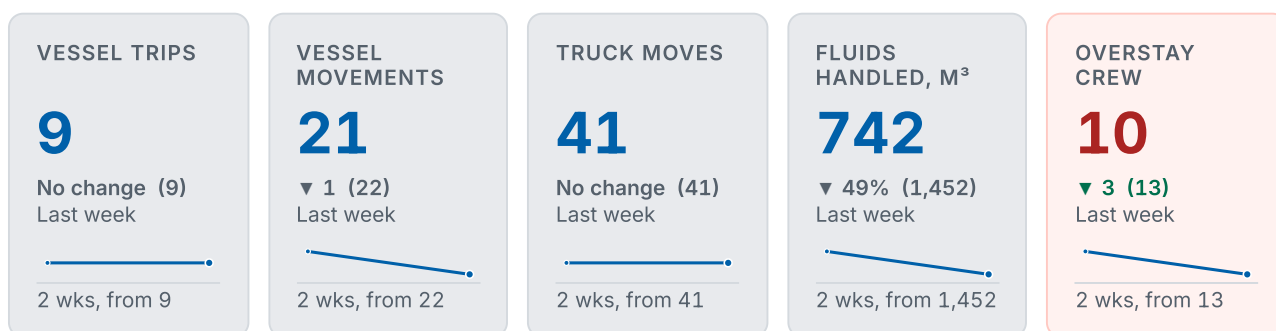

Rig OD1

ON HIRE

STBY waiting for BOUM-0001 location clearance

Personnel onboard	75 incl. 53 visa
Overstay crew	COSL 10
Last week	Cut 38" conductor pipe, install protection structure, release rig to new well BOUM-0001, waiting for BOUM-0001 location clearance
Next steps	Rig preparation for move; rig move for new well BOUM-0001

Rig OPH

OFF HIRED

Rig off-hired

Personnel onboard	Nil
Overstay crew	Nil
Last week	Nil
Next steps	Nil

What happened


- **OD1 cut the 38" conductor pipe and installed the protection structure**, and was released to new well **BOUM-0001**. The rig is on standby and waits for BOUM-0001 location clearance.
- **Overstay crew fell from 13 to 10**. HLB cleared both of its overstay crew. COSL still holds 10 and needs follow up.
- OD1 personnel onboard fell from 82 to 75. 53 of the 75 hold a seaman or business visa.
- **OPH stayed off-hired for a second week**, and demobilisation continued. CA1 discharged 21 lifts at OPH across Tue 01 and Wed 02 Sep.
- Vessel trips held at 9, but the mix changed. CA1 fell from 4 trips to 2. CA3 and CA5 each ran 1 trip

after most of the week on station. Charlie-3 again ran all 5 crew change circuits.


- Truck moves also held at 41 on a consistent count, against the 46 the 26-08 report published. Per day the rate fell from 6.8 to 5.1, because this period runs 8 days against the previous 6.
- Ground transport peaked on **Mon 31 Aug with 8 dispatches**, of which six trucks carried empty mud skips to HETCO Mina Abdallah Yard.
- Cut casing joints of 18-5/8", 13-5/8", 10-3/4" and 7-5/8" went to the KOC scrap yard on Sun 30 Aug. The SWT burner boom sections A, B and C moved to TSS-WT Hall Mina Abdallah on Wed 02 Sep.
- Fluids handled fell by about half, 742 m³ against 1,452 m³, and no slops movement is recorded. The port ran day shift only on all eight days.
- Vessel movements remain under **MARSEC Level 2**.

Full figures three charts, and every figure


Daily ground transport movements (35 out / 6 in, 41 total)

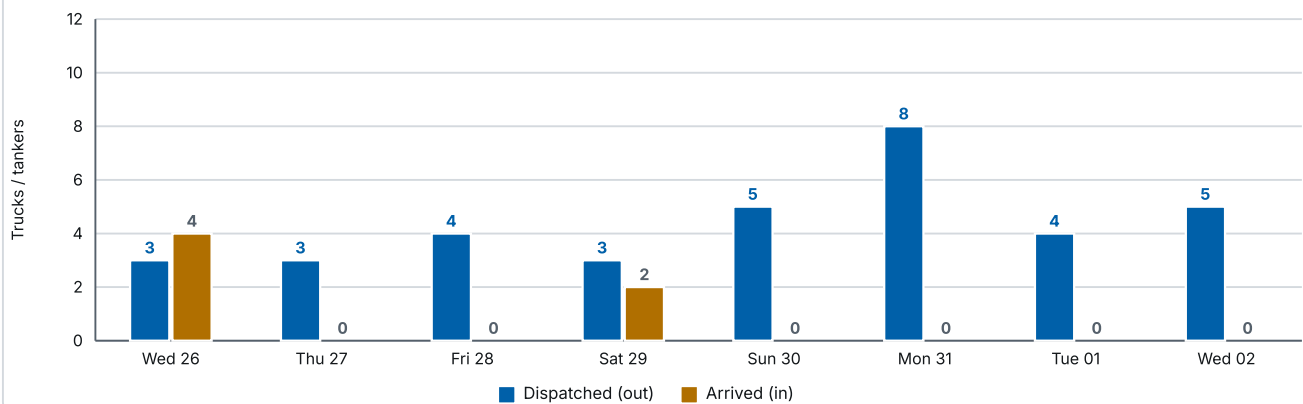

Vessel trips by vessel (9 this week, 9 previous week)

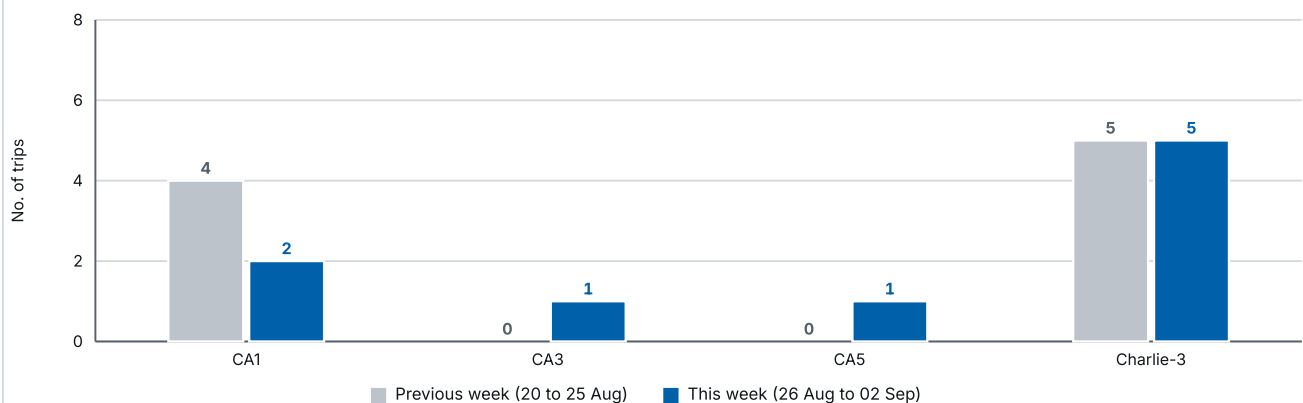

Fluids and bulk managed (742 m³ this week, 1,452 m³ previous week)

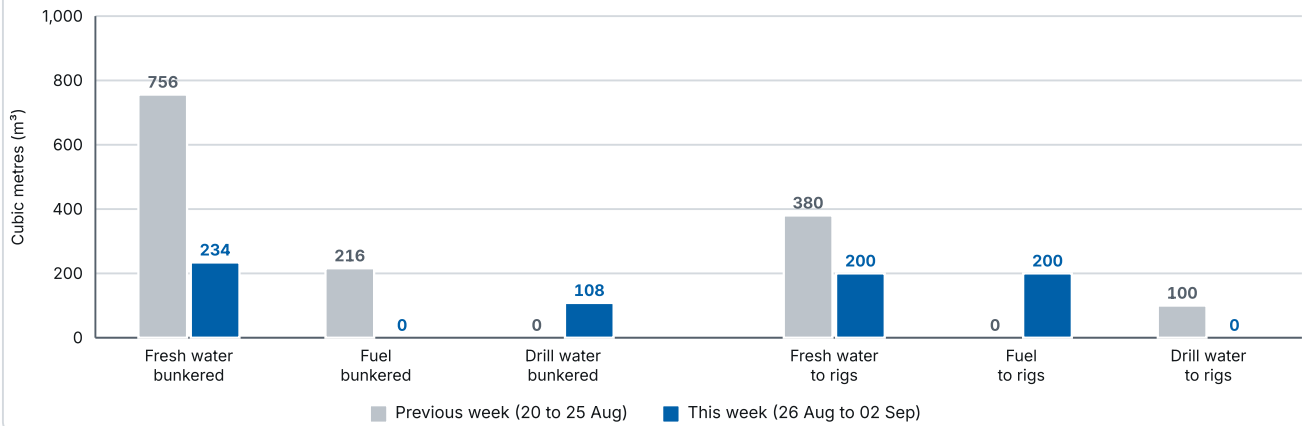

Slops: none recorded. Previous week: 320 bbl.

Metric	26 Aug to 02 Sep 8 days	20 to 25 Aug 6 days	Change
VESSEL TRIPS			
CA1	2	4	▼ 2 (4)
CA3	1	0	▲ 1 (0)
CA5	1	0	▲ 1 (0)
Charlie - 3	5	5	No change (5)
Total vessel trips	9	9	No change (9)
VESSEL MOVEMENTS port to rig, rig to port, rig to rig			
CA1	3	10	▼ 7 (10)
CA3	3	0	▲ 3 (0)
CA5	2	0	▲ 2 (0)
Charlie - 3	13	12	▲ 1 (12)
Total vessel movements	21	22	▼ 1 (22)
Movements per day	2.6	3.7	▼ 1.1 (3.7)
GROUND TRANSPORT			
Dispatched (out)	35	30	▲ 5 (30)
Arrived (in)	6	11	▼ 5 (11)
Total truck / tanker moves	41	41	No change (41)
Moves per day	5.1	6.8	▼ 1.7 (6.8)
FLUIDS AND BULK			
Fresh water bunkered at port	234 m ³	756 m ³	▼ 522 m ³ (756 m ³)
Fuel bunkered at port	0 m ³	216 m ³	▼ 216 m ³ (216 m ³)
Drill water bunkered at port	108 m ³	0 m ³	▲ 108 m ³ (0 m ³)
Fresh water to rigs	200 m ³	380 m ³	▼ 180 m ³ (380 m ³)
Fuel to rigs	200 m ³	0 m ³	▲ 200 m ³ (0 m ³)

Metric	26 Aug to 02 Sep 8 days	20 to 25 Aug 6 days	Change
Drill water to rigs	0 m³	100 m³	▼ 100 m³ (100 m³)
Total fluids managed	742 m³	1,452 m³	▼ 710 m³ (1,452 m³)
Slops discharged	0 bbl	320 bbl	▼ 320 bbl (320 bbl)
RIGS AND CREW			
Active rigs	1	1	No change (1)
OD1 personnel onboard	75	82	▼ 7 (82)
Overstay crew, KOC	0	0	No change (0)
Overstay crew, HLB	0	2	▼ 2 (2)
Overstay crew, COSL	10	11	▼ 1 (11)
Total overstay crew	10	13	▼ 3 (13)

Daily log 61 operations

Port operations 8 days, 29 operations

Wednesday 26.08.2026 Not Normal	- Two trucks were dispatched with one 18-3/4" and one 18-3/4" Dual Rams BOP received from OPH to COSL Mina Abdallah facility. - One truck was dispatched with 3 backloads received from OD1 to COSL Mina Abdallah facility. - Two trucks arrived with 5 lifts from TSS-WT Hall Mina Abdallah facility. - Two trucks arrived with 2 lifts received for OPH from COSL Mina Abdallah facility. no night shift; date reads 26.08.2025, outside the report period; read as 26.08.2026
Thursday 27.08.2026 not stated	- One truck was dispatched with 2 backloads received from OD1 to KOC Shuaiba Port pipe Yard. - One truck was dispatched with 1 basket with Running tools received from OD1 to KOC Shuaiba Port pipe Yard. - One truck was dispatched with 1 empty pipe rack received from KOC Shuaiba Port pipe yard to TSS-WT Hall facility. no night shift; date inferred; no Date in the workbook; no Day in the workbook; no Status in the workbook
Friday 28.08.2026 Not Normal	- One truck was dispatched with 5 Grease drums to Cementing Facility received from OPH. - Two truck dispatched with 4 empty baskets to Odfjell facility. - One truck dispatched with 4 Containers to Baroid Magwa Plant received from OPH. no night shift

Saturday 29.08.2026 Not Normal	- One truck was dispatched with 3 backloads received from OD1 to COSL Mina Abdallah facility. - One truck was dispatched with 2 backloads received from OD1 to KOC Shuaiba Port pipe Yard. - One truck was dispatched with 2 backloads received from OD1 to Odfjell Mina Abdallah facility. - Two trucks arrived with 4 lifts for OD1 from COSL Mina Abdallah facility. - Four Trucks loaded with 18-5/8", 13-5/8", 10-3/4" & 7-5/8" Cut casing joints. no night shift
Sunday 30.08.2026 Not Normal	- Four Trucks dispatched with 18-5/8", 13-5/8", 10-3/4" & 7-5/8" Cut casing joints to KOC scrape yard. - One truck was dispatched with 2 backloads received from OD1 to Solas Marine Mina Abdallah facility. - cargo operation with Vessel Charlie-3, offloaded 4 backload cargo lifts from Charlie-3 deck. no night shift
Monday 31.08.2026 Not Normal	- KOC Maintenance and road support visited Shuaiba port. - Two trucks were dispatched with 6 backloads received from OD1 & OPH to COSL, OWS & Soloas Mina Abdallah facility. - Six trucks were dispatched with each 20 Empty mud skips with Slings & Shackless to HETCO Mina Abdallah Yard. - Cargo operation with Charlie-3, offloaded 4 cargo lifts from Charlie-3 deck as per & backloaded 7 cargo lifts on Vessel for OPH. no night shift
Tuesday 01.09.2026 Not Normal	- Two trucks were dispatched with 10 Empty mud skips with Slings & Shackless to HETCO Mina Abdallah Yard. - One truck was dispatched with 2 Casing Cut Joints to Shuaiba Port Pipe Yard. - One truck was dispatched to Burgan SLB Yard to transfer empty Pipe Rack to TSS-WT Hall. Mina Abdallah facility. - Cargo operation with CA1, backloaded 13 cargo lifts on CA1 deck & offloaded 3 cargo lifts from CA1 deck. no night shift
Wednesday 02.09.2026 Not Normal	- Two trucks were dispatched with SWT Burner Boom two Sections of both B & C to TSS-WT Hall Mina Abdallah facility. - Two trucks were dispatched with SWT Burner Boom two Sections of A to TSS-WT Hall Mina Abdallah facility. - One Boom truck was dispatched with two 6-5/8" X-Overs from KOC Shuaiba Port Pipe Yard to COSL Mina Abdallah facility. no night shift

Vessel movements 8 days, 32 operations

Wednesday 26.08.2026 Normal	• Vessel CA1 - Vessel STBY at Shuaiba port, cargo operation, backloading 1 lifts for OD1 and 9 lifts for OPH, at 18:45 cast off and sail to OD1, arrived OD1 at 22:42, cargo operation, offload 1 lift, babackload 7 lifts, transfer fresh water yo OD1 in progress, vessel at OD1. • Vessel CA3 - Vessel STBY at OPH location. • Vessel CA5 - Vessel STBY at OD1 location. • Vessel Charlie 3 - Vessel STBY at Shuaiba Port, cargo operation, offload 3 lifts, backload 3 lifts, embarked 1 Pax, at 07:45 cast off and sail MM port, received 10 Pax from Abul Kheer boat, sail to OD1, arrived OD1 at 11:35, transfer Pax (4 out/ 6 in), at 11:45 pull out and sail to OPH, arrived OPH at 13:10, cargo operation, offload 3 lifts, backload 3 lifts, transfer Pax (7 out/ 9 in), at 14:28 pull out and sail to MM port, transfer 9 Pax to Abul Kheer boat, proceed to Shuaiba port, arrived Shuaiba port at 17:20, disembarked 6 Pax, offload 3 lifts, vessel STBY at Shuaiba port B.4.
Thursday 27.08.2026 Normal	• Vessel CA1 - Vessel at OD1, continue transfer 200 m3 fresh water and 100 m3 Fuel to OD1, cargo operation, backload 1 lift, vessel STBY at OD1 • Vessel CA3 - Vessel STBY at OPH location. • Vessel CA5 - Vessel STBY at OD1 location. • Vessel Charlie 3 - Vessel STBY at Shuaiba port, vesssl received 18 m3 fresh water
Friday 28.08.2026 Normal	• Vessel CA1 - Vessel STBY at OD1, cargo operation, offload 8 lifts, at 02:15 pull out ans proceed to exit 500 meter from OD1, vessel STBY at OD1 • Vessel CA3 - vessel STBY at OPH location. • Vessel CA5 - Vessel STBY at OD1 location, cargo operation , backload 13 lifts, at 06:10 pull out and STBY at 400 meter from OD1, at 17:30 proceed to OD1, cargo operation ,backload 5 lifts, offload 1 lift, at 20:46 pull out and exit 500 meter away from OD1. • Vessel Charlie 3 - vessel STBY at Shuaiba port, back load 1 lift for OPH.
Saturday 29.08.2026 Normal	• Vessel CA1 - Vessel STBY at OD1 location • Vessel CA3 - Vessel STBY at OPH location. • Vessel CA5 - Vessel STBY at OD1, at 04:00 vessel sail to shuaiba port, arrived Shuaiba port at 07:30, cargo operation, received 72 m3 fresh water and 108 m3 drill water, vessel STBY at Shuaiba port. • Vessel Charlie 3 - Vessel STBY at Shuaiba port, at 06:00 cast off and departed to OPH with cargo (CM-OP- 1247) via MM port, embarked 5 Pax from MM port, sail to OPH, arrived OPH at 09:35 transfer 5 Pax to OPH, offload 1 lift cargo, sail to OD1, arrived OD1 at 11:25, embarked 4 Pax from OD1, sail to OPH, arrived OPH at 13:05 embarked 4 Pax from OPH, cargo operation, backload 2 lifts , sail to MM port, disembarked 8 Pax, sail to Shuaiba port, arrived Shuaiba port at 17:39, offload cargo at Shuaiba port.
Sunday 30.08.2026 Normal	• Vessel CA1 - Vessel STBY at OD1 location,, transfer 100 m3 Fuel to OD1 • Vessel CA3 - Vessel STBY at OPH location. • Vessel CA5 - Vessel STBY at Shuaiba port B.20. • Vessel Charlie 3 - Vessel STBY at Shuaiba port , embarked 1 Pax, at 07:40 cast off and sail to new port (Ras Al-Ard), disembarked 1 Pax, at 10:50 cast off and sail to OPH, arrived OPH at 11:55, backload 4 lifts, at 13:05 pull out and sail to Shuaiba port, arrived Shuaiba port at 14:40, offload 4 lifts, backload 1 lifts, at 17:00 cast off and sail to OD1, arrived OD1 at 18:15, offload 1 lift, backload 4 lifts, at 19:10 pull out and sail to Shuaiba port, arrived Shuaiba port at 20:30. Vessel STBY at Shuaiba port B.4.

Monday 31.08.2026 Normal	• Vessel CA1 - Vessel STBY at OD1 location. • Vessel CA3 - Vessel STBY at OPH location. • Vessel CA5 - Vessel STBY Shuaiba port B.20., received 144 m3 fresh water. • Vessel Charlie 3 - Vessel STBY at Shuaiba port, offload 4 lifts, backloading 7 lifts, at 14:30 cast off and sail to MM port, embarked 20 Pax from Abul Kheer boat, at 16:25 proceed to OPH, arrived OPH at 17:25, cargo operation, offload 7 lifts and backload 6 lifts, disembarked 20 Pax, at 19:27 pull out and sail to Shuaiba port, arrived shuaiba port at 21:15, vessel STBY at Shuaiba port B.4.
Tuesday 01.09.2026 Normal	• Vessel CA1 - Vessel STBY at OD1 location, cargo operation, backload 1 lifts, embarked 10 Pax, at 11:50 pull out and sail to Shuaiba port, arrived Shuaiba port at 15:18, disembarked 10 Pax, cargo operation , offload 3 lifts, backload 13 lifts, at 17:33 cast off and sail to OPH, arrived OPH at 22:30, cargo operation, offload 6 lifts, vessel has cargo operation at OPH • Vessel CA3 - Vessel STBY at OPH location, cargo operation, at 20:55 pull out and sail to Shuaiba port, arrived Shuaiba port at 00:00, Vessel STBY at Shuaiba port. • Vessel CA5 - Vessel STBY at Shuaiba port, cargo operation, backload 3 lifts, embarked 9 Pax, at 09:35 cast off and sail to OD1, arrived OD1 at 13:55, disembarked 9 Pax, cargo operation , offload 10 lifts, backload 1 lift, Vessel STBY at OD1. • Vessel Charlie 3 - Vessel STBY at Shuaiba port B.4, offload 6 lifts
Wednesday 02.09.2026 Normal	• Vessel CA1 - Vessel at OPH, continue cargo operation, offload 15 lifts, backload 3 lifts, Vessel STBY at OPH • Vessel CA3 - Vessel STBY at Shuaiba port, embarked 1 KOC Pax, at 07:42 cast off and sail to OD1, arrived OD1 at 11:35, disembarked 1 KOC Pax, cargo operation, at 14:12 pull put and sail to Shuaiba port, arrived Shuiaba port at 18:30, vessel STBY at Shuiaba port B.20. • Vessel CA5 - Vessel STBY at OD1 location. • Vessel Charlie 3 - Vessel STBY at Shuaiba port


One trip is one outbound voyage from Shuaiba Port plus its return; a rig to rig transit is not a new trip. A vessel movement is a transit between locations -- port to rig, rig to port or rig to rig -- so a pull-out and re-berth at the same rig is not one. A truck move counts one truck unit per dispatch or arrival, and a truck loaded on one day and dispatched the next is one movement, counted on dispatch. Every week is counted on that one rule, which is why 20 to 25 Aug reads 41 truck moves here against the 46 its own report published. Source: Email of 03.09.2026 plus DWOS_Weekly_Offshore_Logistics_Report_03.09.2026.xlsx (report 23, sheets Port and Vessel).

03 to 09 Sep 2026

OD1 idle all week awaiting BOUM-0001 clearance. The BM-0001 casing arrived: ground transport reversed to 32 arrivals against 12 dispatches.


VESSEL TRIPS

13

▲ 44% (9)
Last week


VESSEL MOVEMENTS

18

▼ 3 (21)
Last week

TRUCK MOVES

44

▲ 7% (41)
Last weekFLUIDS HANDLED, M³

1,782

▲ 140% (742)
Last week

OVERSTAY CREW

11

▲ 1 (10)
Last weekRig OD1 **ON HIRE**

STBY waiting for BOUM-0001 location clearance, to start jack-down and move to BM-0001

Personnel onboard 79 incl. 57 visa

Overstay crew COSL 11

Last week Nil

Next steps Rig preparation for move; rig move for new well BOUM-0001

Rig OPH **OFF HIRED**

Rig off-hired

Personnel onboard Nil

Overstay crew Nil

Last week Nil


Next steps Nil

What happened


- **OD1 stayed on standby for BOUM-0001 location clearance**, now to start jack-down and move to BM-0001. Last week activities are recorded as Nil: the rig was idle for the full seven days.
- **Overstay crew rose from 10 to 11**, all of them COSL. KOC and HLB are nil.
- OD1 personnel onboard rose from 75 to 79. 57 of the 79 hold a seaman or business visa.
- **Ground transport turned sharply inbound: 32 arrivals against 12 dispatches**, 44 moves in total against 41. The week before ran 35 out and 6 in, so the direction reversed.
- The inbound load is the **BM-0001 move materials**: 18-5/8" and 24" casing and short joints, a casing spool, X-overs, and Fugro positioning tools, from KOC Ahmadi Yard-4 and Yard-5 and HETCO Mina Abdallah. Arrivals peaked on **Wed 09 Sep with 9**.
- **Fluids handled more than doubled, 1,782 m³ against 742 m³**. Fuel delivered to the rigs rose from 200 m³ to 394 m³, of which CA1 transferred 260 m³ on Sun 06 Sep.
- **Vessel trips rose to 13 from 9**, per the covering email: CA1 6, CA3 2, CA5 nil, Charlie-3 5. CA1 carried the increase, working OD1 and OPH through the week. See the data queries on the counting basis.
- OPH stayed off-hired for a third week, and still drew cargo and fluids: CA1 delivered 300 m³ of fresh water and 294 m³ of fuel to OPH across 03 and 07 Sep.
- **Port status reads Normal on all 7 days**, where both previous weeks read Not Normal on every day. The port again ran day shift only.
- Vessel movements remain under **MARSEC Level 2**.

Full figures three charts, and every figure


Daily ground transport movements (12 out / 32 in, 44 total)

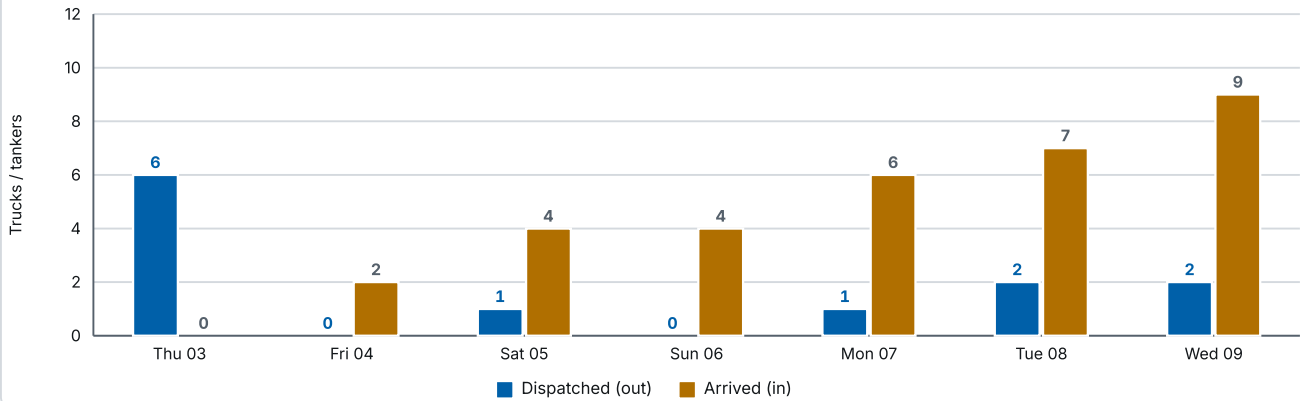

Vessel trips by vessel (13 this week, 9 previous week)

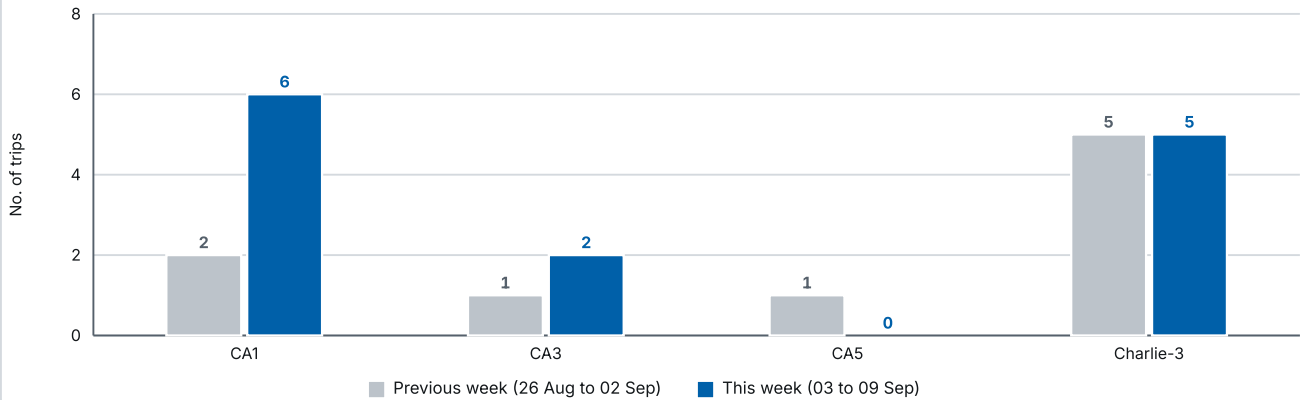

Fluids and bulk managed (1,782 m³ this week, 742 m³ previous week)

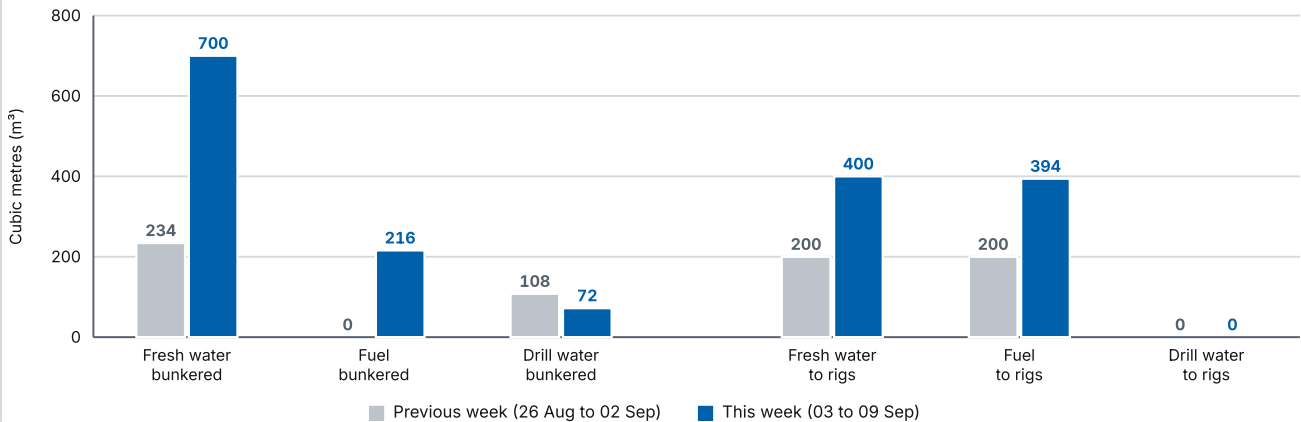

Slops: none recorded.

Metric	03 to 09 Sep 7 days	26 Aug to 02 Sep 8 days	Change
VESSEL TRIPS			
CA1	6	2	▲ 4 (2)
CA3	2	1	▲ 1 (1)
CA5	0	1	▼ 1 (1)
Charlie-3	5	5	No change (5)
Total vessel trips	13	9	▲ 4 (9)
VESSEL MOVEMENTS port to rig, rig to port, rig to rig			

Metric	03 to 09 Sep 7 days	26 Aug to 02 Sep 8 days	Change
CA1	5	3	▲ 2 (3)
CA3	2	3	▼ 1 (3)
CA5	0	2	▼ 2 (2)
Charlie - 3	11	13	▼ 2 (13)
Total vessel movements	18	21	▼ 3 (21)
Movements per day	2.6	2.6	No change (2.6)
GROUND TRANSPORT			
Dispatched (out)	12	35	▼ 23 (35)
Arrived (in)	32	6	▲ 26 (6)
Total truck / tanker moves	44	41	▲ 3 (41)
Moves per day	6.3	5.1	▲ 1.2 (5.1)
FLUIDS AND BULK			
Fresh water bunkered at port	700 m³	234 m³	▲ 466 m³ (234 m³)
Fuel bunkered at port	216 m³	0 m³	▲ 216 m³ (0 m³)
Drill water bunkered at port	72 m³	108 m³	▼ 36 m³ (108 m³)
Fresh water to rigs	400 m³	200 m³	▲ 200 m³ (200 m³)
Fuel to rigs	394 m³	200 m³	▲ 194 m³ (200 m³)
Drill water to rigs	0 m³	0 m³	No change (0 m³)
Total fluids managed	1,782 m³	742 m³	▲ 1,040 m³ (742 m³)
Slops discharged	0 bbl	0 bbl	No change (0 bbl)
RIGS AND CREW			
Active rigs	1	1	No change (1)
OD1 personnel onboard	79	75	▲ 4 (75)
Overstay crew, KOC	0	0	No change (0)
Overstay crew, HLB	0	0	No change (0)
Overstay crew, COSL	11	10	▲ 1 (10)
Total overstay crew	11	10	▲ 1 (10)

Daily log 86 operations

Port operations 7 days, 58 operations

Thursday 03.09.2026 Normal	• One truck was dispatched with container has rig Spares received from OPH to COSL Mina Abdallah facility. • One truck was dispatched with 2 lifts received from OPH to Sperry Hall Mina Abdallah facility. • One truck was dispatched with 4 lifts received from OPH & OD1 to COSL Mina Abdallah facility • One truck was dispatched with 2 baskets has BSS Equipment's received from OPH to BAROID BSS Mud Plant facility. • Two trucks were dispatched with 3 lifts received from OPH to BAROID BSS Mud Plant facility. • Two Baskets backloaded from Shuaiba Berth - 20 & Shuaiba Pipe yard with Bit breakers, circulating Swages & Water bushings & sent to WPS facility for inspection by Al-Mansoori. • Fresh water bunkering (216 m3) to CA3 no night shift
Friday 04.09.2026 Normal	• One boom truck arrived with one 28" MT Drill Bit and one 22" MT Drill Bit for Rig OD1 from SLB Warehouse. • One half Lorry arrived with Frac H-Beam sent as sample to Hetco. • Vessel CA1, offloading cargo from OD1 and OPH • Fresh water bunkering (180 m3) to CA1 • Fresh water bunkering (16 m3) to Charlie-3 no night shift
Saturday 05.09.2026 Normal	• One truck was dispatched with 20' container with BSS Auger frames received from OPH as per manifest RCM-OP-1195 to BSS Mud Plant facility. • 4 Trucks arrived with items as per Call off: OP-RI3-N-19-3 from COSL Mina Abdallah facility. • Loaded Cargo for Rig OD1 and OPH on CA-1 and Sailed Vessel to the Rig • 4 x Trucks with Cargo for Rig OPH from COSL offloaded. no night shift
Sunday 06.09.2026 Normal	• 4 x Trucks with Cargo for Rig OPH and Rig OD1 from COSL offloaded. • One truck arrived with 1 x lifts for OPH as per Call off: OP-RI3-N-20-3 from COSL Mina Abdallah facility. • One truck arrived with 2 x lift for OPH as per Call off: OP-RI3-N-20-3 from COSL Mina Abdallah facility. • One truck arrived with 2 x lifts for OD1 as per Call off: OD-JL3-N-16-3 from COSL Mina Abdallah facility. • One call off truck arrived with 6 x lifts for OD1 as per Call off: OD-JL3-N-16-3 from COSL Mina Abdallah facility. no night shift

Monday
07.09.2026
Normal

- One truck was dispatched with 3 × OD1 empty food containers to the Reliance Subhan Facility, as per Delivery Note RM-SP-8146.
- One truck arrived with six 6' mini containers containing chemicals for OD1 as per Call-off: OD-BM1-A-1-4 from the BSS Mud Plant Facility.
- Three trucks arrived with casing spool and X-overs for OD1 BM-0001 from KOC Yard-4, Ahmadi.
- One truck arrived with spare parts and tools for OD1 BM-0001 from KOC Yard-4, Ahmadi.
- One truck arrived with six 6' mini containers containing chemicals for OD1 as per Call-off: OD-BM1-A-1-4 from the BSS Mud Plant Facility.
- Offloaded 4 x Trucks with 24" Casing Accessories at Pipe Yard.
- Offloaded 2 x Trucks with Chemical Containers from Baroid for Rig OD1
- Loaded 1 x Truck with Empty Food Containers for Rig OD1 and sent to Reliance
- Fuel Bunkering to Charlie-3 (35.997 M3)

no night shift

Tuesday
08.09.2026
Normal

- One truck was dispatched with 3 x Full Mud Skips received from OPH(RCM-OP-1193) to NCC SEK Mud Plant facility, as per delivery RM-SP-8177
- One truck was dispatched with 2 x lifts received from OD1 as per manifest RCM-OD-931 to COSL Mina Abdallah facility, as per delivery RM-SP-8179
- One truck arrived with 3 x OD1 full food containers from Reliance Subhan facility, as per delivery ticket COSL-DT-OD-047
- One truck arrived with 8 × 24" Short Joints for OD1 BM-0001 from KOC Yard-4 Ahmadi, as per delivery ticket 2026/9/8/0660
- One call off truck arrived with 4 × 24" Short Joints for OD1 BM-0001 from KOC Yard-4 Ahmadi, as per delivery ticket 2026/9/8/0647
- One truck arrived with 2 x lifts for OPH & OD1 as per Call Off: OP-RI3-N-21-3 & OD-JL3-N-17-3 from COSL Mina Abdallah Facility, as per delivery ticket COSL-DT-OP-RI3-N-21-3A
- One truck arrived with 3 x Empty mud skips from NCC SEK Mud Plant facility, as per delivery ticket RDT-SP-8177
- Two trucks arrived with 15 × 24" Joints for OD1 from Hetco Mina Abdallah Yard after inspection, as per delivery ticket HPM-DT-1576
- Fuel Bunkering to CA-1 (107.999 M3)
- Water Bunkering to CA-1 (216 M3)
- Offloaded 2 x Trucks with 24" Casing Accessories at Pipe Yard
- Offloaded 2 x Trucks with 24" Casing from Hetco Yard after Al Mansoori Inspection for Rig OD1
- Loaded Cargo for Rig OD1 and Rig OPH on CA-3

no night shift

Wednesday

09.09.2026

Normal

- Loaded Cargo for Rig OD1 and Rig OPH on CA-1
- One Truck dispatched with 6 lifts received from OD1 & OPH as per manifest RCM-OD-931 & OP-1196 to COSL Mina Abdallah Facility as per Delivery Note RM-SP-8181.
- One Truck arrived with 10 × 18-5/8" short joints for OD1 BM-001 from KOC Ahmadi Yard-5 to Hetco Mina Abdallah Yard as per Delivery Ticket 2026/09/0736
- One Truck dispatched with 4 lifts received from OD1 & OPH (RCM-OD-931 & OP-1196) to COSL Mina Abdallah Facility as per Delivery Note RM-SP-8182.
- One Call-off Truck arrived with 6 × 18-5/8" short joints for OD1 BM-001 from KOC Ahmadi Yard-5 to Shuaiba Port Pipe Yard as per Delivery Ticket 2026/09/0788.
- One Call-off Truck arrived with 4 × 18-5/8" short joints for OD1 BM-001 from KOC Ahmadi Yard-5 to Shuaiba Port Pipe Yard as per Delivery Ticket 2026/09/0648.
- One Call-off Truck arrived with 9 × 18-5/8" casing joints for OD1 BM-001 from KOC Ahmadi Yard-5 to Shuaiba Port Pipe Yard as per Delivery Ticket 2026/09/0741.
- One Truck arrived with 10 × 18-5/8" casing joints for OD1 BM-001 from KOC Ahmadi Yard-5 to Shuaiba Port Pipe Yard as per Delivery Ticket 2026/09/0728
- One Truck arrived with 8 × 24" joints for OD1 from Hetco Mina Abdallah Yard after inspection as per Delivery Ticket HPM-DT-1577.
- One Truck arrived with 2 × 3 mtr baskets c/w circulating swage for OD1 from WPS Hall Mina Abdallah Yard after inspection as per Delivery Ticket HPM-DT-1578.
- One Truck arrived with 7 × 24" R1 & R2 casing joints for OD1 BM-001 from HETCO Mina Abdallah Yard as per Delivery Ticket HPM-DT-1579.
- One Call-off Truck arrived with 3 × positioning tools from Fugro for OD1 BM-001 from PMI W/H Mina Abdallah Yard as per Delivery Ticket HPM-DT-1580.
- Offloaded casing & accessories at pipe yard
- Fuel Bunkering to CA-1 for CA3(71.99 M3)
- Water Bunkering to CA-1 for CA3 (36 M3)

no night shift

Vessel movements 7 days, 28 operations**Thursday**

03.09.2026

Normal

- Vessel CA1- Near OPH, Anchor heaved up@14:30, port side of rig@15:48, continue cargo operation, fresh water transferred(100 M3), Vessel pulled out from OPH @20:54, Vessel started sailing to Shuaiba port @22:06
- Vessel CA3- Vessel STBY at berth 20, received fresh water (144 M3) and drilling water(72M3) , cargo operation, castoff@18:25, arrived OPH@22:10,vessel in position of OPH@22:55,transferred hand carry, pullout@23:15,vessel STBY at OPH@23:42
- Vessel CA5- Vessel STBY at OD1 location.
- Vessel Charlie 3- STBY at berth 4, castoff@04:05, alongside of OD1@05:25, crew transferred, pullout@05:27, sailed, arrived berth 20@06:50, crew embarked,castoff and proceed to south pier @07:05, arrived south pier @07:30, crew transferred,castoff and proceed to OD1@12:00,alongside of OD1@13:25, crew transferred, pullout @13:35,sailed, arrived OPH@15:00, crew transferred, pullout@15:20,arrived berth 4@16:35, crew disembarked, and STBY at berth 4.

Friday 04.09.2026 Normal	• Vessel CA1 -Vessel secured alongside berth 20, cargo operation, fresh water received (180 M3), vessel STBY at berth 20 • Vessel CA3- vessel STBY at OPH location • Vessel CA5- Vessel STBY at OD1 location. • Vessel Charlie 3- Vessel STBY at berth 4, fresh water received(16M3)
Saturday 05.09.2026 Normal	• Vessel CA1 -Vessel secured alongside berth 20, cargo operation, fresh water received(108 M3), Vessel cast off@15:15, arrived near OD1@18:30, waiting for DGPS signal, vessel approaching Rig OD1@23:48 • Vessel CA3- vessel STBY at OPH location • Vessel CA5- Vessel STBY at OD1 location, Anchor aweigh@08:23, in position @ port side of OD1,cargo operation, transferred fresh water(100M3) and fuel(100M3), pullout@13:42, and STBY at OD1 anchorage area. • Vessel Charlie 3- Vessel STBVY at berth 4 , crew embarked, castoff@09:15,alongside of rig OPH@10:25, crew transferred,pullout@10:58, secure alongside of berth 4@13:05, crew disembarked,vessel STBY at berth 4
Sunday 06.09.2026 Normal	• Vessel CA1 - STBY at OPH, fuel transferred(260.2 M3), DGPS not working, pulledout @22:56, vessel STBY at OPH location • Vessel CA3- vessel STBY at OPH location • Vessel CA5- Vessel STBY at OD1 location., • Vessel Charlie 3- Vessel STBVY at berth 4
Monday 07.09.2026 Normal	• Vessel CA1 - STBY at OPH, Anchor heaved up@04:38, vessel at STBD side of OPH@05:40,fresh water(200 M3) and fuel(34M3) transferred,cargo operation,vessel pulled out@13:40, sailed, arrived berth 20@17:15, STBY at berth 20 • Vessel CA3- vessel STBY at OPH location, Heaveup anchor@14:24, vessel in position@16:00,cargo operation, pullout@20:45, vessel STBY at OPH location • Vessel CA5- Vessel STBY at OD1 location. • Vessel Charlie 3- Vessel STBVY at berth 4, received fuel (35.997 M3)
Tuesday 08.09.2026 Normal	• Vessel CA1- STBY at berth 20, received fresh water(216 M3) and fuel oil(107.999 M3), cargo operation,vessel remail STBY atberth 20 • Vessel CA3- vessel STBY at OPH location • Vessel CA5- Vessel STBY at OD1 location, heaveup anchor@06:55,crew transferred,pullout@10:24, completed chopper duty,STBY at OD1 location. • Vessel Charlie 3- Vessel STBY at berth 4 , cargo operation, crew embarked, castoff@07:50, alongside of OD1@09:15, cargo operation, crew transferred, pullout@10:10,alongside of berth 4@11:50, crew disembarked, vessel STBY at berth 4

Wednesday

09.09.2026

Normal

- Vessel CA1 - STBY at berth 20, received fresh water(36M3) and fuel oil(71.99 M3), cargo operation, castoff@10:08, Vessel arrived outside 500 meters of OD1@13:12, vessel in port side of OD1 @13:50, cargo operation, pulledout@15:48, sailing towards OPH, DGPS signal lost, DGPS back to normal @20:08, Vessel arrived outside 500 meters of OPH@22:42, STBY at OPH anchorage area.
- Vessel CA3 - vessel STBY at OPH location, Heaveup anchor@12:58, Vessel in position on the port side of OPH @14:00, cargo operation, pullout @19:40, STBY at OPH anchorage,heave up anchor@22:48, vessel enroute to Shuaiba port.
- Vessel CA5 - Vessel STBY at OD1 location.
- Vessel Charlie 3- Vessel STBY at berth 4 , castoff@11:25, alongside of OPH@11:30, transferred and received hand carry, pullout@11:38, alongside of berth 4@12:50, crew disembarked, cargo operation, vessel STBY at berth 4

One trip is one outbound voyage from Shuaiba Port plus its return; a rig to rig transit is not a new trip. A vessel movement is a transit between locations -- port to rig, rig to port or rig to rig -- so a pull-out and re-berth at the same rig is not one. A truck move counts one truck unit per dispatch or arrival, and a truck loaded on one day and dispatched the next is one movement, counted on dispatch. Every week is counted on that one rule, which is why 20 to 25 Aug reads 41 truck moves here against the 46 its own report published. Source: Email of 10.09.2026 from Rejeesh Kumar Kunjupillai plus DWOS_Weekly_Offshore_Logistics_Report_10.09.2026.xlsx (report 24, sheets Port and Vessel).

10 to 16 Sep 2026

OD1 idle a second week, still awaiting BOUM-0001 clearance. Overstay down to 8, its lowest in the series, and the casing went back out to Ahmadi.

VESSEL TRIPS

16

▲ 23% (13)
Last week



4 wks, from 9

VESSEL MOVEMENTS

23

▲ 5 (18)
Last week



4 wks, from 22

TRUCK MOVES

44

No change (44)
Last week



4 wks, from 41

FLUIDS HANDLED, M³

818

▼ 54% (1,782)
Last week



4 wks, from 1,452

OVERSTAY CREW

8

▼ 3 (11)
Last week



4 wks, from 13

Rig OD1

ON HIRE

STBY waiting for BOUM-0001 location clearance, to start jack-down and move to BM-0001

Personnel onboard 78 incl. 58 visa

Overstay crew HLB 1 COSL 7

Last week Nil

Next steps Rig preparation for move; rig move for new well BOUM-0001

Rig OPH

OFF HIRED

Rig off-hired

Personnel onboard Nil

Overstay crew Nil


Last week Nil

Next steps Nil


What happened

- **OD1 was idle for a second week**, still waiting on BOUM-0001 location clearance to start jack-down. Last week activities are again recorded as Nil.
- **Overstay crew fell from 11 to 8**. COSL came down from 11 to 7, and HLB now holds 1 where it held none.
- OD1 personnel onboard eased from 79 to 78, and visa holders rose from 57 to 58.
- **CA1 took 300 m³ of fuel from the bunker barge MT SEDRA-II** at Mina Al Ahmadi anchorage on Sat 12. The workbook records it as an adjustment to balance the 294.2 m³ given to OPH on 06 and 07 Sep, which settles where last week's fuel went.
- Vessel movements were **23 against 18**, the busiest of the four weeks tracked. Charlie-3 made 13 of them.
- **CA5 has now spent 14 straight days on station at OD1** without moving between locations, across both this week and last.
- Truck and pickup moves held at 44, but turned outbound again: **25 out against 19 in**, where the week before ran 12 out and 32 in as the BM-0001 casing arrived.
- Casing went back out: 30", 24" and 36" and 38" R3 joints returned to KOC Ahmadi Yard 4 across Sat 12, Sun 13 and Mon 14, and 18-5/8" R3 went to HETCO for inspection and came back to the Shuaiba pipe yard.
- Charlie-3 ran crew changes through **two new transfer points, Jal Boot Village and Khiran Marina**, alongside the usual Shuaiba runs.
- Vessel movements remain under **MARSEC Level 2**.


Full figures three charts, and every figure

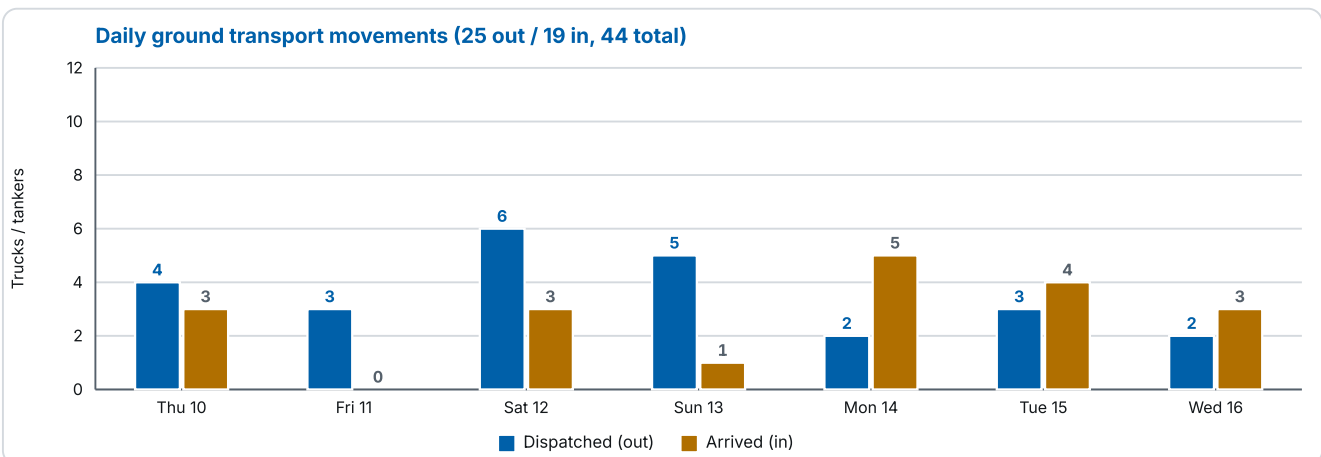

Vessel trips by vessel (16 this week, 13 previous week)

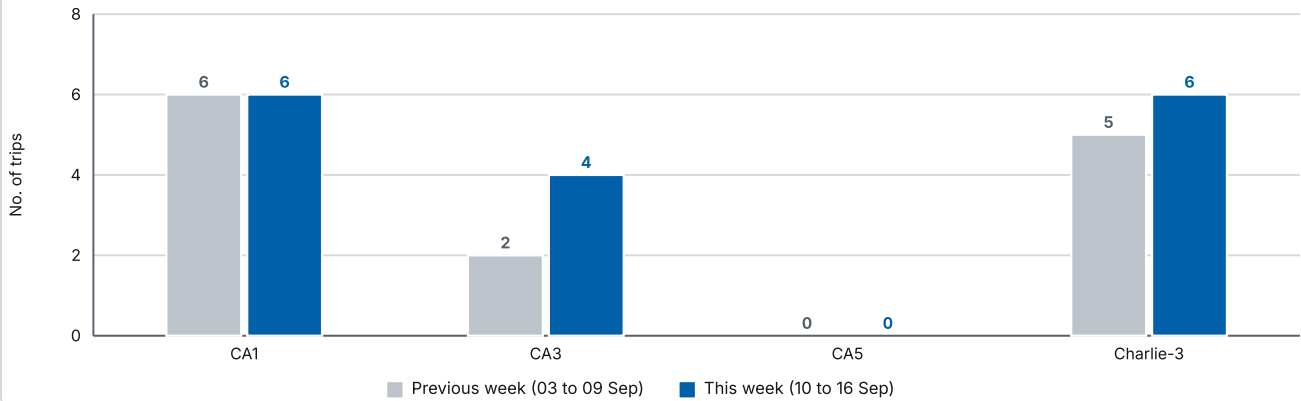

Fluids and bulk managed (818 m³ this week, 1,782 m³ previous week)

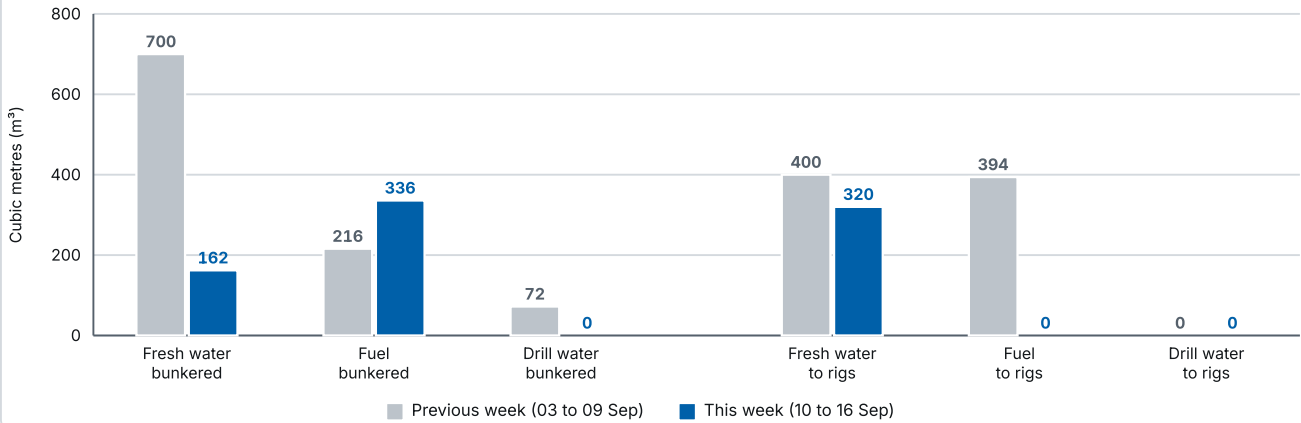

Slops: none recorded.

Metric	10 to 16 Sep 7 days	03 to 09 Sep 7 days	Change
VESSEL TRIPS			
CA1	6	6	No change (6)
CA3	4	2	▲ 2 (2)
CA5	0	0	No change (0)
Charlie-3	6	5	▲ 1 (5)
Total vessel trips	16	13	▲ 3 (13)
VESSEL MOVEMENTS port to rig, rig to port, rig to rig			
CA1	7	5	▲ 2 (5)
CA3	3	2	▲ 1 (2)
CA5	0	0	No change (0)
Charlie-3	13	11	▲ 2 (11)
Total vessel movements	23	18	▲ 5 (18)
Movements per day	3.3	2.6	▲ 0.7 (2.6)
GROUND TRANSPORT			
Dispatched (out)	25	12	▲ 13 (12)

Metric	10 to 16 Sep 7 days	03 to 09 Sep 7 days	Change
Arrived (in)	19	32	▼ 13 (32)
Total truck / tanker moves	44	44	No change (44)
Moves per day	6.3	6.3	No change (6.3)
FLUIDS AND BULK			
Fresh water bunkered at port	162 m ³	700 m ³	▼ 538 m ³ (700 m ³)
Fuel bunkered at port	336 m ³	216 m ³	▲ 120 m ³ (216 m ³)
Drill water bunkered at port	0 m ³	72 m ³	▼ 72 m ³ (72 m ³)
Fresh water to rigs	320 m ³	400 m ³	▼ 80 m ³ (400 m ³)
Fuel to rigs	0 m ³	394 m ³	▼ 394 m ³ (394 m ³)
Drill water to rigs	0 m ³	0 m ³	No change (0 m ³)
Total fluids managed	818 m³	1,782 m³	▼ 964 m³ (1,782 m³)
Slops discharged	0 bbl	0 bbl	No change (0 bbl)
RIGS AND CREW			
Active rigs	1	1	No change (1)
OD1 personnel onboard	78	79	▼ 1 (79)
Overstay crew, KOC	0	0	No change (0)
Overstay crew, HLB	1	0	▲ 1 (0)
Overstay crew, COSL	7	11	▼ 4 (11)
Total overstay crew	8	11	▼ 3 (11)

[Daily log](#) 89 operations

[Port operations](#) 7 days, 61 operations

Thursday
10.09.2026
Normal

- One truck was dispatched with 1 × 7.8mtr. basket received from OPH(RCM-OP-1197) to COSL Mina Abdallah facility, as per delivery RM-SP-8184
- One truck was dispatched with 1 x full trash skip received from OPH(RCM-OP-1197) to COSL Mina Abdallah facility, as per delivery RM-SP-8183
- One truck carrying 10 × 18-5/8" R3 casing was dispatched to HETCO Mina Abdallah Yard for inspection
- One call off truck was dispatched with 3 x lifts received from OPH(RCM-OP-1197) to Hetco Stevedoring facility, as per delivery RM-SP-8185
- One truck arrived with 5 × 18-5/8" Short Joints for OD1 BM-001
- from Hetco Mina Abdallah Yard after inspection, as per delivery ticket HPM-DT-1581
- One truck carrying 10 × 18-5/8" R3 casing for OD1 BM-001 arrived from Hetco Mina Abdallah Yard. Following inspection, the material was stacked in the Shuaiba Port Pipe Yard
- One truck arrived with 4 x lifts for OPH(Call Off: OP-RI3-N-21-3) from COSL Mina Abdallah Facility, as per delivery ticket COSL-DT-OP-RI3-N-21-3C
- One truck arrived with 4 x lifts for OPH(Call Off: OP-RI3-N-21-3) from COSL Mina Abdallah Facility, as per delivery ticket COSL-DT-OP-RI3-N-21-3C
- One truck carrying 10 × 18-5/8" R3 casing for OD1 BM-001 arrived from Hetco Mina Abdallah Yard. Following inspection, the material was stacked in the Shuaiba Port Pipe Yard
- Fuel Bunkering to CA3(36 M3)
- Loaded Cargo for Rig OPH on CA-3
- Offloaded the items from the truck at pipe yard and berth 20.

no night shift

Friday
11.09.2026
Normal

- Offloaded the items from the truck at pipe yard.
- One truck(23/41295) was dispatched with Backload of 2 x Units received from OPH(RCM-OP-1197) to Cementing, as per delivery RM-SP-8184
- One truck(91/59613) was dispatched with Backload of 2 x Units received from OPH(RCM-OP-1197) to Cementing, as per delivery RM-SP-8185
- One truck(91/53434) was dispatched with Backload of 4 x Units received from OPH(RCM-OP-1197) to Cementing, as per delivery RM-SP-8186

no night shift

Saturday 12.09.2026 Normal	• One truck arrived with 10 x lifts from KOC DWS-3 Ahmadi to Shuaiba Port Pipe Yard, as per delivery ticket 2026/9/12/0735 • One truck was dispatched with 2 × 36" R3 Casing to Ahmadi KOC Yard # 4 , as per delivery RM-SP-8191 • One truck arrived with 06 x lifts from KOC DWS-3 Ahmadi to Shuaiba Port Pipe Yard, as per delivery ticket 2026/9/12/0720 • One truck was dispatched with 2 × 38" R3 Casing to Ahmadi KOC Yard # 4 , as per delivery RM-SP-8191 • One truck arrived with 1 × 10' OT Container for OPH(Call Off: OP-RI3-N-22-3) from COSL Mina Abdallah Yard, as per delivery ticket COSL-DT-OP-RI3-N-22-3 • One truck was dispatched with 2 x lifts received from OPH(RCM-OP-1197) to Cementing Hall Mina Abdallah facility, as per delivery RM-SP-8187 • One truck was dispatched with 2 x lifts received from OPH(RCM-OP-1197) to Cementing Hall Mina Abdallah facility, as per delivery RM-SP-8188 • One truck was dispatched with 4 x lifts received from OD1(RCM-OD-932 & 933) to COSL Mina Abdallah facility, as per delivery RM-SP-8189 • One truck was dispatched with 2 x lifts received from OD1(RCM-OD-932 & 933) to COSL Mina Abdallah facility, as per delivery RM-SP-8190 • Fuel bunkering to Vessel CA1 from MT. SEDRA II (300.120 M3) (Checked with HLB, this adjustment made to balance the quantity which was given to Oriental Phoenix (294.2 M3) on 06.09.2026 &07.09.2026 • Water Bunkering to CA-1 for CA3 (72 M3) no night shift
Sunday 13.09.2026 Normal	• One truck was dispatched with 2 lifts received from OPH (RCM-OP-1198) to COSL Mina Abdallah Facility, as per Delivery Ticket RM-SP-8193 • One pickup was dispatched with 2 H-Carry units received from OD1 (RCM-OD-932 & 933) to HPM & IT Hall, Mina Abdallah Facility, as per Delivery Ticket RM-SP-8194 • One truck was dispatched with 18-5/8", 24", and 30" MLL Running Tools to KOC SP-17, as per KOC Delivery Ticket 2026/9/13/0620. • One truck was dispatched with 2 × 30" R3 Casing from KOC Shuaiba Port Pipe Yard to Ahmadi KOC Yard #4, as per Delivery Ticket 2026/9/13/1050 • One truck was dispatched with 2 × 24" R3 Casing from KOC Shuaiba Port Pipe Yard to Ahmadi KOC Yard #4, as per Delivery Ticket 2026/9/13/1072 • One truck arrived with 5 lifts for OD1 (Call-Off: OD-RI3-N-18-3) from COSL Mina Abdallah Yard, as per Delivery Ticket COSL-DT-OD-RI3-N-18-3 no night shift

Monday
14.09.2026
Normal

- One truck arrived from Odfjell Mina Abdallah Yard with 4 × 3 mtr empty baskets, as per Delivery Ticket HPM-DT-1582
- One truck arrived from Shuaiba Port Pipe Yard with 2 × 24" R3 casing joints, as per Delivery Ticket HPM-DT-1583
- One call-off truck arrived from KOC Ahmadi to Shuaiba Port Pipe Yard carrying 2 packers for BM-0001, as per Delivery Ticket 2026/9/14/0297
- One truck was dispatched to Ahmadi KOC Yard #4 carrying 2 × 24" R3 casing joints, as per Delivery Ticket 2026/9/14/1129
- One truck was dispatched to Ahmadi KOC Yard #4 carrying 2 × 24" R3 casing joints, as per Delivery Ticket 2026/9/14/1129
- One truck was dispatched to the Reliance Subhan Facility carrying 3 OD1 empty food containers, as per Delivery Ticket RM-SP-8195
- One truck arrived from the BSS Mud Plant Facility carrying a BSS Compressor, as per Delivery Ticket HPM-DT-1583
- One truck arrived from COSL Mina Abdallah Yard with 1 × 10' OT container and 1 empty basket for OPH (Call Off: OP-RI3-N-23-3), as per Delivery Ticket COSL-DT-OP-RI3-N-23-3
- Water Bunkering to Charlie 3 (18 M3)
- Baroid Team Pumped 23 MT Bentonite on CA3 for Rig OD1
- Loaded 2 × 24" R3 casing joints on truck for sending to KOC Yard 4

no night shift

Tuesday
15.09.2026
Normal

- One truck was dispatched with 3 x lifts received from OPH & OD1(RCM-OP-1199 & OD-934 – 935) to COSL Mina Abdallah Facility , as per delivery RM-SP-8196
- One truck was dispatched with 3 x PH Empty food containers to Reliance Subhan facility, as per delivery ticket RM-SP-8197
- One truck was dispatched with 2 x Full Mud Skips received from OD1(RCM-OD-934) to NCC SEK Mud Plant facility, as per delivery RM-SP-8198
- One truck arrived with 3 x OD1 full food containers from Reliance Subhan facility, as per delivery ticket COSL-DT-OD-048
- One truck arrived with 1 × 10' OT Container for OD1(Call Off: OD-BM1-E-1-3) from COSL Mina Abdallah Yard, as per delivery ticket COSL-DT- OD-BM1-E-1-3
- Water Bunkering to CA 3 (72 M3)
- Loaded Cargo as per manifest CM-OD-1003 for Rig OD1 on Charlie-3
- Offloaded Two Trucks with 24" and 18-5/8" X-Over and Landing Joints at Pipe Yard

no night shift

Wednesday

16.09.2026

Normal

- Loaded Cargo as per manifest CM-OD-1004 on vessel CA1 for Rig OD1.
- 02 Nos Skip with OBM cuttings sent to KOC- NCC for disposal.
- One Pickup was dispatched with KOC / Cementing Hall received from OD1(RCM-OD-933 – 935) to KOC Ahmadi / CMT Hall. Mina Abdallah Facility , as per delivery RM-SP-8199.
- One Pickup was dispatched with Network Switch & Land Line Handset received from OPH(RCM-OP-1195) to Sperry SDL Hall. Mina Abdallah Facility , as per delivery RM-SP-9000.
- One truck arrived with 3 x OPH full food containers from Reliance Subhan facility, as per delivery ticket COSL-DT-OP-045.
- One truck arrived with 2 x Empty mud skips from NCC SEK facility, as per delivery ticket RDT-SP-8198.
- One truck arrived with 3 x Lifts for OD1(Call Off: OD-BM1-E-2-3) from COSL Mina Abdallah Yard, as per delivery ticket COSL-DT- OD-BM1-E-2-3
- Offloaded 1 truck/3 food containers for Rig OPH from Reliance, 1 truck/2 empty mud skips from SEK treatment Plant, and 1 truck/3 lifts for Rig OD1 from COSL.

no night shift

Vessel movements 7 days, 28 operations**Thursday**

10.09.2026

Normal

- Vessel CA1- VSL STBY near ORIENTAL PHOENIX anchorage; DP operation delayed due to DGPS signal loss. DGPS active Anchor heave up and proceeded to OPH@@10:40. Entered 500 m zone and positioned under port-side crane. 15:00-19:20, Cargo operations completed with 5 lifts offloaded to OPH and 3 lifts backloaded , Pullout, clear of OPH, exited the 500 m zone, and continued passage toward ORIENTAL DRAGON-1 @19:28
- Vessel CA3- Vessel Arrived Shuaiba Port Berth 20, secured alongside at 04:54 hrs. Cargo operations carried out, including 1 truck of fuel oil received from shore and food provisions loaded@ 07:48-15:54, Cast off from Shuaiba Port and proceeded to OPH@ 16:12 hrs. Arrived at OPH location@1912 hrs , dropped standby anchor and remained anchored at OPH.
- Vessel CA5- Vessel STBY at OD1 location
- Vessel Charlie 3- Vessel STBY at Shuaiba Port Berth 4, cast off @12:40 hrs and proceeded to OPH. Entered 500 m zone @13:40 hrs and came alongside STBD side of rig @13:50 hrs. Received 7 PAX from rig @14:41-14:46 hrs, pulled out @14:47 hrs and exited 500 m zone @14:50 hrs. Proceeded to Jal Boot Village and maintained position off channel entrance awaiting taxi boat. Transferred 7 PAX to taxi boat @18:15 hrs, proceeded to Shuaiba Port @18:20 hrs and secured alongside B#4 @20:35 hrs. Vessel remained STBY alongside Shuaiba Port Berth 4.

Friday 11.09.2026 Normal	• Vessel CA1 - VSL enroute from OPH to OD-1, arrived 500 m zone OD-1 @02:18 and standby. Proceeded to CA5 @12:20, came alongside in DP mode to collect modified flange, cast off @13:05 and returned to OD-1. Entered 500 m zone @13:40, one crew transferred to rig for flange modification discussion and rejoined vessel @15:00. Collected modified flange @18:25, departed OD-1 @18:30 and proceeded to Bunker Barge MT SEDRA-II. Secured alongside @20:08, bunker hose connected @20:45, commenced fuel receiving @21:12 (in progress). • Vessel CA1 - Vessel STBY at OPH location,heave up anchor@16:04,VSL in position on the port side of OPH@19:00,transferred fresh water (120 M3), cargo operation completed, Pull out@22:00, Vessel STBY at OPH location. • Vessel CA5 - Vessel STBY at OD1 location, Heaveup anchor@ 07:45, port side crane of OD1@08:55,transferred fresh water(100M3), Pull out to 500m@11:05,Vessel STBY at OD1 anchorage area. • Vessel Charlie 3- Vessel STBY Shuaiba Port B erth 4. cast off @04:50 for OPH, entered 500 m zone @05:55, alongside rig OPH @06:00. Embarked 7 PAX (06:20-06:32) and unloaded 1 lift cargo @06:39. Pulled out @06:40, arrived and secured at Shuaiba Port Berth 4 @07:55, disembarked 7 PAX (07:55-08:00). Loaded 3 lifts cargo (16:20-16:35), vessel STBY alongside Berth 4
Saturday 12.09.2026 Normal	• Vessel CA1 - Received fuel oil from MT SEDRA-II at Mina Al Ahmadi Anchorage@00:00-01:10; bunker hose disconnected @0110,Cast off and proceeded to OD-1 @ 01:30 Alongside OD-1@03:12, received 3 lifts backload cargo, Departed OD-1 @03:35 sailed to Shuaiba Port. Secured alongside Jetty No.20@07:14; offloaded 17 lifts cargo. Received 72 m³ fresh water, Vessel remained alongside Shuaiba Port . • Vessel CA3- Vessel STBY at OPH location • Vessel CA5- Vessel STBY at OD1 location • Vessel Charlie 3- Vessel STBY at Berth 4, Loaded 1 lift cargo.
Sunday 13.09.2026 Normal	• Vessel CA1- Vessel STBY at Berth 20 • Vessel CA3- Vessel STBY at OPH location, Heaveup anchor@4:18,VSL in position on the port side of OPH@05:24, Transferred offsigner crew.Pull out@05:36 and STBY at OPH anchorage. • Vessel CA5- Vessel STBY at OD1 location • Vessel Charlie 3-Vessel STBY Shuaiba Port B#4, cast off @04:50, arrived OPH 500 m zone @05:55, alongside rig @06:00, embarked 7 PAX, discharged 1 lift cargo, departed from rig @06:40, secured Shuaiba Berth 4 @07:55, disembarked 7 PAX, loaded 3 lifts cargo, vessel STBY alongside Berth 4
Monday 14.09.2026 Normal	• Vessel CA1- Vessel STBY at Berth 20,Received Bentonite from 1st Truck, (23MT), 1 lift cargo loaded, Vessel cast off from Shuaiba Port Jetty No. 20@21:54 sailing to OPH. • Vessel CA3- Vessel STBY at OPH location, • Vessel CA5- Vessel STBY at OD1 location • Vessel Charlie 3-Vessel STBY at Berth No. 4, cast off @04:30, Arrived Khiran Marina @06:40, embarked 7 PAX, sailed, alongside OD1 @08:05, offloaded 3 lifts cargo, transferred 5 PAX out/5 PAX in and hand carry, loaded 2 lifts cargo, pull out @08:58, alongside OPH @10:20, transferred 3 PAX and offloaded 1 lift cargo, pull out @10:43, Khiran Marina @13:30, disembarked 7 PAX, alongside Berth No. 4 @15:45, offloaded 1 lift cargo, received FW bunker 18 m³, vessel STBY at Berth No. 4.

Tuesday
15.09.2026
Normal

- Vessel CA1 - Enroute OPH, Anchored near OPH due propulsion issue@. 02:00; vessel standby, Anchor aweigh@11:06, propulsion/DP trials completed, proceeded to OPH 500 m zone. Alongside OPH@13:18, offloaded 1 lift cargo,Departed OPH @ 13:20 and returned to Shuaiba Port. Secured alongside Jetty No.20@16:36, Vessel remained alongside Shuaiba Port .
- Vessel CA3 - Vessel STBY at OPH location, Heaveup anchor@02:30, Arrived Shuaiba port berth 20 @6:54, fresh water received(72 M3) , cargo operation completred, castoff@09:13, arrived at OPH anchorage @13:00 and STBY at OPH anchorage.
- Vessel CA5 - Vessel STBY at OD1 location, Heaveup anchor@6:55, port side crane of OD1@08:00, offloaded trash skip, Pull out for standby at 400m, back to port side crane of OD1@10:10, loaded trash skip,Pull out for standby at 500m @10:12, vessel standby anchored at OD1 Location.
- Vessel Charlie 3 -VSL STBY at Shuaiba Port B.No.4, 6 PAX onboard, Loaded 4 lifts cargo, Cast off Shuaiba Port and proceed to OD1 @07:30, Alongside rig OD1@ 08:55, transferred 4 lifts cargo, completed crew change (6 PAX Out / 6 PAX In), Pulled out@09:43, Arrived,Secured alongside Shuaiba Port B.No.4@11:10, Offloaded 2 lifts cargo, Received provisions, vessel STBY at Berth No. 4.

Wednesday
16.09.2026
Normal

- Vessel CA1 - Vessel STBY at Berth 20,castoff for DP trial @09:58, Vessel arrived DP Trial Location@10:35, DP Trial Completed. DP Mode off. Vessel proceed back to Shuaiba Port@16:54, cargo operation,castoff for rig OD1@ 21:56, vessel enroute to OD1
- Vessel CA3 - Vessel STBY at OPH location, Heaveup anchor@11:24, in position on the stbd side of OPH@13:24, received pax, pullout@13:36,vessel standby anchored at OPH Location.
- Vessel CA5 - Vessel STBY at OD1 location, Heaveup anchor@8:10,Completed standby for chopper duty,drop port anchor, Heaveup anchor@14:35,port side crane of OD1@16:00,transferred fresh water(100M3), Pull out to 500m@18:38,drop port anchor,Heaveup anchor@19:21, port side crane of OD1@21:00, received backload,Pull out to 500m@ 22:23, vessel standby anchored at OD1 Location.
- Vessel Charlie 3 - VSL STBY at Shuaiba Port B.No.4, 5 PAX onboard, Loaded 3 lifts cargo, Cast off Shuaiba Port and proceed to OPH @11:15, Alongside rig OPH@ 12:25,offloaded 3 lifts cargo, completed crew transfer Pulled out@13:05, Arrived,Secured alongside Shuaiba Port B.No.4@14:15, vessel STBY at Berth No. 4.

One trip is one outbound voyage from Shuaiba Port plus its return; a rig to rig transit is not a new trip. A vessel movement is a transit between locations -- port to rig, rig to port or rig to rig -- so a pull-out and re-berth at the same rig is not one. A truck move counts one truck unit per dispatch or arrival, and a truck loaded on one day and dispatched the next is one movement, counted on dispatch. Every week is counted on that one rule, which is why 20 to 25 Aug reads 41 truck moves here against the 46 its own report published. Source: Email of 17.09.2026 from Rejeesh Kumar Kunjupillai plus DWOS_Weekly_Offshore_Logistics_Report_17.09.2026.xlsx (report 25, sheets Port and Vessel).

Thanks and Best Regards,

Saud Abdulaziz AlKharji

Kuwait Oil Company (KOC)

Engineer Drilling & Workover | Drilling & Workover Operational Support Team

skharji@kockw.com | www.kockw.com

