

03 to 09 Sep 2026

OD1 idle all week awaiting BOUM-0001 clearance. The BM-0001 casing arrived: ground transport reversed to 32 arrivals against 12 dispatches.

VESSEL TRIPS

13

▲ 44% (9)
Last week



3 wks, from 9

TRUCK MOVES

44

▲ 7% (41)
Last week



3 wks, from 41

FLUIDS HANDLED, M³

1,782

▲ 140% (742)
Last week



3 wks, from 1,452

OVERSTAY CREW

11

▲ 1 (10)
Last week



3 wks, from 10

Rig OD1

ON HIRE

STBY waiting for BOUM-0001 location clearance, to start jack-down and move to BM-0001

Personnel onboard 79 incl. 57 visa

Overstay crew COSL 11

Last week Nil

Next steps Rig preparation for move; rig move for new well BOUM-0001

Rig OPH

OFF HIRED

Rig off-hired

Personnel onboard Nil

Overstay crew Nil

Last week Nil




Next steps Nil

What happened

- **OD1 stayed on standby for BOUM-0001 location clearance**, now to start jack-down and move to BM-0001. Last week activities are recorded as Nil: the rig was idle for the full seven days.
- **Overstay crew rose from 10 to 11**, all of them COSL. KOC and HLB are nil.
- OD1 personnel onboard rose from 75 to 79. 57 of the 79 hold a seaman or business visa.
- **Ground transport turned sharply inbound: 32 arrivals against 12 dispatches**, 44 moves in total against 41. The week before ran 35 out and 6 in, so the direction reversed.
- The inbound load is the **BM-0001 move materials**: 18-5/8" and 24" casing and short joints, a casing spool, X-overs, and Fugro positioning tools, from KOC Ahmadi Yard-4 and Yard-5 and HETCO Mina Abdallah. Arrivals peaked on **Wed 09 Sep with 9**.
- **Fluids handled more than doubled, 1,782 m³ against 742 m³**. Fuel delivered to the rigs rose from 200 m³ to 394 m³, of which CA1 transferred 260 m³ on Sun 06 Sep.
- **Vessel trips rose to 13 from 9**, per the covering email: CA1 6, CA3 2, CA5 nil, Charlie-3 5. CA1 carried the increase, working OD1 and OPH through the week. See the data queries on the counting basis.
- OPH stayed off-hired for a third week, and still drew cargo and fluids: CA1 delivered 300 m³ of fresh water and 294 m³ of fuel to OPH across 03 and 07 Sep.
- **Port status reads Normal on all 7 days**, where both previous weeks read Not Normal on every day. The port again ran day shift only.

- Vessel movements remain under **MARSEC Level 2**.

Full figures three charts, and every figure

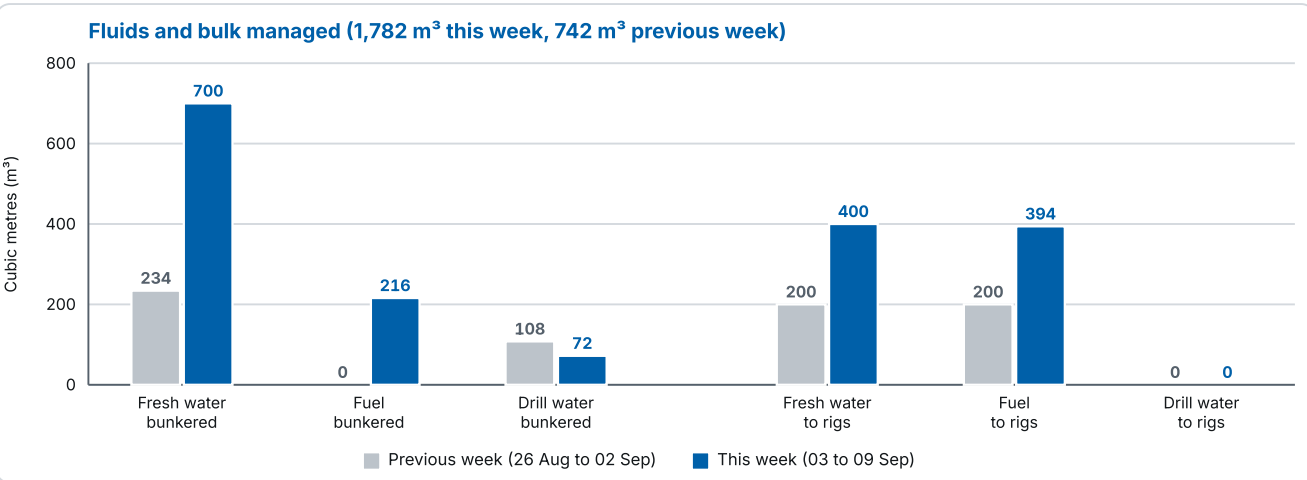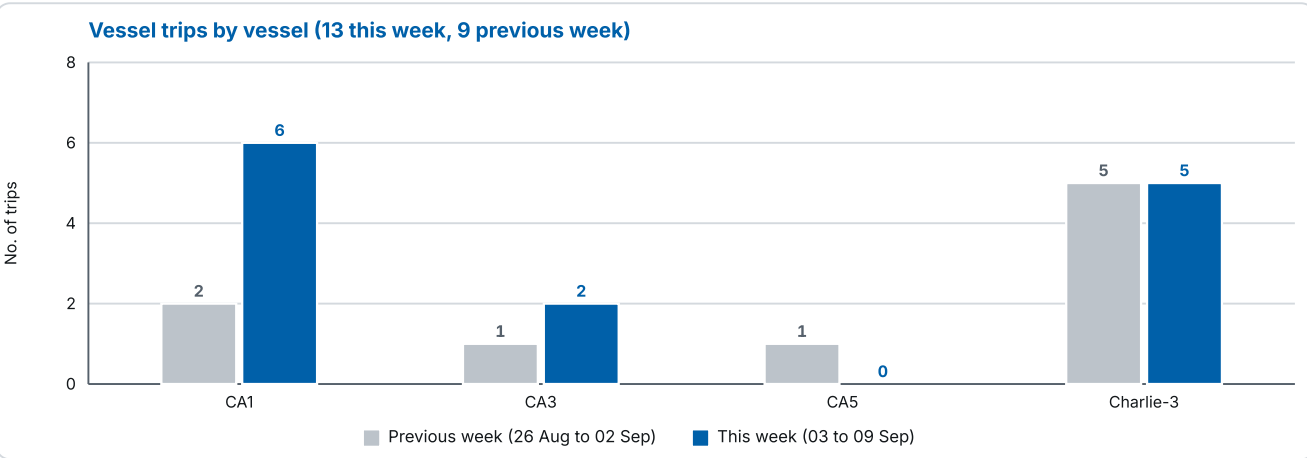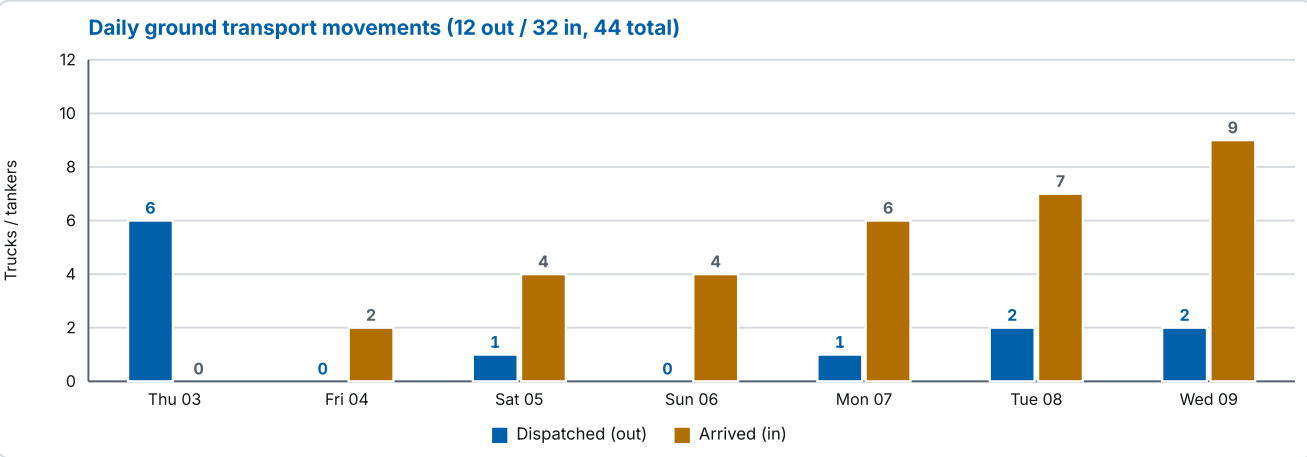

Slops: none recorded.

Metric	03 to 09 Sep 7 days	26 Aug to 02 Sep 8 days	Change
VESSEL TRIPS			
CA1	6	2	▲ 4 (2)
CA3	2	1	▲ 1 (1)
CA5	0	1	▼ 1 (1)

Metric	03 to 09 Sep 7 days	26 Aug to 02 Sep 8 days	Change
Charlie - 3	5	5	No change (5)
Total vessel trips	13	9	▲ 4 (9)
VESSEL MOVEMENTS port to rig, rig to port, rig to rig			
CA1	5	3	▲ 2 (3)
CA3	2	3	▼ 1 (3)
CA5	0	2	▼ 2 (2)
Charlie - 3	11	13	▼ 2 (13)
Total vessel movements	18	21	▼ 3 (21)
Movements per day	2.6	2.6	No change (2.6)
GROUND TRANSPORT			
Dispatched (out)	12	35	▼ 23 (35)
Arrived (in)	32	6	▲ 26 (6)
Total truck / tanker moves	44	41	▲ 3 (41)
Moves per day	6.3	5.1	▲ 1.2 (5.1)
FLUIDS AND BULK			
Fresh water bunkered at port	700 m³	234 m³	▲ 466 m³ (234 m³)
Fuel bunkered at port	216 m³	0 m³	▲ 216 m³ (0 m³)
Drill water bunkered at port	72 m³	108 m³	▼ 36 m³ (108 m³)
Fresh water to rigs	400 m³	200 m³	▲ 200 m³ (200 m³)
Fuel to rigs	394 m³	200 m³	▲ 194 m³ (200 m³)
Drill water to rigs	0 m³	0 m³	No change (0 m³)
Total fluids managed	1,782 m³	742 m³	▲ 1,040 m³ (742 m³)
Slops discharged	0 bbl	0 bbl	No change (0 bbl)
RIGS AND CREW			
Active rigs	1	1	No change (1)
OD1 personnel onboard	79	75	▲ 4 (75)
Overstay crew, KOC	0	0	No change (0)
Overstay crew, HLB	0	0	No change (0)
Overstay crew, COSL	11	10	▲ 1 (10)
Total overstay crew	11	10	▲ 1 (10)

Daily log 86 operations

Port operations 7 days, 58 operations

Thursday 03.09.2026 Normal	- One truck was dispatched with container has rig Spares received from OPH to COSL Mina Abdallah facility. - One truck was dispatched with 2 lifts received from OPH to Sperry Hall Mina Abdallah facility. - One truck was dispatched with 4 lifts received from OPH & OD1 to COSL Mina Abdallah facility - One truck was dispatched with 2 baskets has BSS Equipment's received from OPH to BAROID BSS Mud Plant facility. - Two trucks were dispatched with 3 lifts received from OPH to BAROID BSS Mud Plant facility. - Two Baskets backloaded from Shuaiba Berth - 20 & Shuaiba Pipe yard with Bit breakers, circulating Swages & Water bushings & sent to WPS facility for inspection by Al-Mansoori. - Fresh water bunkering (216 m3) to CA3 no night shift
Friday 04.09.2026 Normal	- One boom truck arrived with one 28" MT Drill Bit and one 22" MT Drill Bit for Rig OD1 from SLB Warehouse. - One half Lorry arrived with Frac H-Beam sent as sample to Hetco. - Vessel CA1, offloading cargo from OD1 and OPH - Fresh water bunkering (180 m3) to CA1 - Fresh water bunkering (16 m3) to Charlie-3 no night shift
Saturday 05.09.2026 Normal	- One truck was dispatched with 20' container with BSS Auger frames received from OPH as per manifest RCM-OP-1195 to BSS Mud Plant facility. 4 Trucks arrived with items as per Call off: OP-RI3-N-19-3 from COSL Mina Abdallah facility. - Loaded Cargo for Rig OD1 and OPH on CA-1 and Sailed Vessel to the Rig 4 x Trucks with Cargo for Rig OPH from COSL offloaded. no night shift
Sunday 06.09.2026 Normal	4 x Trucks with Cargo for Rig OPH and Rig OD1 from COSL offloaded. - One truck arrived with 1 x lifts for OPH as per Call off: OP-RI3-N-20-3 from COSL Mina Abdallah facility. - One truck arrived with 2 x lift for OPH as per Call off: OP-RI3-N-20-3 from COSL Mina Abdallah facility. - One truck arrived with 2 x lifts for OD1 as per Call off: OD-JL3-N-16-3 from COSL Mina Abdallah facility. - One call off truck arrived with 6 x lifts for OD1 as per Call off: OD-JL3-N-16-3 from COSL Mina Abdallah facility. no night shift

Monday
07.09.2026
Normal

- One truck was dispatched with 3 × OD1 empty food containers to the Reliance Subhan Facility, as per Delivery Note RM-SP-8146.
- One truck arrived with six 6' mini containers containing chemicals for OD1 as per Call-off: OD-BM1-A-1-4 from the BSS Mud Plant Facility.
- Three trucks arrived with casing spool and X-overs for OD1 BM-0001 from KOC Yard-4, Ahmadi.
- One truck arrived with spare parts and tools for OD1 BM-0001 from KOC Yard-4, Ahmadi.
- One truck arrived with six 6' mini containers containing chemicals for OD1 as per Call-off: OD-BM1-A-1-4 from the BSS Mud Plant Facility.
- Offloaded 4 x Trucks with 24" Casing Accessories at Pipe Yard.
- Offloaded 2 x Trucks with Chemical Containers from Baroid for Rig OD1
- Loaded 1 x Truck with Empty Food Containers for Rig OD1 and sent to Reliance
- Fuel Bunkering to Charlie-3 (35.997 M3)

no night shift

Tuesday
08.09.2026
Normal

- One truck was dispatched with 3 x Full Mud Skips received from OPH(RCM-OP-1193) to NCC SEK Mud Plant facility, as per delivery RM-SP-8177
- One truck was dispatched with 2 x lifts received from OD1 as per manifest RCM-OD-931 to COSL Mina Abdallah facility, as per delivery RM-SP-8179
- One truck arrived with 3 x OD1 full food containers from Reliance Subhan facility, as per delivery ticket COSL-DT-OD-047
- One truck arrived with 8 × 24" Short Joints for OD1 BM-0001 from KOC Yard-4 Ahmadi, as per delivery ticket 2026/9/8/0660
- One call off truck arrived with 4 × 24" Short Joints for OD1 BM-0001 from KOC Yard-4 Ahmadi, as per delivery ticket 2026/9/8/0647
- One truck arrived with 2 x lifts for OPH & OD1 as per Call Off: OP-RI3-N-21-3 & OD-JL3-N-17-3 from COSL Mina Abdallah Facility, as per delivery ticket COSL-DT-OP-RI3-N-21-3A
- One truck arrived with 3 x Empty mud skips from NCC SEK Mud Plant facility, as per delivery ticket RDT-SP-8177
- Two trucks arrived with 15 × 24" Joints for OD1 from Hetco Mina Abdallah Yard after inspection, as per delivery ticket HPM-DT-1576
- Fuel Bunkering to CA-1 (107.999 M3)
- Water Bunkering to CA-1 (216 M3)
- Offloaded 2 x Trucks with 24" Casing Accessories at Pipe Yard
- Offloaded 2 x Trucks with 24" Casing from Hetco Yard after Al Mansoori Inspection for Rig OD1
- Loaded Cargo for Rig OD1 and Rig OPH on CA-3

no night shift

Wednesday

09.09.2026

Normal

- Loaded Cargo for Rig OD1 and Rig OPH on CA-1
- One Truck dispatched with 6 lifts received from OD1 & OPH as per manifest RCM-OD-931 & OP-1196 to COSL Mina Abdallah Facility as per Delivery Note RM-SP-8181.
- One Truck arrived with 10 × 18-5/8" short joints for OD1 BM-001 from KOC Ahmadi Yard-5 to Hetco Mina Abdallah Yard as per Delivery Ticket 2026/09/0736
- One Truck dispatched with 4 lifts received from OD1 & OPH (RCM-OD-931 & OP-1196) to COSL Mina Abdallah Facility as per Delivery Note RM-SP-8182.
- One Call-off Truck arrived with 6 × 18-5/8" short joints for OD1 BM-001 from KOC Ahmadi Yard-5 to Shuaiba Port Pipe Yard as per Delivery Ticket 2026/09/0788.
- One Call-off Truck arrived with 4 × 18-5/8" short joints for OD1 BM-001 from KOC Ahmadi Yard-5 to Shuaiba Port Pipe Yard as per Delivery Ticket 2026/09/0648.
- One Call-off Truck arrived with 9 × 18-5/8" casing joints for OD1 BM-001 from KOC Ahmadi Yard-5 to Shuaiba Port Pipe Yard as per Delivery Ticket 2026/09/0741.
- One Truck arrived with 10 × 18-5/8" casing joints for OD1 BM-001 from KOC Ahmadi Yard-5 to Shuaiba Port Pipe Yard as per Delivery Ticket 2026/09/0728
- One Truck arrived with 8 × 24" joints for OD1 from Hetco Mina Abdallah Yard after inspection as per Delivery Ticket HPM-DT-1577.
- One Truck arrived with 2 × 3 mtr baskets c/w circulating swage for OD1 from WPS Hall Mina Abdallah Yard after inspection as per Delivery Ticket HPM-DT-1578.
- One Truck arrived with 7 × 24" R1 & R2 casing joints for OD1 BM-001 from HETCO Mina Abdallah Yard as per Delivery Ticket HPM-DT-1579.
- One Call-off Truck arrived with 3 × positioning tools from Fugro for OD1 BM-001 from PMI W/H Mina Abdallah Yard as per Delivery Ticket HPM-DT-1580.
- Offloaded casing & accessories at pipe yard
- Fuel Bunkering to CA-1 for CA3(71.99 M3)
- Water Bunkering to CA-1 for CA3 (36 M3)

no night shift

Vessel movements 7 days, 28 operations**Thursday**

03.09.2026

Normal

- Vessel CA1- Near OPH, Anchor heaved up@14:30, port side of rig@15:48, continue cargo operation, fresh water transferred(100 M3), Vessel pulled out from OPH @20:54, Vessel started sailing to Shuaiba port @22:06
- Vessel CA3- Vessel STBY at berth 20, received fresh water (144 M3) and drilling water(72M3) , cargo operation, castoff@18:25, arrived OPH@22:10,vessel in position of OPH@22:55,transferred hand carry, pullout@23:15,vessel STBY at OPH@23:42
- Vessel CA5- Vessel STBY at OD1 location.
- Vessel Charlie 3- STBY at berth 4, castoff@04:05, alongside of OD1@05:25, crew transferred, pullout@05:27, sailed, arrived berth 20@06:50, crew embarked,castoff and proceed to south pier @07:05, arrived south pier @07:30, crew transferred,castoff and proceed to OD1@12:00,alongside of OD1@13:25, crew transferred, pullout @13:35,sailed, arrived OPH@15:00, crew transferred, pullout@15:20,arrived berth 4@16:35, crew disembarked, and STBY at berth 4.

Friday 04.09.2026 Normal	• Vessel CA1 -Vessel secured alongside berth 20, cargo operation, fresh water received (180 M3), vessel STBY at berth 20 • Vessel CA3- vessel STBY at OPH location • Vessel CA5- Vessel STBY at OD1 location. • Vessel Charlie 3- Vessel STBY at berth 4, fresh water received(16M3)
Saturday 05.09.2026 Normal	• Vessel CA1 -Vessel secured alongside berth 20, cargo operation, fresh water received(108 M3), Vessel cast off@15:15, arrived near OD1@18:30, waiting for DGPS signal, vessel approaching Rig OD1@23:48 • Vessel CA3- vessel STBY at OPH location • Vessel CA5- Vessel STBY at OD1 location, Anchor aweigh@08:23, in position @ port side of OD1,cargo operation, transferred fresh water(100M3) and fuel(100M3), pullout@13:42, and STBY at OD1 anchorage area. • Vessel Charlie 3- Vessel STBVY at berth 4 , crew embarked, castoff@09:15,alongside of rig OPH@10:25, crew transferred,pullout@10:58, secure alongside of berth 4@13:05, crew disembarked,vessel STBY at berth 4
Sunday 06.09.2026 Normal	• Vessel CA1 - STBY at OPH, fuel transferred(260.2 M3), DGPS not working, pulledout @22:56, vessel STBY at OPH location • Vessel CA3- vessel STBY at OPH location • Vessel CA5- Vessel STBY at OD1 location., • Vessel Charlie 3- Vessel STBVY at berth 4
Monday 07.09.2026 Normal	• Vessel CA1 - STBY at OPH, Anchor heaved up@04:38, vessel at STBD side of OPH@05:40,fresh water(200 M3) and fuel(34M3) transferred,cargo operation,vessel pulled out@13:40, sailed, arrived berth 20@17:15, STBY at berth 20 • Vessel CA3- vessel STBY at OPH location, Heaveup anchor@14:24, vessel in position@16:00,cargo operation, pullout@20:45, vessel STBY at OPH location • Vessel CA5- Vessel STBY at OD1 location. • Vessel Charlie 3- Vessel STBVY at berth 4, received fuel (35.997 M3)
Tuesday 08.09.2026 Normal	• Vessel CA1 - STBY at berth 20, received fresh water(216 M3) and fuel oil(107.999 M3), cargo operation,vessel remail STBY atberth 20 • Vessel CA3- vessel STBY at OPH location • Vessel CA5- Vessel STBY at OD1 location, heaveup anchor@06:55,crew transferred,pullout@10:24, completed chopper duty,STBY at OD1 location. • Vessel Charlie 3- Vessel STBY at berth 4 , cargo operation, crew embarked, castoff@07:50, alongside of OD1@09:15, cargo operation, crew transferred, pullout@10:10,alongside of berth 4@11:50, crew disembarked, vessel STBY at berth 4

Wednesday

09.09.2026

Normal

- Vessel CA1 - STBY at berth 20, received fresh water(36M3) and fuel oil(71.99 M3), cargo operation, castoff@10:08, Vessel arrived outside 500 meters of OD1@13:12, vessel in port side of OD1 @13:50, cargo operation, pulledout@15:48, sailing towards OPH, DGPS signal lost, DGPS back to normal @20:08, Vessel arrived outside 500 meters of OPH@22:42, STBY at OPH anchorage area.
- Vessel CA3 - vessel STBY at OPH location, Heaveup anchor@12:58, Vessel in position on the port side of OPH @14:00, cargo operation, pullout @19:40, STBY at OPH anchorage,heave up anchor@22:48, vessel enroute to Shuaiba port.
- Vessel CA5 - Vessel STBY at OD1 location.
- Vessel Charlie 3 - Vessel STBY at berth 4 , castoff@11:25, alongside of OPH@11:30, transferred and received hand carry, pullout@11:38, alongside of berth 4@12:50, crew disembarked, cargo operation, vessel STBY at berth 4

Thanks and Best Regards,

Saud Abdulaziz AlKharji

Kuwait Oil Company (KOC)

Engineer Drilling & Workover | Drilling & Workover Operational Support Team

skharji@kockw.com | www.kockw.com
